FILE NO. 2023

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

FEBRUARY 5, 1984 — THIS LICENSE OR PERMIT EXPIRES

JAMES E. ARTER — LICENSEE OR PERMITTEE

2601 NOTTINGHAM CT. LINCOLN, NE 68512 — ADDRESS

T9N; R7E; Sec. 28; Bk 3; Lot 4; Add. Yankee Ridge Estates — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: NONTRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 60.00	$	$	$	$ 60.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
018754	110.16 XXXXXX	148.14 XXXXXX	6.2 XXXXX

SERIAL NO.	DATE	AMOUNT

652460 53 60.00 -

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION HEALTH

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: ~~474-1541~~ 471-7800

A

FILING FEE: $ $60.00

FILE NO. 2023

DATE: 8/4/83

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 28 ;
   Block 3 : Lot 4 : Addition Yankee Ridge Estates LLCN
   Street Address 6201 Rebel Drive

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: Over 1 mile ft.

James E. Arter
Signature of Applicant (Owner or Lessee)

2601 Nottingham Ct. Lincoln, Ne. 68512
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. ~~8/4~~/83. Date Frwd. ~~8/5~~/83. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. ~~8-5-83~~ Date Frwd. ~~8-5-83~~. ACTION: Approved ☒ Disapproved ☐ Signature: Conrad Demmer

3. City ~~or County~~ Engineer: Date Rec'd. ~~8-5-83~~ Date Frwd. ~~8-5-83~~. ACTION: Approved ☒ Disapproved ☐ Signature:

REMARKS OR REASONS FOR DISAPPROVAL PREXISTING WELL

Site Visits:
Date: 9-2-83 by: jm both laterals have too much fall.
Date: 9/6/83 by: JMN ← Left Health Department as employee
Date: by:

INSTALLATION FINAL WRITTEN APPROVAL
Date: 10/15/85 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. 2023

PROPERTY WHERE SOIL TESTED: LOT 4, BLK 3, YANKEE RIDGE ESTATES LLCN

Location: Township_____; Range_____; Section & ¼ Section_____.
Property Dimensions: 331.40 ft. x 392.67 ft. Area: 3 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 6-21 23 to 6-21-83. Weather: Precip. NR Temp. 90.

OWNER: James E. Arter
Address: 2601 Nottingham Ct. Lincoln, Nebr 68512

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	18	6-21	9	6-22	12	6-21	5 PM	6	6 PM	4 3/4	60	1 1/4	
2	18	6-22	"	"	"	6-21	"	6	"	4 3/4	"	1 1/4	
												✓	
3	18	6-22			"	6-21	"	6	"	4 3/4	"	1 1/4	
4	18	6-21			"	6-21		6		4 3/4	"	1 1/4	
5		6-21				6-21		6	"	4 7/8	"	1 1/8	
6	18	6-21	"	"		6-21		6	"	4 7/8	"	1 1/8	

Signature of Person Conducting Test
Address 6711 Vo 7 Phone 475-1486

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: Satisfactory for septic system
Soil Type (SCS): Shelbyville Silty Clay Loam
Date: June 30, 1983

Approved Percolation Rate (a)
A. 5 1 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 2023

Indicate on sketch if residence and well are exisiting or proposed.

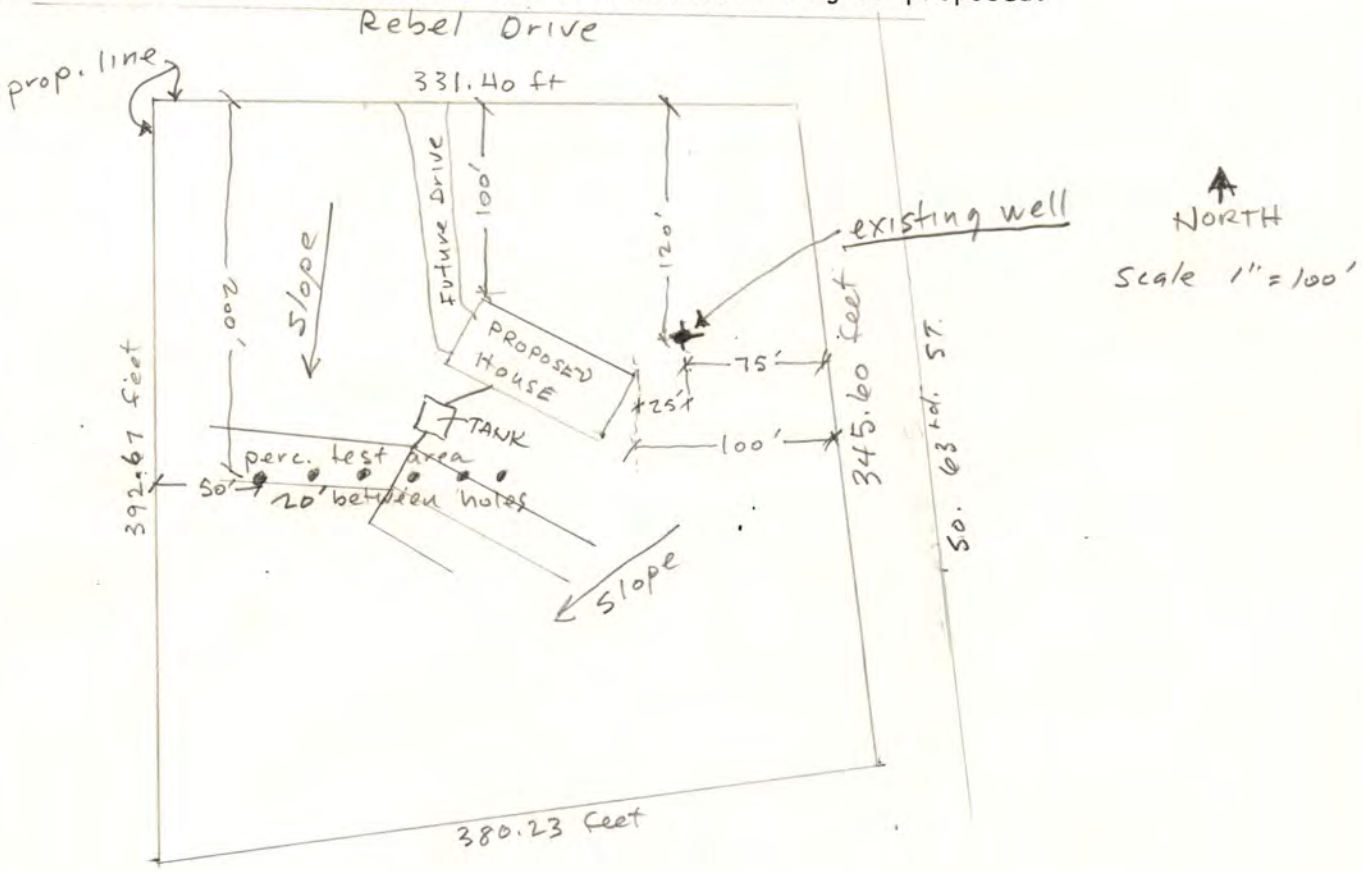

Distance from existing well to proposed laterals 120' to 150'

4 laterals 100'
1 lateral 20'

Lot 4 block 3
Yankee Ridge estates
3.0 Acres.

6201 Rebel Drive

REVIEWING ACTION

Remarks: _____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals 155 ft.
3. With a Trench Width of 48 in.
4. Total Area of Lateral needed 620 sq.ft.

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: SEPT 6 1983

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material 3034 ; Diameter 4 in.
2. Distance above basement floor — in., or below basement floor 16 in.
3. Distance between dwelling and septic tank 88 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line 65 ft.;
Stream — ft.; Pressure Line — ft.; Property Line 130 ft.

B. SEPTIC TANK:
1. Material CONC. ; No. of compartments ONE .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company PRECAST STEP)
4. Manholes: Over Inlet; diam. 12 in.
Over Outlet; diam. 15 in.
Riser Above ☒ Below ☒ Grade 6 in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 6 in.
8. Distances to:
Well or Suction Line 145 ft.;
Stream — ft.; Pressure Line — ft.; Property Line 160 ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 5 .
2. Factory Built: Yes ☒ No ☐
(Company PRECAST STEP)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 20" or
Perforated Pipe _____ .
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____ .
2. Lateral Lines:
Number 2 ; Length of each line 100', 100', _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines _____ ft.
3. Trench dimensions: Width 4 ft.;
Slope 3 in/100 ft.; Average Depth 36 in.
4. Filter Material: ROAD GRAVEL
Depth of Material 22 in.
5. Distances to:
Well or Suction Line 168 ft.;
Stream — ft.; Pressure Line — ft.; Property Line 45 ft.

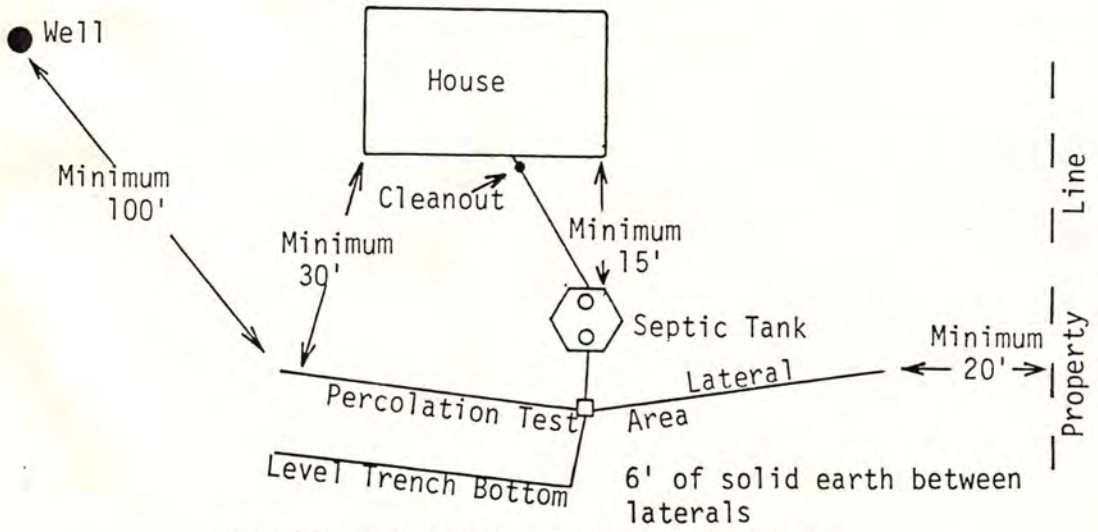


TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE SEPT 1, 1983 INSTALLER JAMES E. ARTER

KEN LIENWEBER BALKHOE
BEATRICE, NEBR.

LATERAL & TANK SET
BY PRE CAST STEP CO.

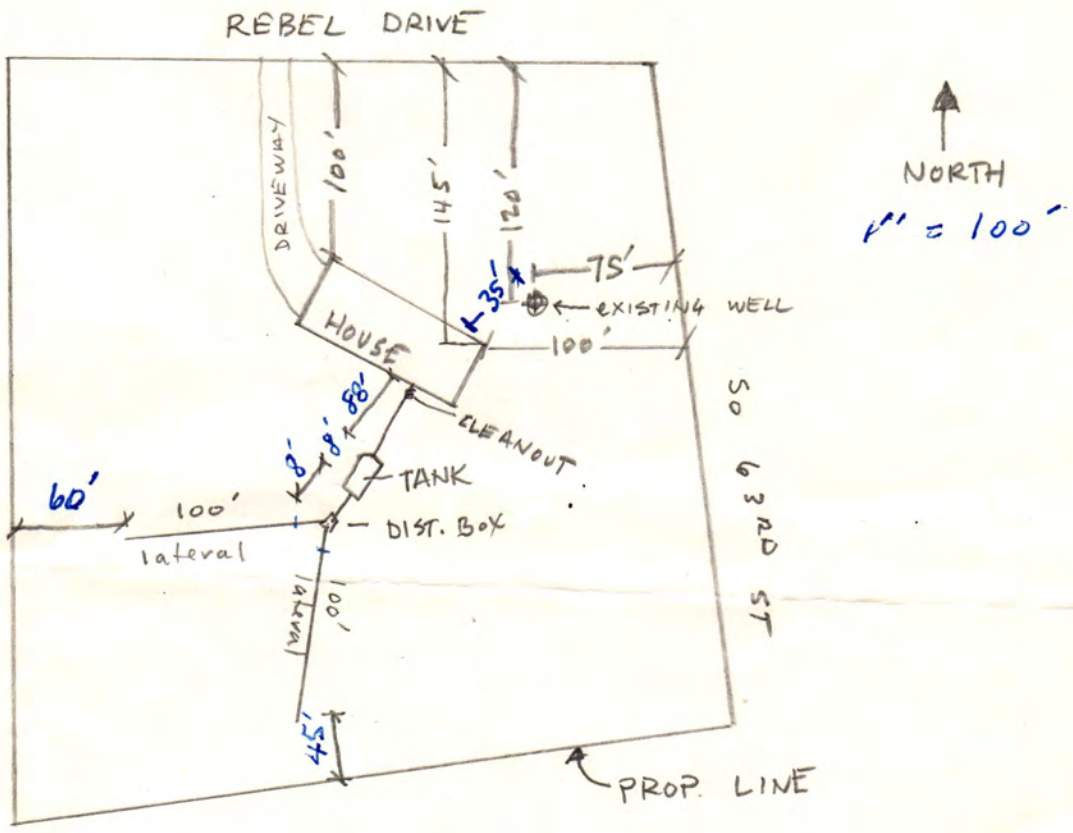

LOT 4, BLOCK 3, YANKEE RIDGE ESTATES
6201 REBEL DRIVE
