LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

P E R M I T

Permit
SEWAGE INSTALLATION

No. 93380102301

Issued 07/12/93
Expires 01/12/94
Revenue Code 18754

Establishment
MIKE REZAC
T9N R7E SEC 28
YANKEE RIDGE 2ND ADD BLK 4 LOT 21
6700 BOLTON ROAD

FEES: $150.00

TOTAL $150.00

Permittee
MIKE REZAC
1830 W BURNHAM
LINCOLN NE 68522

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

Building Permit # B9302023

DATE: 7/9/93

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 28 ; Block 4 : Lot 20 : Addition Yankee Ridge 2nd Add.
   Street Address 6700 Bolton Rd.

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe_____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐

4. Distance to public sewer: _____ft. WILL INSTALL WHATEVER SOIL PERC TEST INDICATES

Mike Rezac
Signature of Applicant (Owner or Lessee)

1830 West Burnham 68522
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/9/93 . Date Frwd. 7/12/93 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd._____. Date Frwd._____. ACTION: Approved ☑ Disapproved ☐ Signature: Norma

3. City or County Engineer : Date Rec'd. 7-12-93 . Date Frwd. 7-12-93 . ACTION: Approved ☒ Disapproved ☐ Signature: Dennis Daniels

REMARKS OR REASONS FOR DISAPPROVAL_____

Site Visits:
Date: 10/7/93 by: J.C.H. Hood Drawing
Date:_____ by:_____
Date:_____ by:_____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 10/12/93 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township _____; Range _____; Section & ¼ Section _____.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 11-29 to 11-30-90. Weather: Precip. — Temp. 40°.

X OWNER: _____

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	26"	11-29	4:00 PM	11-30	7:30 AM	11-30	11:30	11 1/8	12:00	12 1/4	30	1 1/8	
2								12 1/2		13 1/4		3/4	
3								12 1/2		13 1/2		1	
4								10 1/2		11		1/2	
5								9 3/4		9 7/8		1/8	
6								11 1/4		11 3/4		1/2	

Larry Schwarck
Signature of Person Conducting Test

Address 8200 old cheney Phone 489-7294

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____

Soil Type (SCS): _____


Date: _____

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

FORM 20102-0477 PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application) City Ordinance No. 9150 ☐ County Resolution No. 2832 ☒	LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT Division of Environmental Health 2200 St. Marys Avenue Lincoln, Nebraska 68502 Phone: 471-7800 **C**
Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.	FILE NO._____

Indicate on sketch if residence and well are exisiting or proposed.

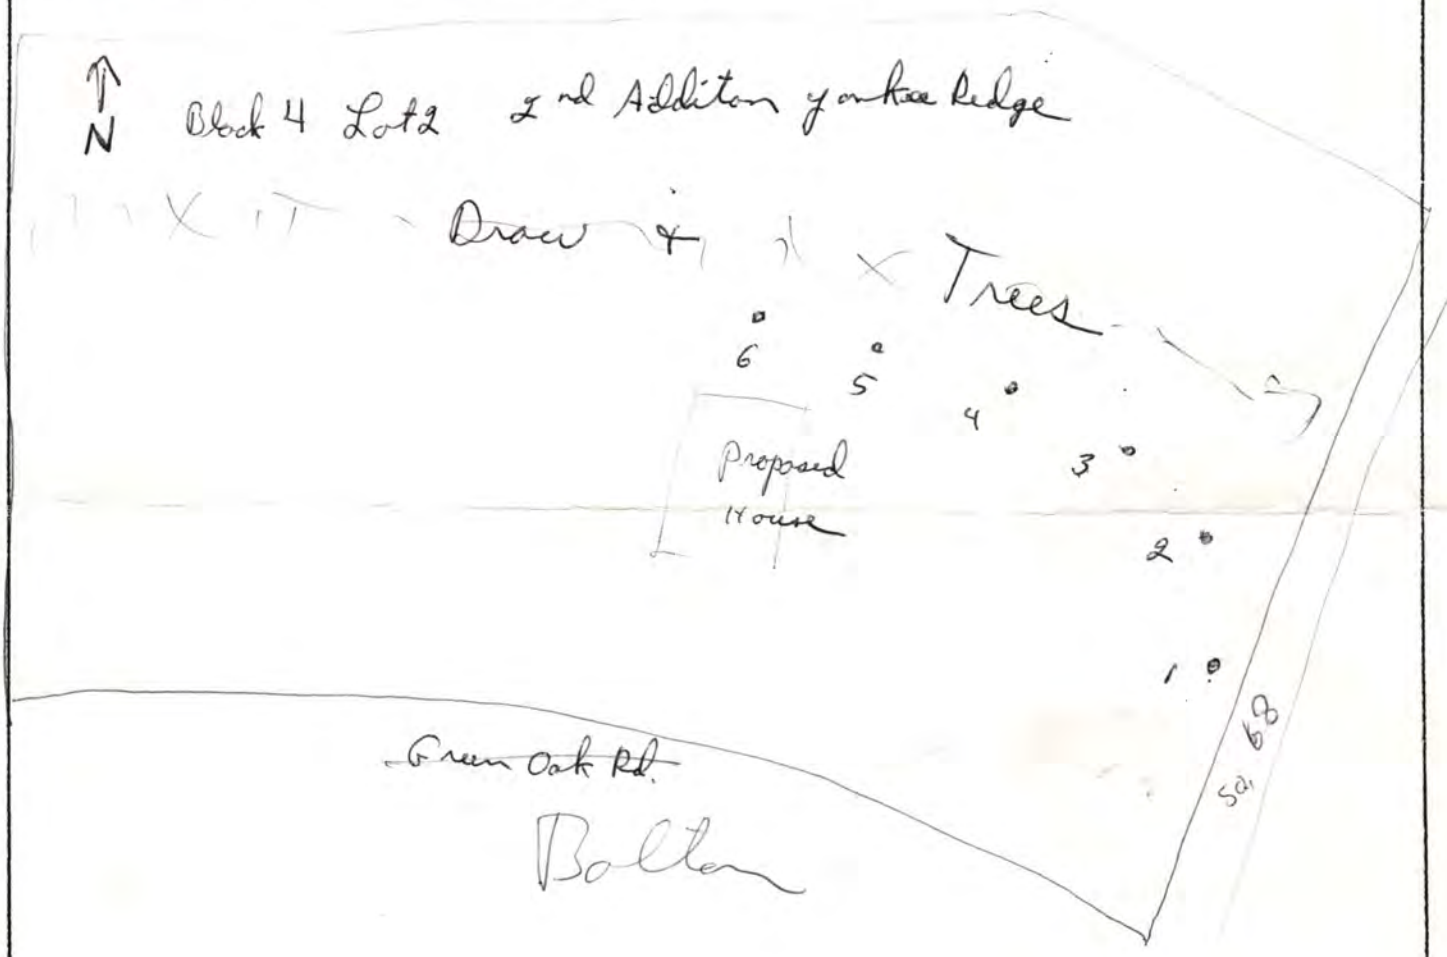

REVIEWING ACTION

Remarks:_____

_____

Date:_____

Minimum Design Requirement

1. Capacity of Septic Tank_____gals.
2. Total Length of Laterals_____ft.
3. With a Trench Width of_____in.
4. Total Area of Lateral needed____sq.ft.

_____

Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Class 160; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 18 in.
3. Distance between dwelling and septic tank 65 ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Precast; No. of compartments _____.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 8" in.
8. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Precast; Number - available outlets _____.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank 10 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 3; Length of each line 100, 100, 100, _____, _____ ft.;
Total length of laterals 300 ft.;
Distance between lateral lines 6 ft.
3. Trench dimensions: Width 3 ft.;
Slope 2 in/100 ft.; Average Depth 32 - 24 in. 49 Tom
4. Filter Material: Road Gravel
Depth of Material 14 in.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

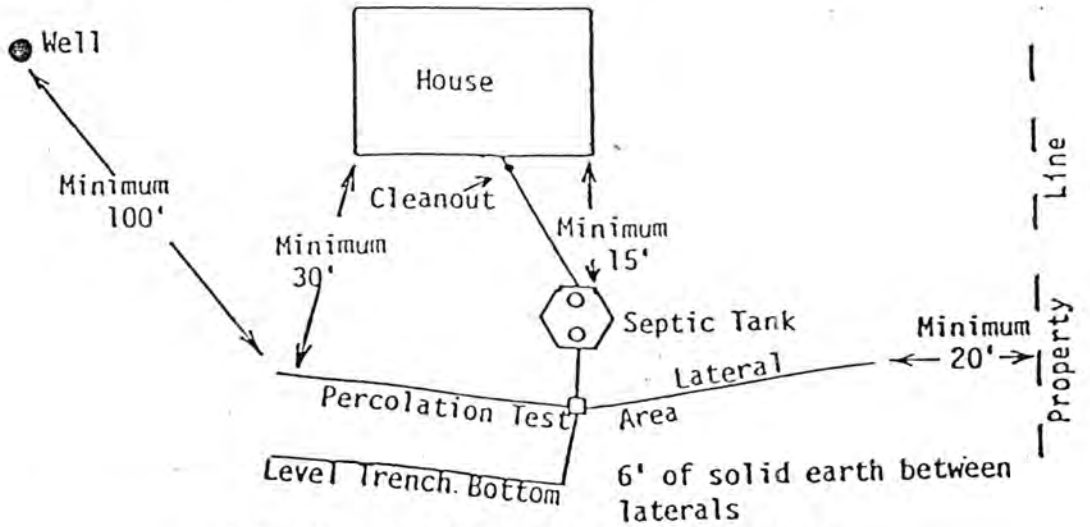

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

Larry Schwanck

10-7-93

N

