LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1298-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

October 14, 1978 — THIS PERMIT EXPIRES

Paul Harms — ISSUED TO

3243 West Summit Blvd., Lincoln, NE — ADDRESS

T9N, R7E, Section 31, Lot 25 I.T. (EXTEND) — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 15.00	$	$	$ 15.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1298C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 4-13-78

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 7E ; Section 31 ;
Block ; Lot 25 I.T. ; Addition
Street Address

2. Property Use: Residential ☒; Commercial ☐
No. Bedrooms 3
Describe
Other Use ☐
Describe

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair:

5. Work to be done by: Owner ☐ ; or Contractor ☐ , Sintek Service Co.
Contractor's Name 2425 So. 21st

6. Estimated cost of project:

a. Materials	$	
b. Labor	$	
c. Other	$	
TOTAL	$	3155 88

Paul Harms
Signature of Applicant (owner or lessee)

So 27 R.R. City
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd:
Filing Fee: $ 15.00

2. Site Visits:
Date: 4/13/78 by: J.C.H.
Date: 4/13/78 by: J.C.H.
Date: 4/13/78 by: J.C.H.

3. Date: Approved ☒; Disapproved ☐
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 4/14/78 by: J. C. Hood

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1298-C

PROPERTY WHERE SOIL TESTED:

Location: Township 9N ; Range 7E ; Section & ¼ Section 31 . Lot 25 IT
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).

Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☒ .

Dates of Tests: 4-10-78 to 4-11-78 . Weather: Precip. N Temp. 60 .

OWNER: Paul Harms

Address: 5027 R.R. City

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1.	24"	8 AM	—	4-10	5 PM	4-11	11 AM	6	12 AM	4 13/16	1 Hr		
		4-10										55 m	
2.	"	"		"	"	"	"	"	"	"	1 Hr	To	
												drop	
3.	"	"		"	"	"	"	"	"	"	1 Hr	1"	
4	24"	8 AM	upon	slope	12 PM	would not pass							
5	"	no	Room	for	Lagoon								
6	"												

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Sintek Service
Signature of Person Conducting Test

Address 2425 Lo St Phone _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____

Soil Type (SCS): _____

Date: _____

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. 1398-C


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Pla ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.


B. SEPTIC TANK:
1. Material conc ; No. of compartments 1.
2 Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre Cast)
4. Manholes: Over Inlet; diam. 4 in.
Over Outlet; diam. 4 in.
Riser Above ☐ Below ☐ Grade 8 in Risers installed
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 8 in.
8. Distances to:
Well or Suction Line 75 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material 2 Boxes Pla ; Number - available outlets 7 each.
2. Factory Built: Yes ☒ No ☐
(Company Hand one)
3. Distance from Septic Tank 355 ft. 1st 376 2nd

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 4 ; Length of each line 90', 100', 100', 26', _____ ft.;
Total length of laterals 316' ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 36 ft.;
Slope 4 in/100 ft.; Average Depth 36 in. + 3" extra in Road Gravel bottom
4. Filter Material: Road Gravel bottom
Depth of Material 12+3=15 in.
5. Distances to:
Well or Suction Line 426 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 150 ft.

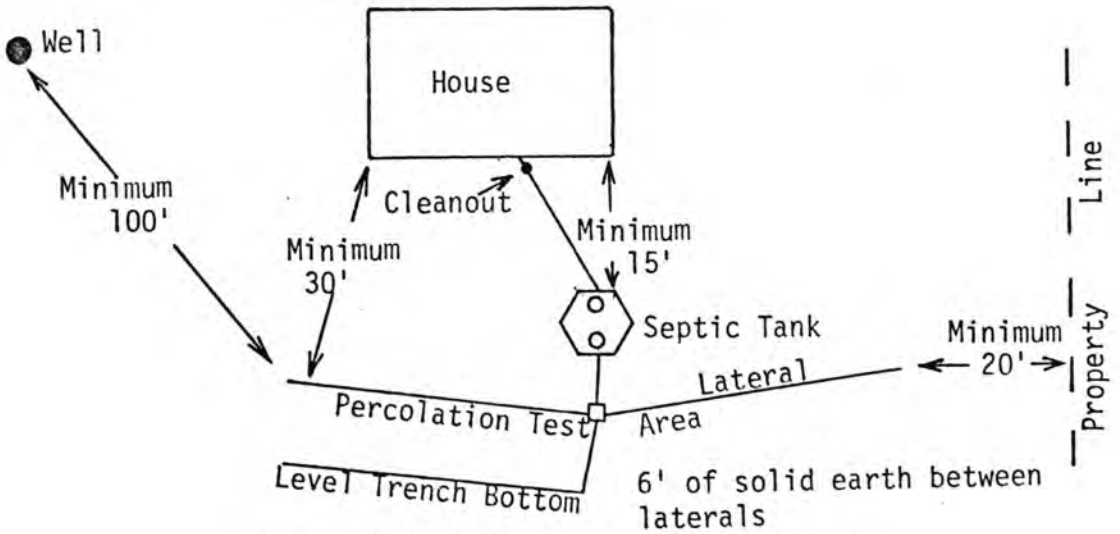

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

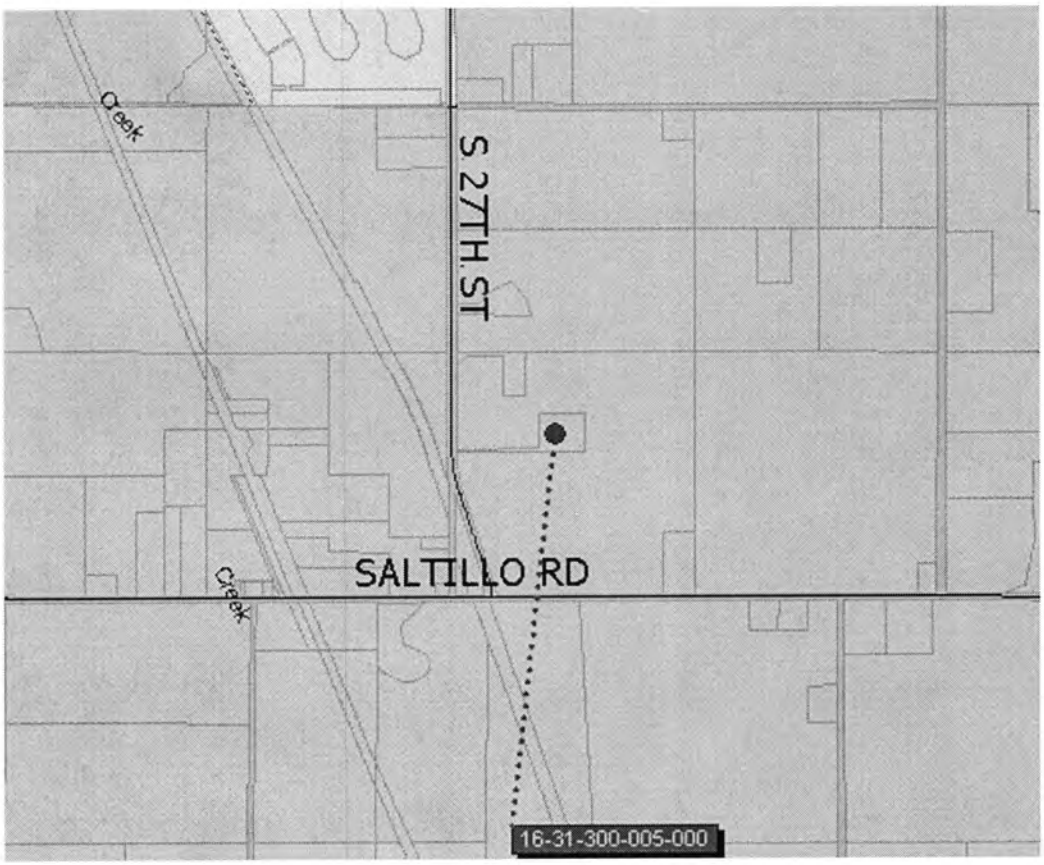
Creek
S 27TH ST
SALTILLO RD
Creek
16-31-300-005-000

Coli + No3
12/10/01

Lincoln-Lancaster County Health Department

3140 "N" Street, Lincoln, Nebraska 68510 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

FOR PROPERTY IN **LANCASTER COUNTY** ONLY

This form must be completed and returned with payment to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: "Lincoln-Lancaster County Health Department" or "LLCHD"

☑ Enclosed is $200.00. Allow two weeks for processing. Incomplete information will delay processing.

Legal Description of Property: Street Address 11000 S 27th Rural

Parcel ID 16 - 31 - 300 - 005 - 000 (i.e. 99-99-999-999-999)

Twp 9N Range 7 Section 31 1/4 ___ 1/4 ___ Block ___ Lot 25 Addition ___

Directions to Property See attached Map

Location of Well Next to Flagpole Tap Location: Inside ☐ Outside ☐

Location of Sewage System North of Flagpole Year Installed 96 Ripped 78'

Site Hazards (dogs, etc.) N/A

	NAME	ADDRESS	PHONE
Present Owner:	Eileen M & Paul J Harms	753 Tanner Dr. Paso Robles, CA 93446	(805) 237-2779
Tenant/Buyer:			
Return to:	Andrew Kozlewski,	Wolfe, Snowden, Hurd, Luers & Ahl Suite 830, 1248 O St Lincoln, NE 68508	474-1507 474-3170 (Fax)

Signature of Applicant [signature] attorney for the Harms Address see above Date 12/07/01

HEALTH DEPARTMENT USE ONLY

RECEIVED Date 12/07/01 Amount 200.00 Check No. 29474 Initials ___

DATA ENTRY Date ___/___/___ Case No. ___ Initials ___

PRELIMINARY STATUS--By Jerrold C. Hood **DATE:** 12/10/01

WATER SYSTEM:	Approved	Disapproved
Construction	☒	☐
Bacteria	☒ 0 /ml	☐ ___ /ml
Nitrate	☒ 1.2 ppm	☐ ___ ppm

SEWAGE SYSTEM	
Approved	☒
Provisional	☐
Disapproved	☐

Additional Site Visits

Date ___/___/___ by ___

Date ___/___/___ by ___

Date ___/___/___ by ___

Comments: IF THE SEPTIC TANK HAS NOT BEEN PUMPED RECENTLY IT SHOULD BE CHECKED TO SEE IF IT IS NEEDED.

See Attached Letter ☐

FINAL STATUS

WATER SYSTEM: Approved ☒ **SEWAGE DISPOSAL SYSTEM:** Approved ☒ Provisional Approval ☐

Approved by Jerrold C. Hood R.E.H.S. Date 12/13/01

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

White - Applicant after approval Yellow - Environmental Health Pink - Business Office

Revised/Reprint: 9-00

AS BUILT DRAWING OF SYSTEM

DATE 4-13-78 INSTALLER Sentek Service Co.

