FILE NO. 1926

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

MARCH 29, 1983 — THIS LICENSE OR PERMIT EXPIRES

LARRY SCHWARCH — LICENSEE OR PERMITTEE

8200 OLD CHENEY ROAD LINCOLN, NE 68516 — ADDRESS

T9N, R7E, SECTION 32, BLOCK 1, LOT 2, ADDITION: HYLANDS — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: NONTRANSFERABLE EXTEND PERMIT

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
018754	110.76	148.14	6-2

SERIAL NO.	DATE	AMOUNT
622443	3-29-83	30.00

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

HEALTH APPLICATION

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☒

County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1926

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 9-24-82

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 7E; Section ~~22~~ 32 ;
Block 1 ; Lot 2 ; Addition The Hy Lands
Street Address 50 56th Rt 8

2. Property Use: Residential ☒; Commercial ☐
No. Bedrooms 3
Describe
Other Use ☐
Describe

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair:
Added 100 ft Lateral

5. Work to be done by: Owner ☐ ; or Contractor ☒ , Larry Schwarck
Contractor's Name

6. Estimated cost of project:

a. Materials	$	250
b. Labor	$	300
c. Other	$	
TOTAL	$	550.00

Larry Schwarck
Signature of Applicant (owner or lessee)

8200 old Cheney
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd:
Filing Fee: $ 30.00

2. Site Visits:
Date: by: J.C.H.
Date: by:
Date: by:

3. Date: Approved ☒; Disapproved ☐
by: Jerold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 9/29/82 by: J.C. Hood

* PROVISIONAL; GROUND WATER SEEPAGE INTO DITCH

FORM HD-32a(67) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
Ordinance No. 9150 11011 S 56+4

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

T9N, R7E, SEC. 32, BLOCK 1, LOT 2, THE HIGHLANDS

FILE NO. _____

SPECIFICATIONS

OUTSIDE 3 MILE JURISDICTION DATE: _____


A. BUILDING SEWER:
1. Material PLASTIC; Diameter 4 in.
2. Distance above basement floor ___in.; or below basement floor ___in.
3. Distance between dwelling and septic tank 88 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 50 ft.;
Stream — ft.; Pressure Line ___ft.;
Property Line ___ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material FIBERGLASS; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ___in.
3. Factory Built: Yes ☒ (Company CORRIGATED FIBERGLASS)
No ☐
4. Manholes: Over Inlet; diam. 16 in.
Over Outlet; diam. ___in.
Below Grade _____in.
5. Inlet: Baffle ☒; or Tee ☐
6. Outlet: Baffle ☒; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade ___in.
8. Distances To:
Well or Suction Line 100 ft.;
Stream — ft.; Pressure Line ___ft.;
Property Line ___ft.


C. DISTRIBUTION BOX
1. Material CON; No. available outlets 5.
2. Factory Built: Yes ☒, (Company PRE-CAST STEP) No ☐
3. Dimension: Length ___in.; Width ___in. Depth ___in.
4. Distance from Septic Tank 4'8" ft.
5. Serial Distribution: Yes ☐, No ☒ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: HALF ROUND
2. Lateral Lines: Depth below grade ___in. Number 2; Length of each line 100 ft Total length of Laterals 200 ft.; Slope 4 in/100 ft. Diameter of pipe 12 in.; Shape O
Material: concrete ☐; fiber asbestos ☐; clay ☐; other FIBERGLASS
Distance between lateral lines 10 ft.
3. Trench Dimensions: Depth 48 in.; Width 48 in.
4. Filter Material: GRAVEL.
Depth of material from trench bottom ___in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream — ft.; Pressure Line ___ft.
Property Line 20 ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

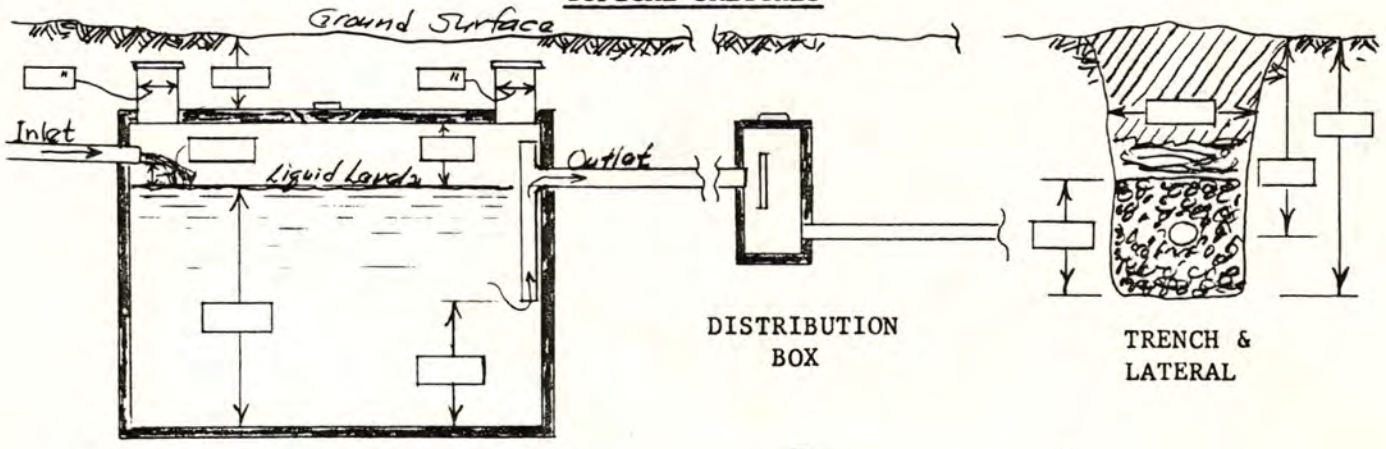

ROGER BAILEY-INSTALL
Signature of Applicant

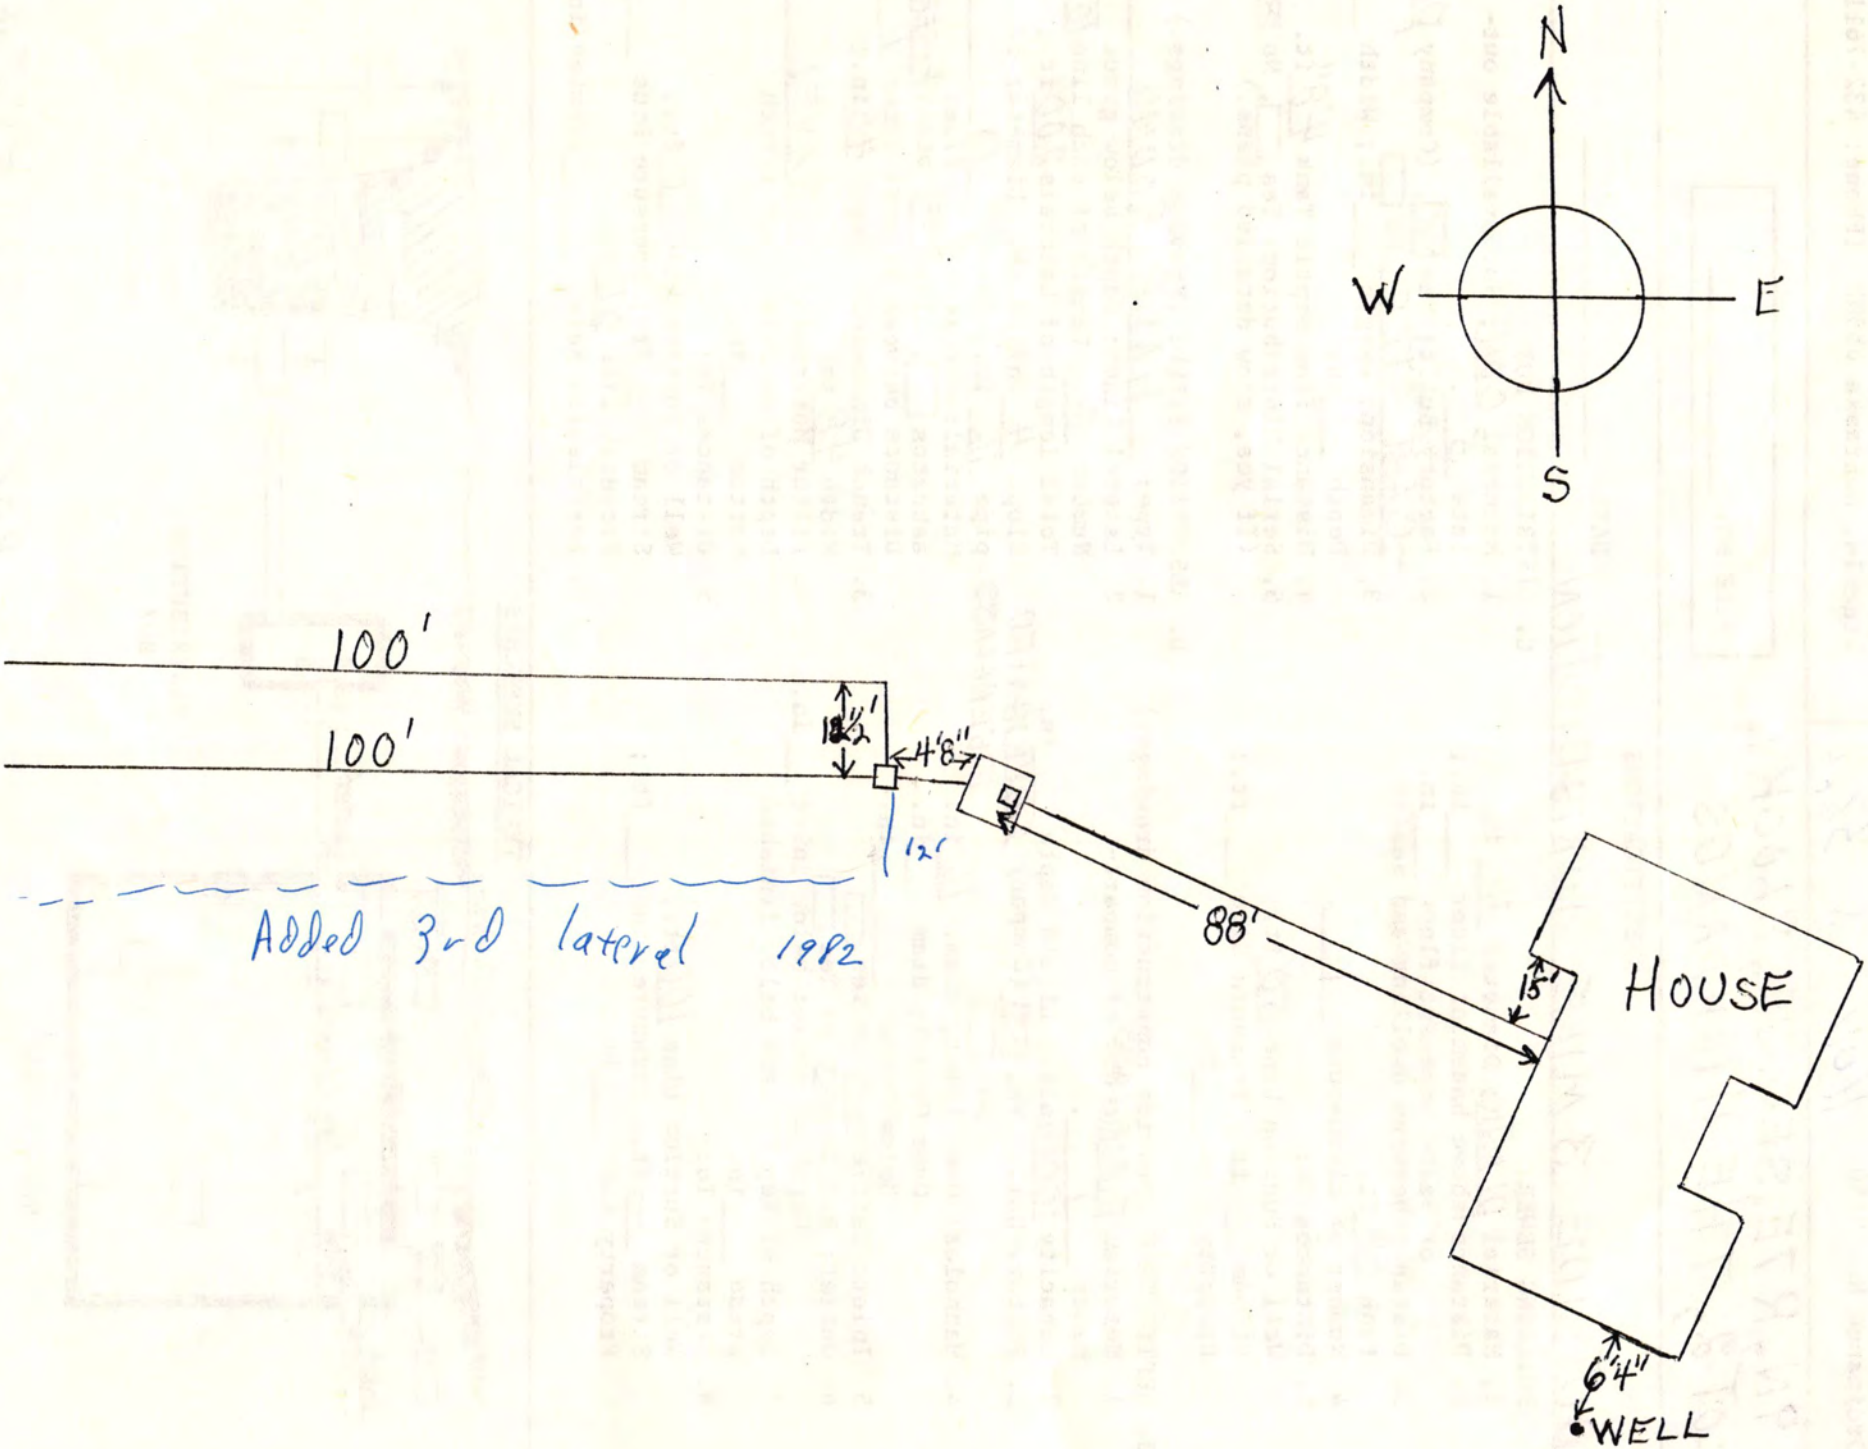
N
W
E
S
100'
100'
12½'
4'8"
12'
Added 3rd lateral 1982
88'
15'
HOUSE
6'4"
WELL
