LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET ENVIRONMENTAL HEALTH DIVISION Lincoln, NE 68510-1514 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit

SEWAGE INSTALLATION

No. 95380136501

Issued 10/26/95
Expires 04/26/96
Revenue Code 18754

Establishment

SAM MANZITTO
T9N R7E SEC 32
SILVER SPRINGS ADD BLK 1 LOT 1
10711 CROMWELL ROAD

FEES: $150.00

TOTAL $150.00

Permittee

SAM MANZITTO
3341 PIONEERS BLVD
LINCOLN NE 68506

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
3140 N Street
Lincoln NE 68510
(402)-441-8022

A

FILING FEE: $_____

FILE NO._____

DATE: 10-23-95

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 32 ;
   Block 1 : Lot 1 : Addition Silver Springs Addition
   Street Address 10711 Cromwell Rd.

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe_____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐

4. Distance to public sewer: N/A ft. EXPERIMENTAL SYSTEM

SAM MANZITTO

Signature of Applicant (Owner or Lessee)

3341 Pioneer Blvd.
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 10/23/95. Date Frwd. 10/24/95. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 10/24/95. Date Frwd. 10/24/95. ACTION: Approved ☒ Disapproved ☐ Signature:

3. City or County Engineer : Date Rec'd. 10/24/95. Date Frwd. 10/24/95. ACTION: Approved ☒ Disapproved ☐ Signature:

REMARKS OR REASONS FOR DISAPPROVAL_____

Site Visits:
Date: 6/26/96 by: J.C.H. SEWER, TANK, & LATERAL TRENCHES
Date: 7/2/96 by: J.C.H.
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 7/2/96 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* EXPERIMENTAL SYSTEM HENCE APPROVAL IS PROVISIONAL

FORM 23-43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

Lincoln-Lancaster County Health Dept.
3140 "N" Street
Lincoln, NE 68510

D

DATE: _____

FILE NO.: _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 12 in.
3. Distance between dwelling and septic tank 132 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.


B. SEPTIC TANK:
1. Material CONCRETE; No. of compartments ____.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☑ No ☐
(Company Pre CAST)
4. Manholes: Over Inlet; diam. ____ in.
Over Outlet; diam. ____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☑ ; or Tee ☐
6. Outlet: Baffle ☑ ; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

C. DISTRIBUTION BOX:
1. Material CONCRETE ; Number - available outlets 5.
2. Factory Built: Yes ☑ No ☐
(Company Pre CAST)
3. Distance from Septic Tank 9 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☑ Perforated Pipe ☐
Diameter of Half Round ____ or Perforated Pipe ____.
Material: fiberglass ☐ ; plastic ☑ ; concrete ☐ ; other ____.
2. Lateral Lines:
Number 2 ; Length of each line 100, 100, ____, ____, ____ ft.;
Total length of laterals ____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 8 ft.; Slope ____ in/100 ft.; Average Depth 42 in.
4. Filter Material: Gravel
Depth of Material 24 in.
5. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

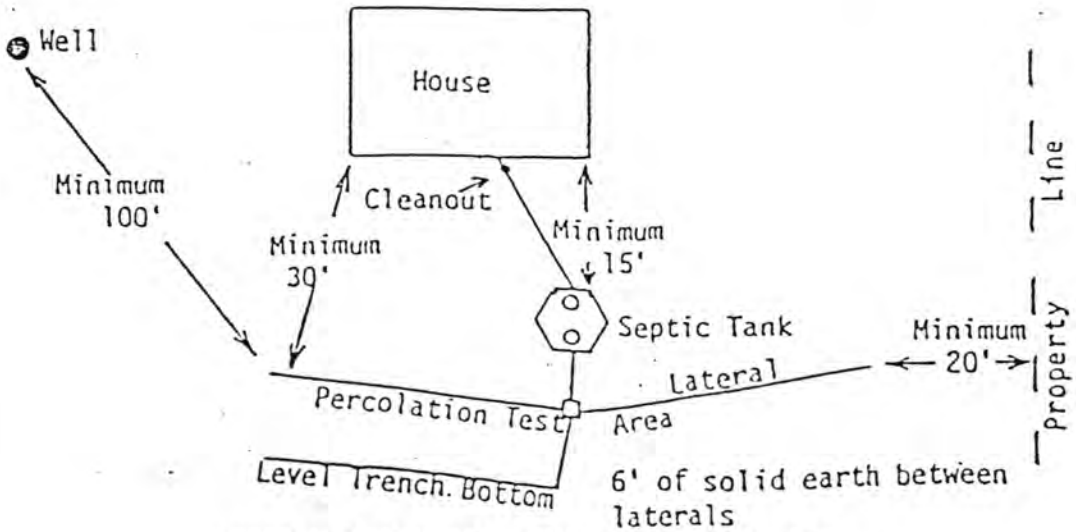

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

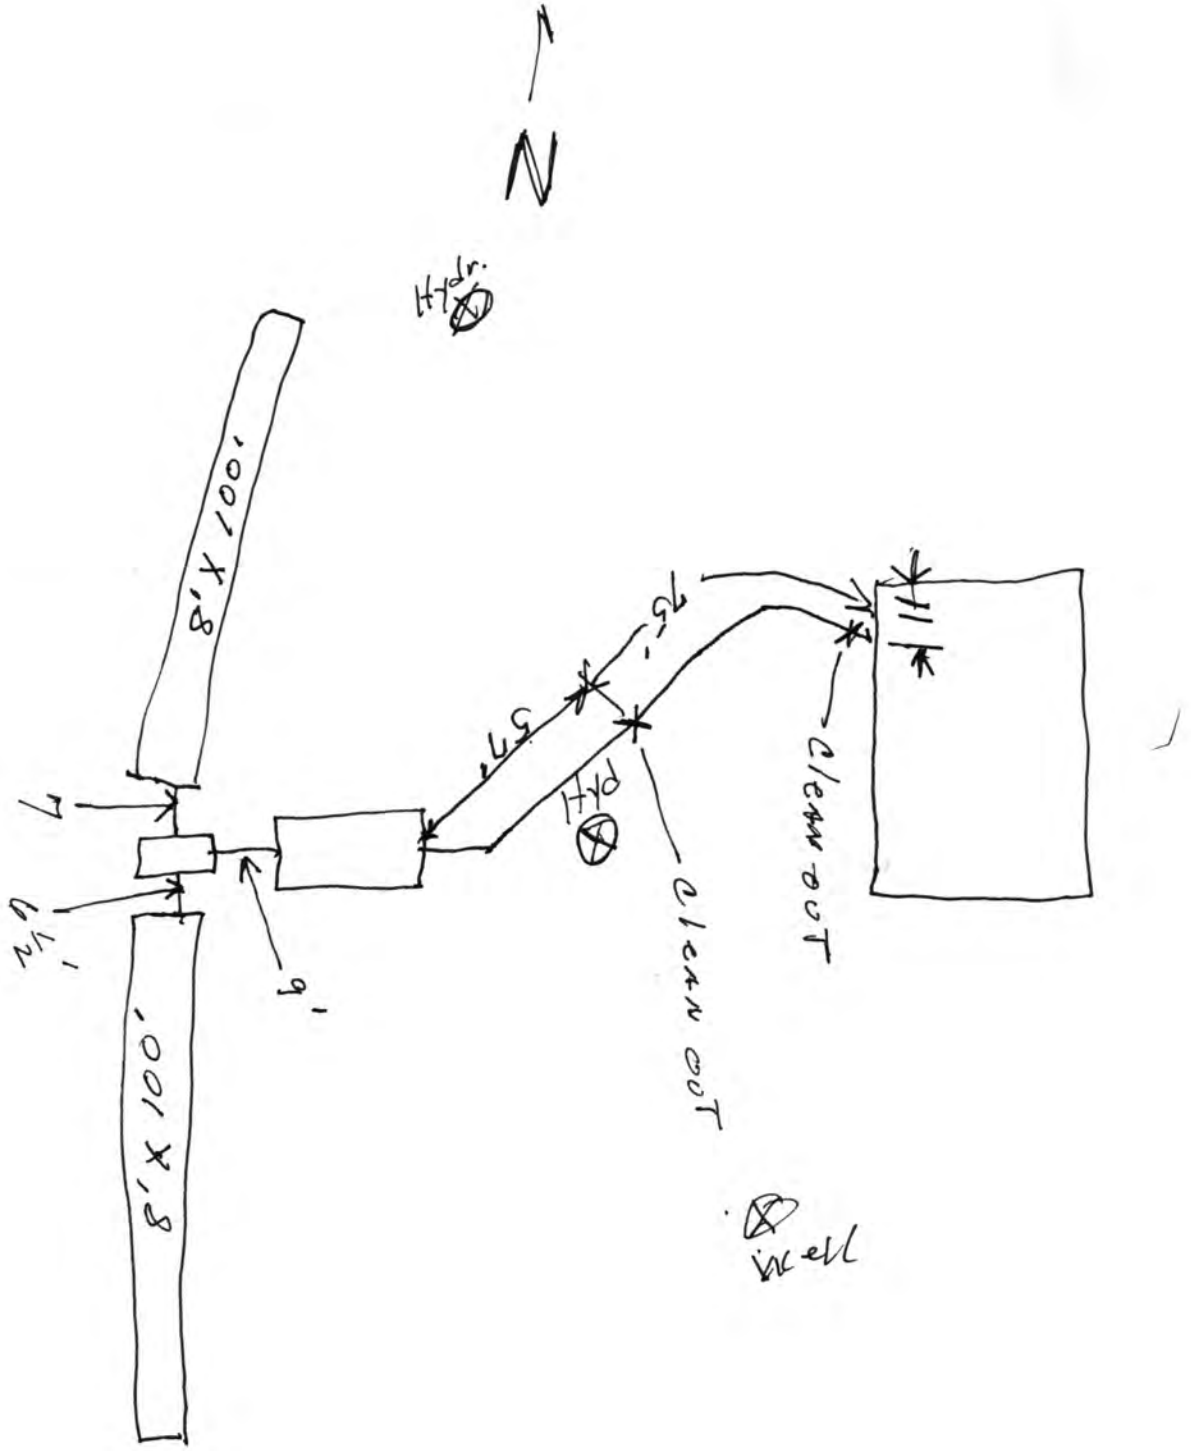

Capetal City Trenching
7-2-96
