LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1459-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

May 14, 1979 — THIS PERMIT EXPIRES

Paul von Gillern — ISSUED TO

3308 North Cotner Blvd., Lincoln, NE — ADDRESS

T9N, R7E, Section 32, Block 4, Lot 3, Addition the Highlands — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE (Extend)

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 15.00	$	$	$ 15.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

Health — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

Martin Dye
Rt 8
Lincoln, Nebr 68506

FILE NO. 1459-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 11-6-78

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 7E ; Section 32 ;
Block 4 ; Lot 3 ; Addition THE HIGHLANDS
Street Address _____

2. Property Use: Residential _____ ☒; Commercial _____ ☐
No. Bedrooms 3 Describe Home
Other Use ☐
Describe _____

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: 100' of 12" Conn-A-Flow Laterals (Tank Perc Test at west & east ends of Lot)

5. Work to be done by: Owner ☐ ; or Contractor ☒, Gaylen Gillum
Contractor's Name
This System 8 years on One Hundred foot of Hall Board

6. Estimated cost of project:

a. Materials	$
b. Labor	$
c. Other	$
TOTAL	$ over $200.00

Gaylen Gillum
Signature of Applicant (owner or lessee)

3508 N Cotner Blvd
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd: _____
Filing Fee: $ 15.00

2. Site Visits:
Date: 11-6-78 by: jpv
Date: _____ by: _____
Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐
by: Jerold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 11-14-78 by: James Devorkin

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 11-7-78 Repair

FILE NO. 1459-C


SPECIFICATIONS AS BUILT Martin Dye RT 8 Lincoln, Nebr 68506

A. BUILDING SEWER:
1. Material Plastic; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor ____ in.
3. Distance between dwelling and septic tank ____ ft.
4. Number of clean-outs ____.
5. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

B. SEPTIC TANK:
1. Material ____; No. of compartments ____.
2. Capacity ____ gals.;
3. Factory Built: Yes ☐ No ☐
(Company ____)
4. Manholes: Over Inlet; diam. ____ in.
Over Outlet; diam. ____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade ____ in.
8. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

C. DISTRIBUTION BOX:
1. Material ____; Number - available outlets ____
2. Factory Built: Yes ☐ No ☐
(Company ____)
3. Distance from Septic Tank ____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 12" or Perforated Pipe ____.
Material: fiberglass ☒; plastic ☐; concrete ☐ ; other ____.
2. Lateral Lines:
Number ___; Length of each line 100', ____, ____, ____, ____ ft.;
Total length of laterals ____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 4' ft.; Slope 2" in/100 ft.; Average Depth 22" in.
4. Filter Material: Rock Gravel & Sand
Depth of Material 4" & 6" Sand in.
5. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

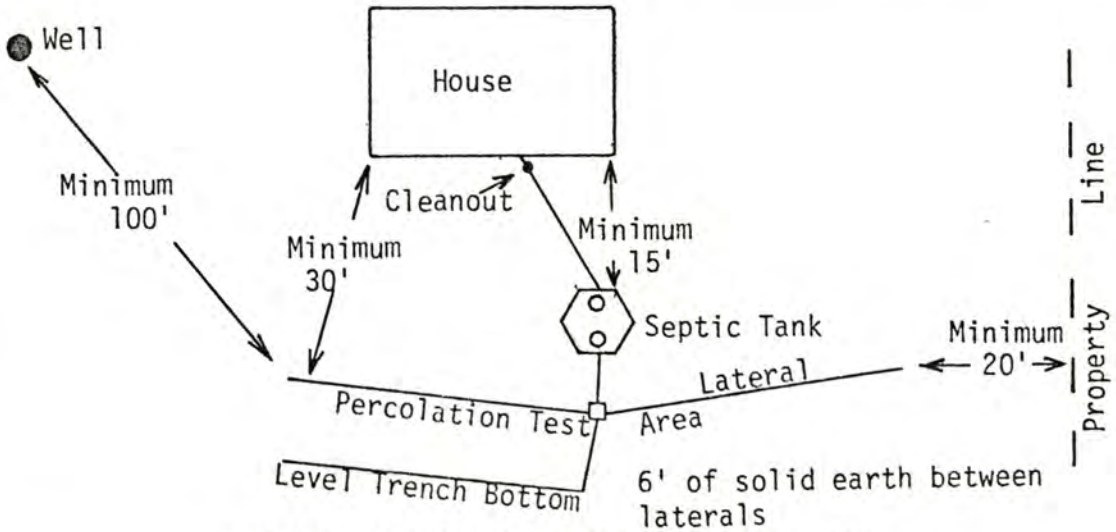

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 11-7-14 INSTALLER Tom Gilliam

