Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

NOV 29 2010

D

Permit Number:

Onsite Wastewater Treatment System

As Built Plans & Specifications

1st Add B 2 L 3

Date 11/23/10 Legal Description NW 1/4 33-9-7 1/4 Section Township Range Nealrene Acres

Onsite System Location

Address (no rural route) 10635 Weeks Dr City Lincoln NE, Zip 68516

Owner Sam Lambert Address same

A. Sewer Pipe

1. Material: 9' SDR35 (old) 68' SDR26 New.
   Diameter: 4 in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: 77' ft.
4. Number of clean-outs: one
5. Distances to: well or suction line 100+ ft.
   stream 100+ ft.
   pressure line 100+ ft.
   property line 100+ ft.

B. Septic Tank

☐ Label with Manufacturer, address and gallon capacity

1. Material: concrete
   Number of compartments: 1
2. Capacity: 1,500 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter 24 in.
   Over outlet, diameter 24 in.
   Riser: ☐ above ☐ below grade At grade in.
5. Inlet: ☐ baffle ☐ tee ☐ 6" dia. inspection pipe
6. Outlet: ☐ baffle ☐ tee ☐ 6" dia. inspection pipe
7. Depth to top of tank, below unfinished grade: 36-30 in.
8. Distances to: Well or suction line 100+ ft.
   Stream 100+ ft.
   Pressure line 100+ ft.
   Property line 100+ ft.

C. ☐ Distribution Box ☑ Drop Boxes

(≥ 12" inspection opening) (removable lid to inspect)

1. Material: Endcaps
   Number available outlets: 2
2. Factory built: ☑ Yes ☐ No
3. Distance from septic tank: 27' ft.

D. Drainfield Absorption


☑ Trench ☐ Bed ☐ Level Bottom

1. Type: ☐ Half rounds ☐ Perforated pipe ☐ Chambers
   Diameter or width: _____
   Number of distribution lines in bed _____
   Material: ☑ fiberglass ☑ plastic ☐ concrete
   ☐ other _____
2. Drainfield Laterals: Number 2 90 old
   Length of each line: 116 New ft. 90 New ft.
   90 new ft. _____ ft., _____ ft.
3. Drainfield dimensions: Width 40 ft.
   Distribution Pipe Slope Flat in/100 ft.
   Average depth 4' - 12'4" in
4. Filter material: Dirt
   Depth of material 4' - 12'4" in.
5. Distances to: Well or suction line 100+ ft.
   Pressure line 100+ ft.
   Property line 20+ ft.
   House or building 100+ ft.
   Lake or Stream 100+ ft.

Complete As-Built drawing on the back fo this form.

Indicate North with Arrow

Onsite Wastewater System Design (Example)

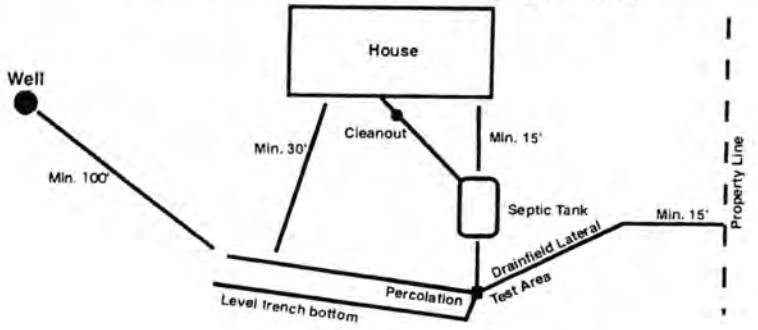

Lincoln-Lancaster County Health Department

2200 St. Mary's Avenue, Lincoln, Nebr

ORIGINAL LOAN APPROVAL FILE
PREVIOUS HISTORY UNKNOWN

REAL ESTATE TRANSFER/LC

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☐ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☐ Evaluation of the Individual Water System ☐ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address 10635 Weeks Dr. Lincoln NE FIRST ADD.
Twp 9N Range 7E Section 33 1/4 ____ 1/4 ____ Block 2 Lot 3 Addition NEALRENE ACRES
Directions to Property from 70th & Hwy 2 south on 70th 3 miles to Rokeby Rd then west 3/4 mile then south on Weeks Dr. 1/2 mile on west side of Road
Location of Well in front by window Tap Location: Inside ☒ Outside ☐
Location of Sewage System on North side of house Year Installed UNKNOWN

	NAME	ADDRESS	PHONE
Present Owner:	Rick Cullus	10635 Weeks Dr Lincoln NE 68516	402-421-1828 402-472-9860
Tenant/Buyer:	UNKNOWN		
Return to:	Real Estate Support Services	5200 Humboldt Ave. S #214 Minneapolis, MN 55431	

Signature of Applicant Real Estate Support Services Address 5200 Humboldt Ave S Minneapolis, MN 55431 Date 11/15/93

HEALTH DEPARTMENT USE ONLY

Date Received 11/18/93 LS Received $150.00 Check ☒ #089671 Cash ☐

PRELIMINARY STATUS--By Verrold Hood **DATE:** 11/23/93

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM	Additional Site Visits
Construction	☐	☒	Approved ☐	Date 12/7/93 by C.H.
Bacteria	☒ 0 /ml	☐ ____ /ml	Provisional ☒	Date ___/___/___ by ____
Nitrate	☒ <0.1 ppm	☐ ____ ppm	Disapproved ☐	Date ___/___/___ by ____

Comments: SCREW IS MISSING OUT OF ELECTRICAL PLATE ON WELL HEAD. NEED EXPLANATION OF SEWAGE SYSTEM CONSTRUCTION. Screw replaced & explanation recieved on sewage system. SEWAGE SYSTEM OPERATES WITHIN REGULATIONS AND INSPECTIONS HENCE APPROVAL IS PROVISIONAL. NO EVIDENCE OF MALFUNCTION. ☐ See Attached Letter

FINAL STATUS

WATER SYSTEM: Approved: ☒ **SEWAGE DISPOSAL SYSTEM** Approved: ☐ Provisional Approval: ☒

Approved by Verrold C. Hood R.E.H.S. Date 12/9/93

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

096

Raymond Contracting
11/23/2010
Repair/New System.
890-6009.

