LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

Division of Environmental Health
2200 St. Marys Ave Lincoln, NE 68502 (402) 471-8000

NON TRANSFERABLE

PERMIT
SEWAGE INSTALLATION

No. 90380061701

Issued 07/20/90
Expires 01/20/91

ESTABLISHMENT
MIKE REZAC
TYN R7E SEC 33
CLAYBURN ACRES LOT 1
6900 CARGER LANE

FEES: Permit 018754 $150.00

Total $150.00

Issued By COUNTY HEALTH

PERMITTEE
MIKE REZAC
1830 W BURNHAM
LINCOLN NE 68522

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

DATE	AMOUNT
7/20/90	PAID

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: 7-19-90

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 33 ;
   Block _____ : Lot 1 : Addition Clay Berlin Acres.
   Street Address 6900 Cargill Ln.

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒ Lagoon *

4. Distance to public sewer: > 300 ft.

Signature of Applicant (Owner or Lessee)

1830 West Burnham
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/19/90. Date Frwd. 7/20/90. ACTION: Approved ☒ Disapproved ☐ Signature: Gerald C. Wood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 7/20/90. Date Frwd. 7/20/90. ACTION: Approved ☐ Disapproved ☐ Signature: Walt Stuart

3. City or County Engineer: Date Rec'd. 7-20-90. Date Frwd. 7-20-90. ACTION: Approved ☒ Disapproved ☐ Signature: [signature]

REMARKS OR REASONS FOR DISAPPROVAL RURAL WATER

Site Visits:
Date: 10-12-90 by: rmm
Date: 11-9-90 by: rmm Wide seepage bed
Date: _____ by: _____

EXPERIMENTAL
INSTALLATION ~~FINAL~~ WRITTEN APPROVAL Lagoon *
Date: 10-12-90 By: Ron Legvold

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* Lagoon was abandoned & wide seepage bed installed instead.

FORM 23-43

Clyborn Acres 6900 Carpenter South 70th

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township _____; Range _____; Section & ¼ Section _____.
Property Dimensions: 346 ft. x 382 ft. Area: 3 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☑; Silty Clay Loam ☐; Sandy Loam ☐; Silt Loam ☐; Clay Loam ☐.
Dates of Tests: 7/16 to 7/18. Weather: Precip. 0 Temp. 90.

OWNER: Reza Const
Address: 1830 West Burnham

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Water Level (in.)	Time (Hr./Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36"	7/16	12:00	7/18	1:00PM	7/18	1:00	37	1:30	37⅛	30min	1/8	
2								33½		33½		0	
3								30		30¼		1/4	
4								28		28		0	
5								27		27⅛		1/8	
6								27½		27⅝		1/8	

Eugene Reza
Signature of Person Conducting Test

Address Box 77 Denton Ne. 68339 Phone 797-3555

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____


(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): _____
Date: _____

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

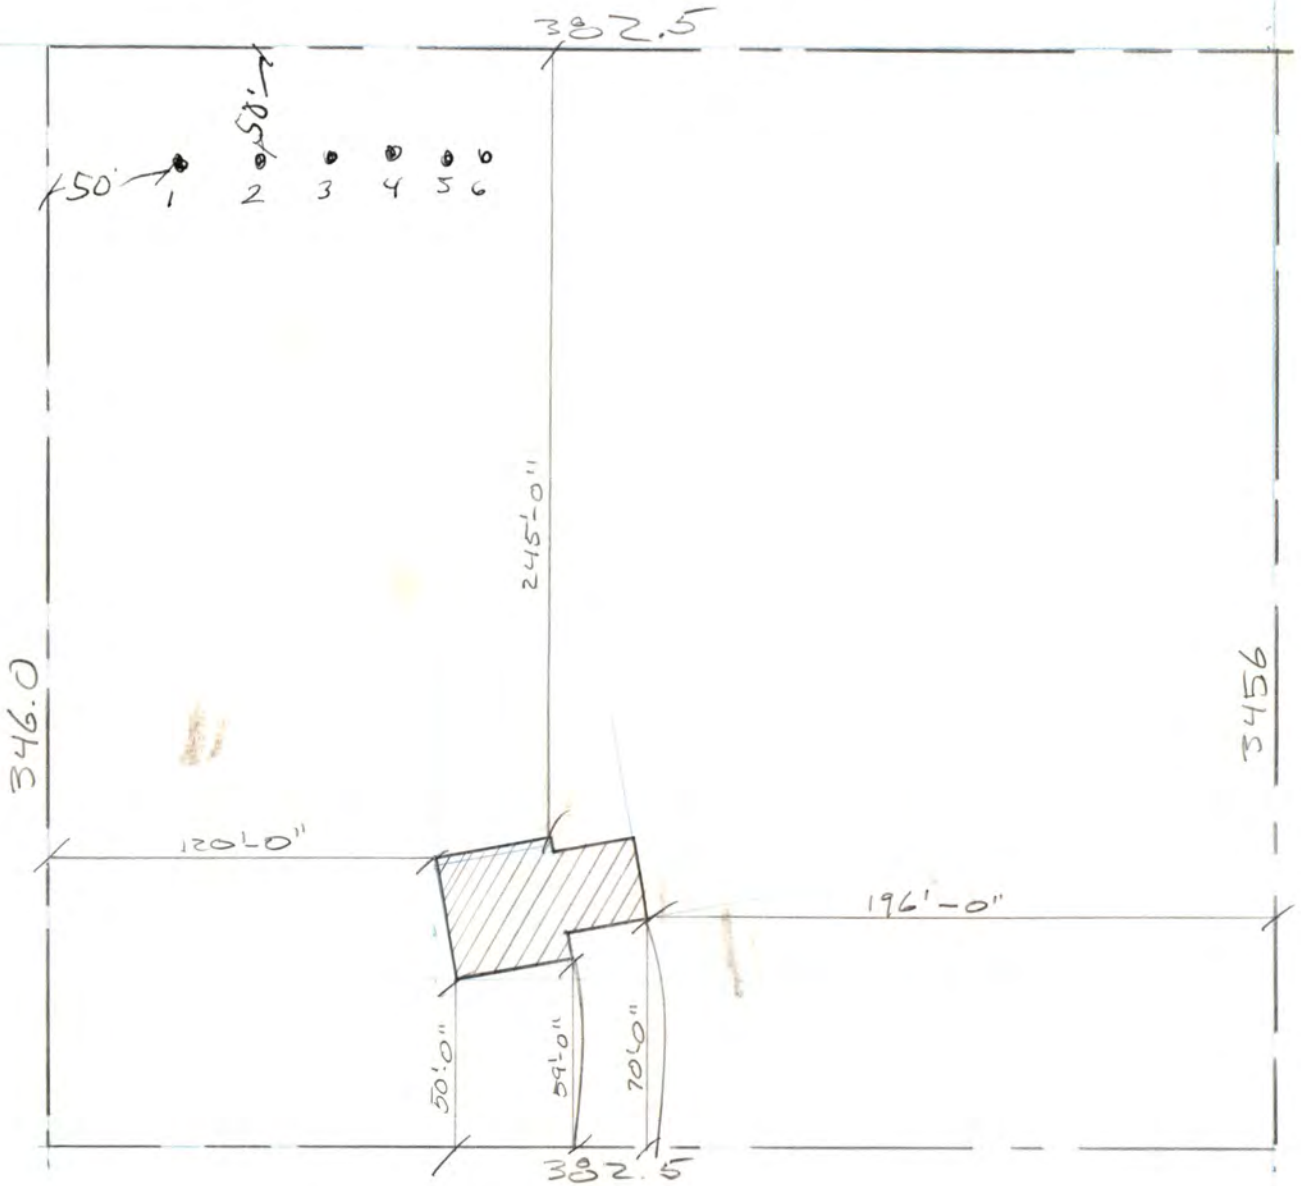

PLOT PLAN
LOT 1 CLYBERN ACRES

REZAC ITO

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor NA in., or below basement floor 12 in.
3. Distance between dwelling and septic tank 84 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 10+ ft.; Property Line 100+ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company American Concrete)
4. Manholes: Over Inlet; diam. 18 in.
Over Outlet; diam. 12 in.
Riser Above ☐ Below ☐ Grade NA in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 16" in.
8. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 100+ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 5 .
2. Factory Built: Yes ☒ No ☐
(Company American Concrete)
3. Distance from Septic Tank 4 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4" .
Material: fiberglass ☐ ;plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 2 ;Length of each line 100 , 100 , _____ , _____ , _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 10+ ft.
3. Trench dimensions: Width 2½ ft.;
Slope 4 in/100 ft.; Average Depth 36 in.
4. Filter Material: Gravel
Depth of Material 30 in.
5. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 50+ ft.

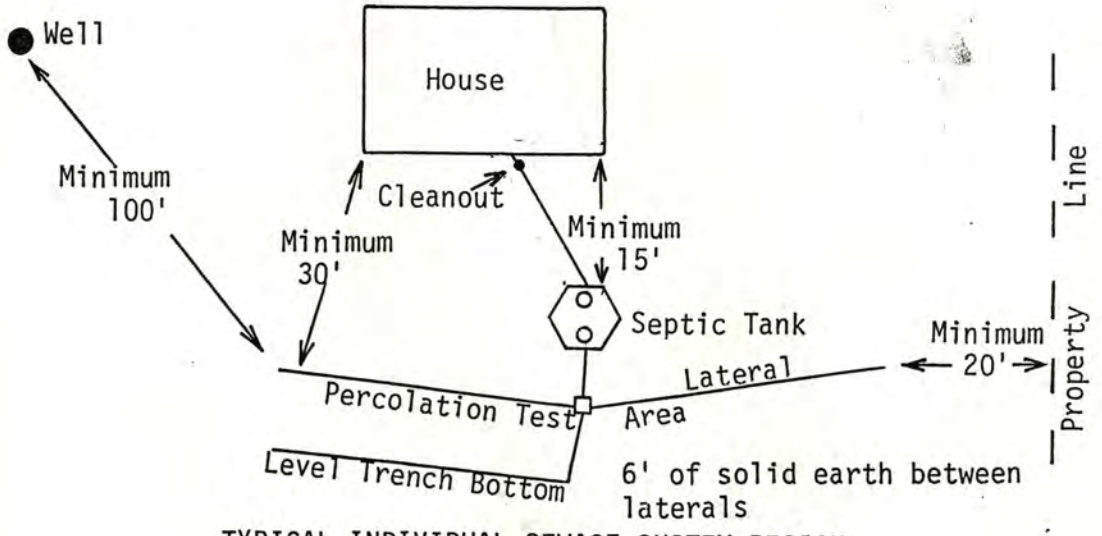

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 11-8-90 INSTALLER Vogt T&T Excavating

6940 Conger Lane

