LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2484-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

OCTOBER 27, 1987 — THIS PERMIT EXPIRES

LEE D. GARTNER — ISSUED TO

P.O. BOX 81-A — ADDRESS

WALTON, NE 68462

T9N; R8E; Sec 4; Lot 22 I.T. — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE ALTER, EXTEND OR REPAIR

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY: AG — DATE: 4-27-87 — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

$ 30.00

APR 2 4 1987

APR 2 4 1987

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 471-7800)

FILE NO. 2484-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: April 22, 1987

The undersigned hereby applies for a permit to ALTER ☒, EXTEND ☐, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 8E ; Section 4 ;
   Block ; Lot 22 Fr; Addition
   Street Address

2. Property Use: Residential ✓ ☒; Commercial ☐
   No. Bedrooms 3
   Describe
   Other Use ☐
   Describe

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: New septic tank & laterals

5. Work to be done by: Owner ☒ ; or Contractor ☐ , Larry Schwarzk
   Contractor's Name

6. Estimated cost of project:

a. Materials	$	
b. Labor	$	
c. Other	$	
TOTAL	$	2600 —

Lee D Lantis
Signature of Applicant (owner or lessee)

Box 81 A - Walton Nebraska
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd:
   Filing Fee: $ 30.00

2. Site Visits:
   Date: 4-22-87 by: rm
   Date: by:
   Date: by:

3. Date: Approved ☒ ; Disapproved ☐
   by: Jerrold C. Rose

4. INSTALLATION FINAL WRITTEN APPROVAL
   Date: 4-27-87 by: Ron Maynard

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

APR 24 1987

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. 2484-C


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Sch 40 ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank 50' ft. old line
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Pre Cast ; No. of compartments _____.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 12" in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Pre Cast ; Number - available outlets _____.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank 8 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or
Perforated Pipe 4 _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 3 ; Length of each line 80, 80, 80, _____, _____ ft.;
Total length of laterals 240 ft.;
Distance between lateral lines 10 ft.
3. Trench dimensions: Width 3 ft.;
Slope 5 in/100 ft.; Average Depth 30 in.
4. Filter Material: Road Gravel
Depth of Material _____ in.
5. Distances to:
Well or Suction Line 100'+ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line 60 ft.

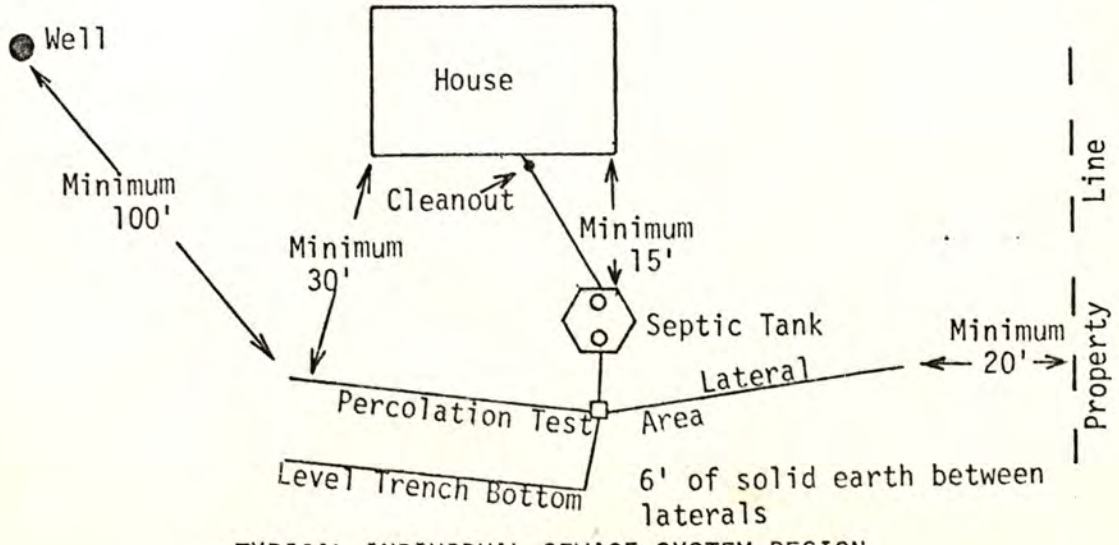


TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE April 22 - 87 INSTALLER Larry Schwoerk

Dr Lee Gartner

$\frac{1}{3}$ mi So. of Pioneers on 148th St

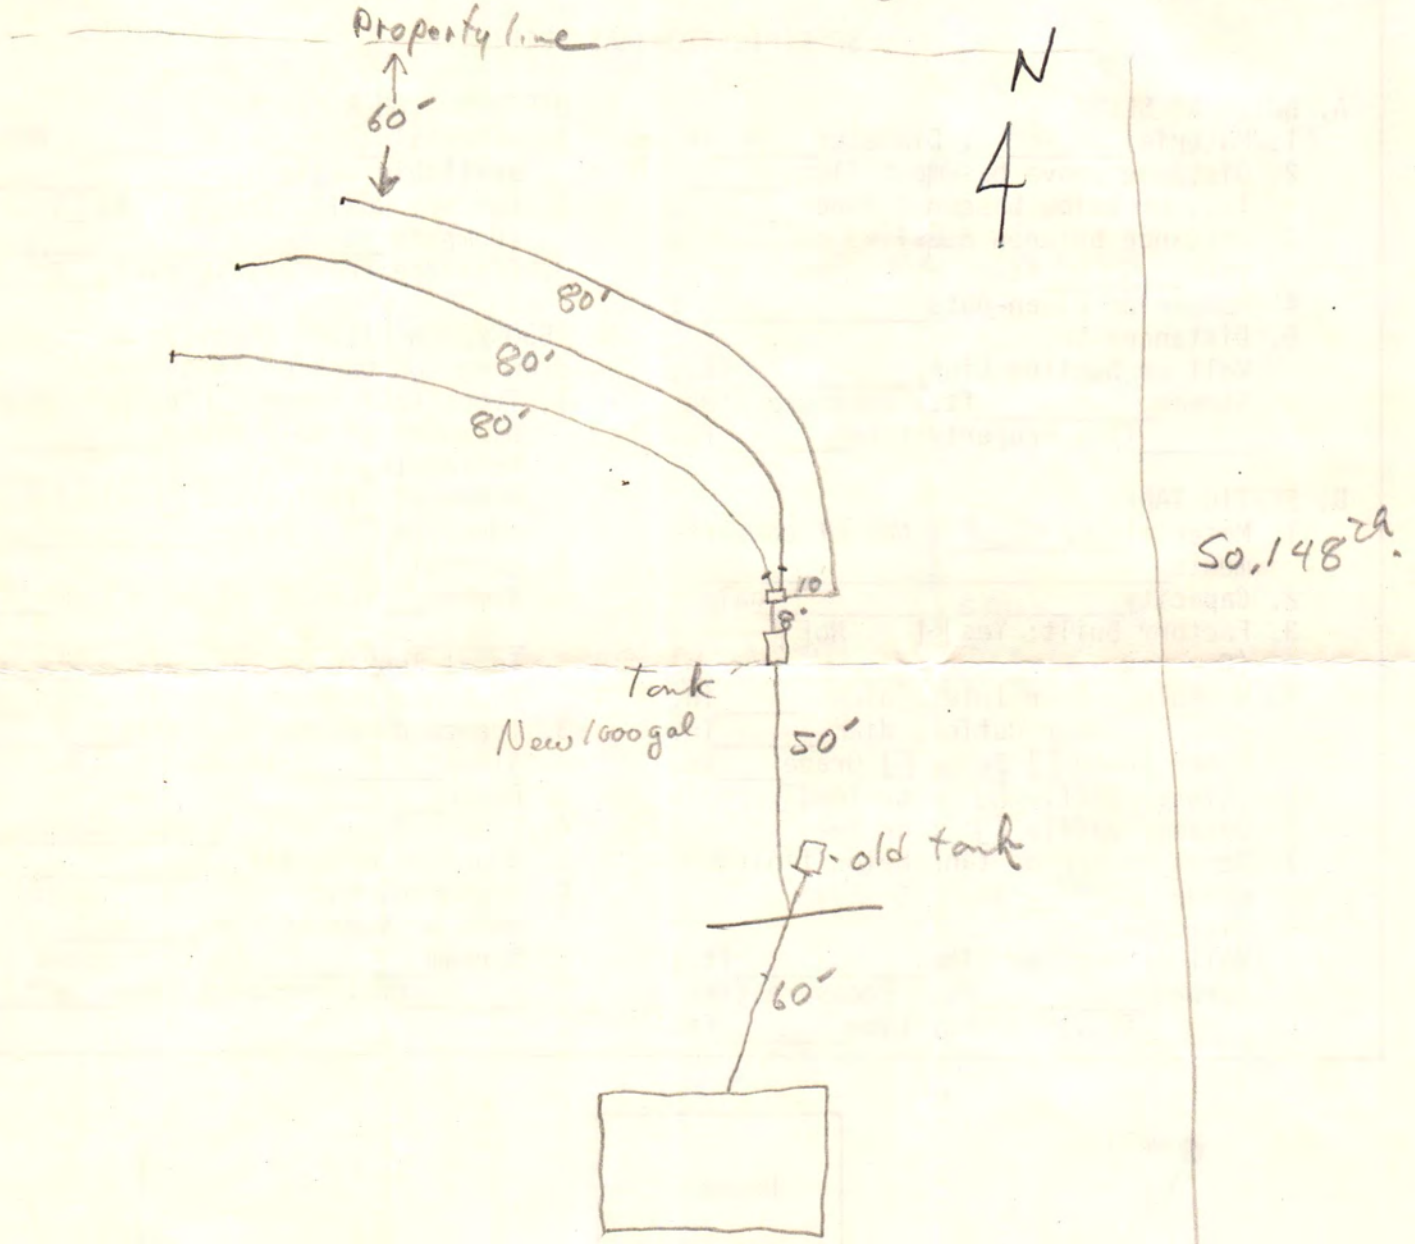

013

Lincoln-Lancaster County Health Department

2200 St. Mary's Avenue, Lincoln, Nebraska 68502 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☒ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☐ Evaluation of the Individual Water System ☒ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address 3601 So. 148th Walton, Ne.

Twp 9N Range 8E Section 4 1/4 SE 1/4 1/4 Block ___ Lot 22 Addition ___

Directions to Property ___

Location of Well ___ Tap Location: Inside ☐ Outside ☐

Location of Sewage System ___ Year Installed ___

	NAME	ADDRESS	PHONE
Present Owner:	Lee D. Gartner	9440 Princess Blvd. Lincoln, NE 68520	489-5813
Tenant/Buyer:	Patricia M. Cole	916 S. 326th. Eagle, Ne 68347	781-9350
Return to:	Crowne Closing Co	6940 O St. #312 Lincoln, NE 68510	464-1200

Signature of Applicant Patricia R Becker Address 6940 O St #312 Date 6/3/94
Crowne Closing Lincoln, NE 68510

HEALTH DEPARTMENT USE ONLY

Date Received 06/06/94 Received $150.00 ✓ Check ☑ 5178 Cash ☐

PRELIMINARY STATUS--By Jerrold Hood DATE: 6/7/94

RURAL WATER DISTRICT?

WATER SYSTEM:	Approved	Disapproved
Construction	☐	☐
Bacteria	☐ ____/ml	☐ ____/ml
Nitrate	☐ ____ppm	☐ ____ppm

SEWAGE SYSTEM
Approved ☐
Provisional ☒
Disapproved ☐

Additional Site Visits
Date ___/___/___ by ___
Date ___/___/___ by ___
Date ___/___/___ by ___

Comments: PROVISIONAL APPROVAL ON SEWAGE SYSTEM BECAUSE A PORTION OF IT (BUILDING SEWER) EXISTED PRIOR TO REGULATIONS. IF THE WELL UNDER THE WIND MILL IS NOT TO BE USED IT MUST BE PROPERLY ABANDONED. See Attached Letter ☐

FINAL STATUS RURAL WATER DISTRICT?

WATER SYSTEM: Approved: ☐ **SEWAGE DISPOSAL SYSTEM** Approved: ☐ Provisional Approval: ☒

Approved by Jerrold C. Hood R.E.H.S. Date 6/7/94

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.
