LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 1865-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

OCTOBER 20, 1982 — THIS PERMIT EXPIRES

WENDELL JOHNSON BOX 195 WAVERLY NE — ISSUED TO / ADDRESS

T12N, R7E, SECTION W-½-9 SE

LEGAL DESCRIPTION

REMARKS: NONTRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. _____

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 60.00

FILE NO. 1865-C

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 12 N ; Range 7-E ; Section W-½-SE¼-9;
   Block _____ : Lot _____ : Addition _____
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: — ft.

Wendell Johnson
Signature of Applicant (Owner or Lessee)

Box 195 Waverly NE
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 4/20/82. Date Frwd. 4/20/82. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 4/21/82. Date Frwd. 4/21/82. ACTION: Approved ☒ Disapproved ☐ Signature: Paul Bauma
3. City or County Engineer: Date Rec'd. 4/21/82. Date Frwd. 4/21/82. ACTION: Approved ☒ Disapproved ☐ Signature: Larry V. Worrell

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 4/23/81 by: L.C.H.
Date: 8-4-82 by: rm hydrant not moved.
Date: 3-18-83 by: rm hydrant disconnected

INSTALLATION FINAL WRITTEN APPROVAL
Date: 3-18-83 By: Ron Maynard

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

Water Hydrant has to be moved.

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 12-N ; Range 7-E ; Section & ¼ Section W-½-9.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☒ .
Dates of Tests: 4-16-82 to 4-19-82. Weather: Precip. _____ Temp. _____.

OWNER: _____

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36	4-16	6.0	4-19	6.0	4-19	5:30	3"	6.00	3 1/8	30	7/8	
2	"	"	"	"	"	"	"	"	"	"	"	"	
3	"	"	"	"	"	"	"	"	"	"	"	"	
4	"	"	"	"	"	"	"	"	"	"	"	"	
5	"	"	"	"	"	"	"	"	"	"	"	"	
6	"	"	"	"	"	"	"	"	"	"	"	"	

Kendall Johnson
Signature of Person Conducting Test

Address Box 195 Waverly NE Phone 786-3023

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Sharpsburg Silty Clay Loam
Date: April 20, 1982

Approved Percolation Rate (a)
A. 34 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO._____

Indicate on sketch if residence and well are exisiting or proposed.

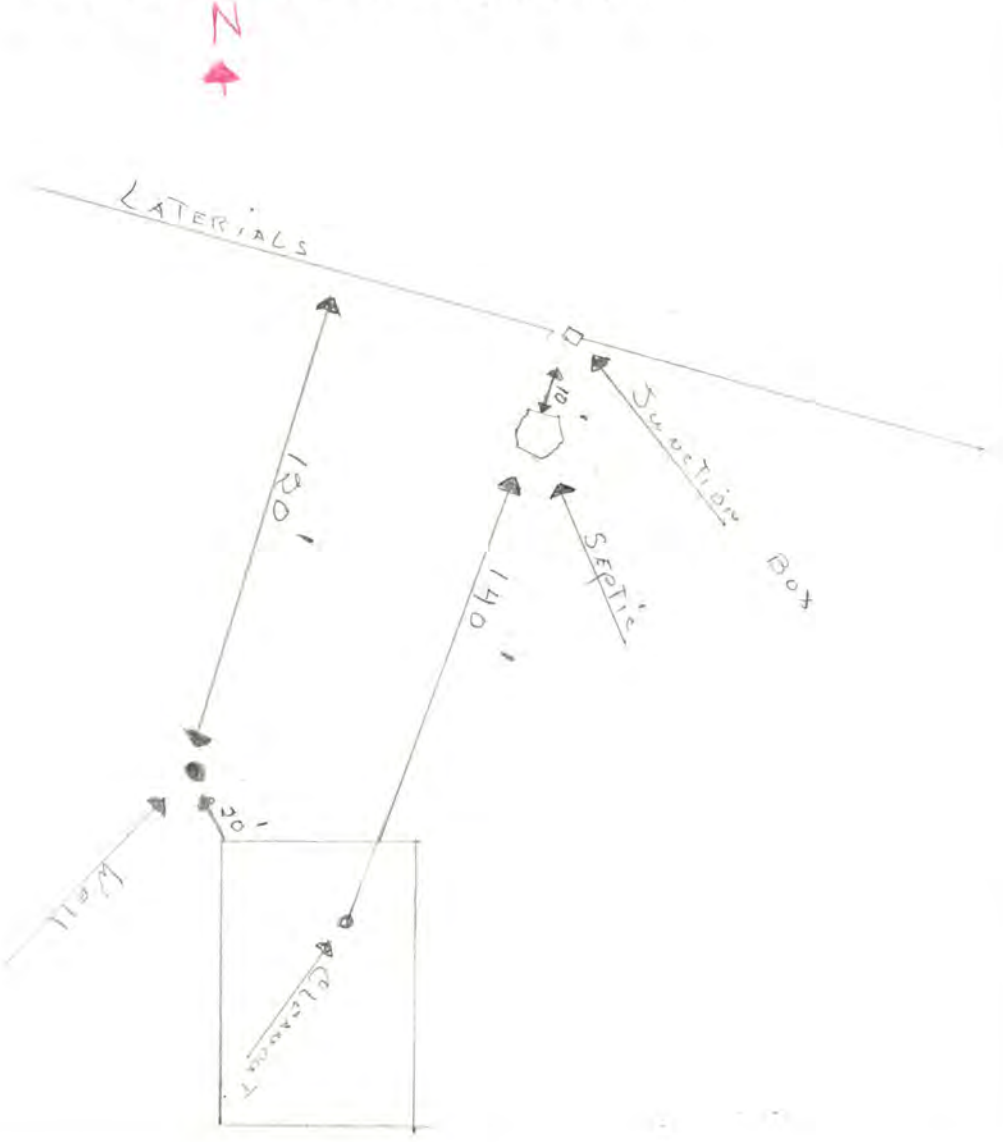

REVIEWING ACTION

Remarks :_____

Date: April 20, 1982

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed 198 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre Cast Step Co)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 6 in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 14" in.
8. Distances to:
Well or Suction Line 101 ft.; Stream — ft.; Pressure Line _____ ft.; ~~Property Line~~ County Rd 400 ft.

C. DISTRIBUTION BOX:
1. Material Concrete; Number - available outlets 5.
2. Factory Built: Yes ☒ No ☐
(Company Pre Cast Step Co)
3. Distance from Septic Tank 9½ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 20" or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____.
2. Lateral Lines:
Number 3 ; Length of each line 100, 100, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 11½ ft.
3. Trench dimensions: Width 4 ft.;
Slope 3" in/100 ft.; Average Depth 40 in.
4. Filter Material: Road Gravel
Depth of Material 22 in.
5. Distances to:
Well or Suction Line 120 ft.; Stream — ft.; Pressure Line _____ ft.; Property Line 410 ft. Road

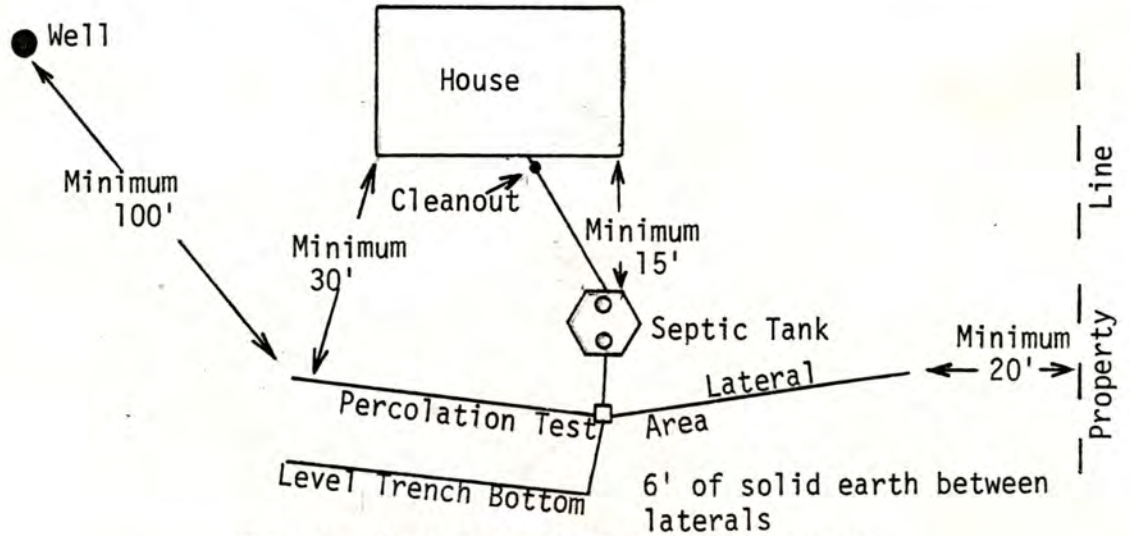

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM Old House

DATE _____ INSTALLER Johnson Wood Products



