Lincoln-Lancaster County Health Department
ENVIRONMENTAL PUBLIC HEALTH DIVISION

005176

3140 N STREET · LINCOLN, NE 68510-1514

(402) 441-8000

Permit: SEWAGE SYSTEM REPAIR
SEWAGE REPAIR

Permit # 04390078901

Issued 06/11/04
Expires 12/11/04
Revenue Code 3157

Establishment:
JOHN OSTERMAN
T12N R7E SEC 13
9200 ROCK CREEK RD-WAVERLY

FEES: $100.00

Permittee:
JOHN OSTERMAN
9200 ROCK CREEK RD
WAVERLY NE 68462

TOTAL: $100.00

Bruce D. Dart

Bruce D. Dart, Health Director

EPH COPY

#043900789

Application to Alter, Extend or Repair an Individual Sewage Disposal System

☐ Municipal Code 24.38 ☒ County Resolution Number 2832

The undersigned hereby applies for a permit to: ☐ **ALTER** ☒ **EXTEND** ☐ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 12N Range 7E Section 13 1/4 Section _____
   Block _____ Lot _____ Addition _____
   Parcel ID ____-____-_____-_____-_____ (i.e. 99-99-999-999-999)
   Street Address 9200 Rock Creek Rd. Waverly Ne 68462

2. **Property use:** ☒ residential ☐ commercial ☐ other use
   Number of bedrooms _____ Describe _____

3. **Type of Present Individual Disposal System** ☒ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** extend lateral field w/ 100' of Gravelless ADS BIODIFFUSER (3' wide Material)

5. **Work to be done by:** ☐ owner ☒ contractor's name Southwick Sewer & Drain

6. **Estimated project:**
   a. Repair, replace or minor extension with a cost less than $400 (no fee required).
   (b.) Total cost is greater than $400 (Return fee with this application)
   c. A "construction permit" is required if the use, operation, location, or type of the system is being change.

Print Name John Osterman Address 9200 Rock Ck Rd Phone 785-2324
Applicant Signature (owner or lessee) _____

Please include the permit fee ($100) with this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 6/11/04 REVIEW: ☒ Approved ☐ Disapproved By: Doug Svoboda

Site visits
Date ____/____/____ By _____
Date ____/____/____ By _____
Date ____/____/____ By _____

Installation final written approval
Date 6/21/04 By Doug Svoboda

Return application to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8022

Business Office Use Only
Received: Date: 06/11/04 Amount 100.00 Check No. 1027 Initials ns

White - Division Copy Pink - Business Office Revised 9/00

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System

As Built Plans & Specifications

Date 6-13-04

System Location (Indicate correct number and street)

Address 9200 Rock Creek Rd. (no rural route) City Waverly NE, Zip 68462

A. Building Sewer

1. Material: Sch 40 PVC
   Diameter: 4" in.
2. Distance above basement floor: 60 in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: 53 ft.
4. Number of clean-outs: 1
5. Distances to: well or suction line > 50 ft.
   stream > 50 ft.
   pressure line 1 ft.
   property line > 20 ft.

B. Septic Tank

1. Material: Concrete
   Number of compartments: 1
2. Capacity: 1,000 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter _____ in.
   Over outlet, diameter _____ in.
   Riser: ☐ above ☐ below grade _____ in.
5. Inlet: ☐ baffle ☐ tee
6. Outlet: ☐ baffle ☒ tee
7. Depth to top of tank, below unfinished grade: 14 in.
8. Distances to: Well or suction line > 50 ft.
   Stream > 50 ft.
   Pressure line _____ ft.
   Property line > 20 ft.

C. Distribution Box

1. Material: PVC
   Number available outlets: 3
2. Factory built: ☒ Yes ☐ No Hanscor
3. Distance from septic tank: 6 ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round: 16"
   or perforated pipe: _____
   Material: ☐ fiberglass ☒ plastic ☒ concrete
   ☐ other _____
2. Lateral lines: Number 2
   Length of each line: 100 ½ Stone ft. _____ ft.
   84 Tile ft. Total ft., _____ ft.
3. Trench dimensions: Width 4 ft.
   Slope 4 in/100 ft.
   Average depth 36 in
4. Filter material: Gravel & Crushed Stone
   Depth of material 16 in.
5. Distances to: Well or suction line > 100 ft.
   Stream > 50 ft.
   Pressure line _____ ft.
   Property line > 20 ft.

Indicate North with Arrow


Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

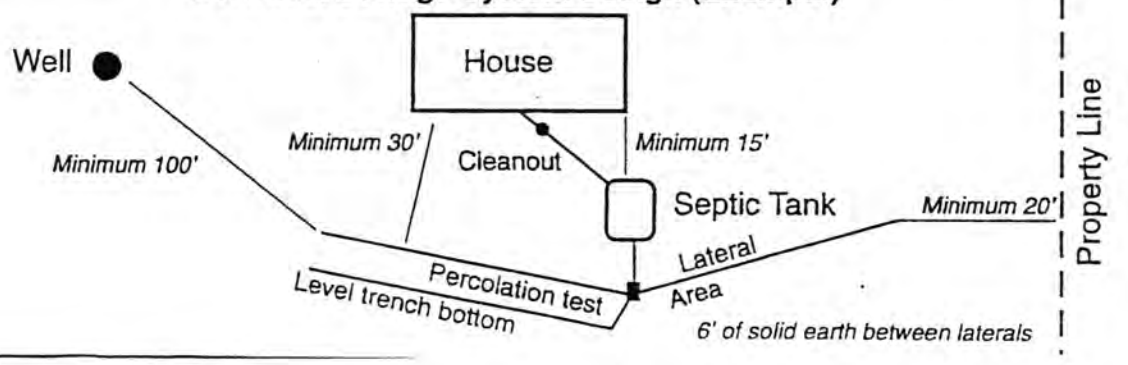

FORM 23-103 10-96

As Built Drawing

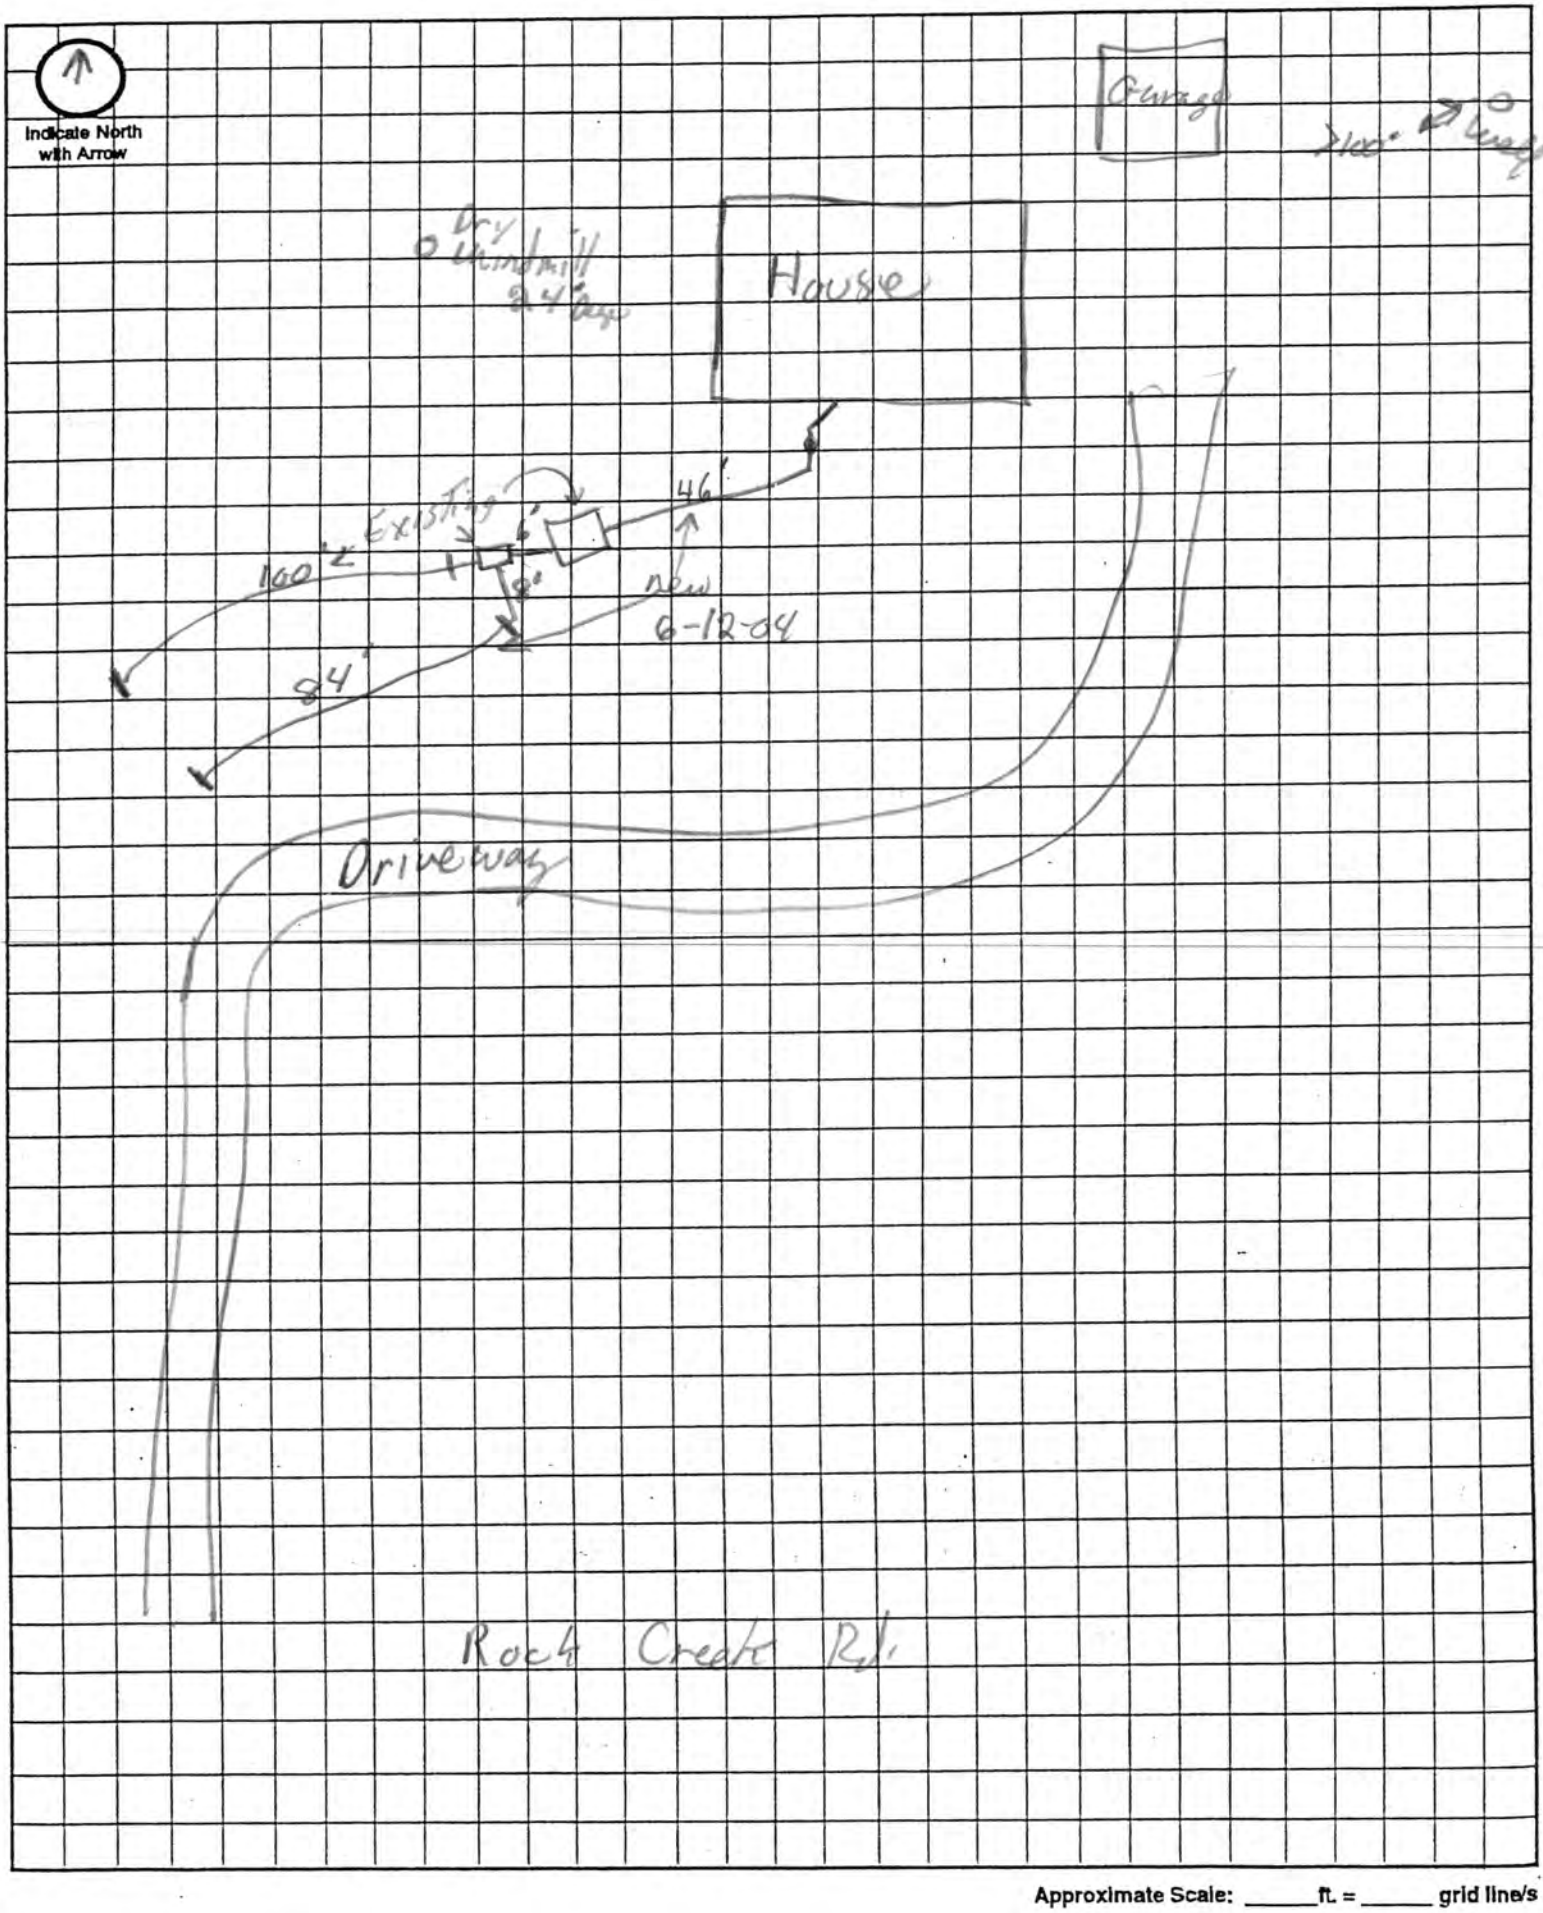

Approximate Scale: _____ ft. = _____ grid line/s
