LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2849-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

6 MONTHS — THIS PERMIT EXPIRES

MICHAEL L. ISAACSON — ISSUED TO

5613 FALCON CIRCLE, LINCOLN, NE 68516 — ADDRESS

T9N; R8E; Sec. 30 — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE NEW CONSTRUCTION

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY: MG — DATE: 6-5-99 — AMOUNT:

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. ———

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2849-C

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 8E ; Section 30 ; SEE ATTACHED
   Block _____ : Lot _____ : Addition _____
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☐

4. Distance to public sewer: _____ ft. WILL INSTALL WHATEVER PERC TEST INDICATES

Michael L. Isaacson
Signature of Applicant (Owner or Lessee)

5613 Falcon Circle Lincoln, Ne. 68516
Address
474-1400 Work

(Do not write below this double line)

1. Health Department: Date Rec'd. 6/1/89 . Date Frwd. 6/1/89 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 6-1-89 . Date Frwd. 6-1-89 . ACTION: Approved ☒ Disapproved ☐ Signature: Paul Boeshart

3. City or County Engineer: Date Rec'd. 6/1/89 . Date Frwd. 6/1/89 . ACTION: Approved ☒ Disapproved ☐ Signature: Lanyl Worrell

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 8-9-89 by: mm
Date: 8-10-89 by: mm
Date: 8-11-89 by: mm

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 8-21-89 By: Ron Mazgent

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 2849-C

PROPERTY WHERE SOIL TESTED:

Location: Township 9N ; Range 8E ; Section & ¼ Section 30.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: _____ to _____. Weather: Precip. _____ Temp. _____.

OWNER: Mike Issacson

3 Bdrm

Address: Lincoln, Ne

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36						2:45	20⅛	3:15	21	30	⅞	.8750
2								21¾		22¾		1	1.0
3								24		24¾		¾	.75
4								25⅛		26¼		1⅛	1.125
5								21½		22⅝		1⅛	1.125
6								21¾		22¾		1⅛	1.125
											.6	6	
												1.0	

Sum of Percolation Rates: 6
Average of Rates: 1
Mean of Rates: _____

Don Magee
Signature of Person Conducting Test

Address RFD 8 Lincoln Phone _____

(Do not write below this line) 1848 4 30 min/in 250 - 36

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): _____
Date: _____

Approved Percolation Rate (a)
A. 30 min/in min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 8-10-89

FILE NO. 2849-C

Mike Issacson


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material SCH 40 PVC; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 10 in.
3. Distance between dwelling and septic tank 75 ft.
4. Number of clean-outs 1.
5. Distances to:
Well or Suction Line N/A ft.; Stream N/A ft.; Pressure Line >100 ft.; Property Line 250 ft.

B. SEPTIC TANK:
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre Cast)
4. Manholes: Over Inlet; diam. 10 in.
Over Outlet; diam. 12 in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 7-12 in.
8. Distances to:
Well or Suction Line N/A ft.; Stream N/A ft.; Pressure Line >100 ft.; Property Line 250 ft.


C. DISTRIBUTION BOX:
1. Material Plastic; Number - available outlets 7.
2. Factory Built: Yes ☒ No ☐
(Company ____)
3. Distance from Septic Tank 75 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round ____ or Perforated Pipe 4".
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other ____.
2. Lateral Lines:
Number 3 ; Length of each line 80, 80, 90, ____, ____ ft.;
Total length of laterals 250 ft.;
Distance between lateral lines 10 ft.
3. Trench dimensions: Width 3-3½ ft.;
Slope 4 in/100 ft.; Average Depth 36 in.
4. Filter Material: Road Gravel
Depth of Material 14 in.
5. Distances to:
Well or Suction Line N/A ft.;
Stream N/A ft.; Pressure Line >100 ft.; Property Line 250 ft.

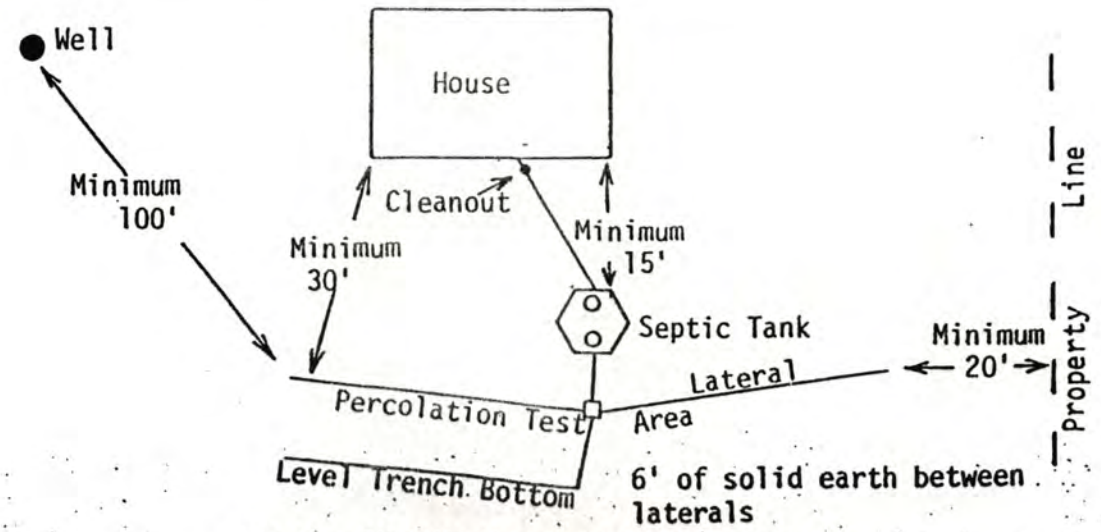

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

Southwick
Sewer &
Drain

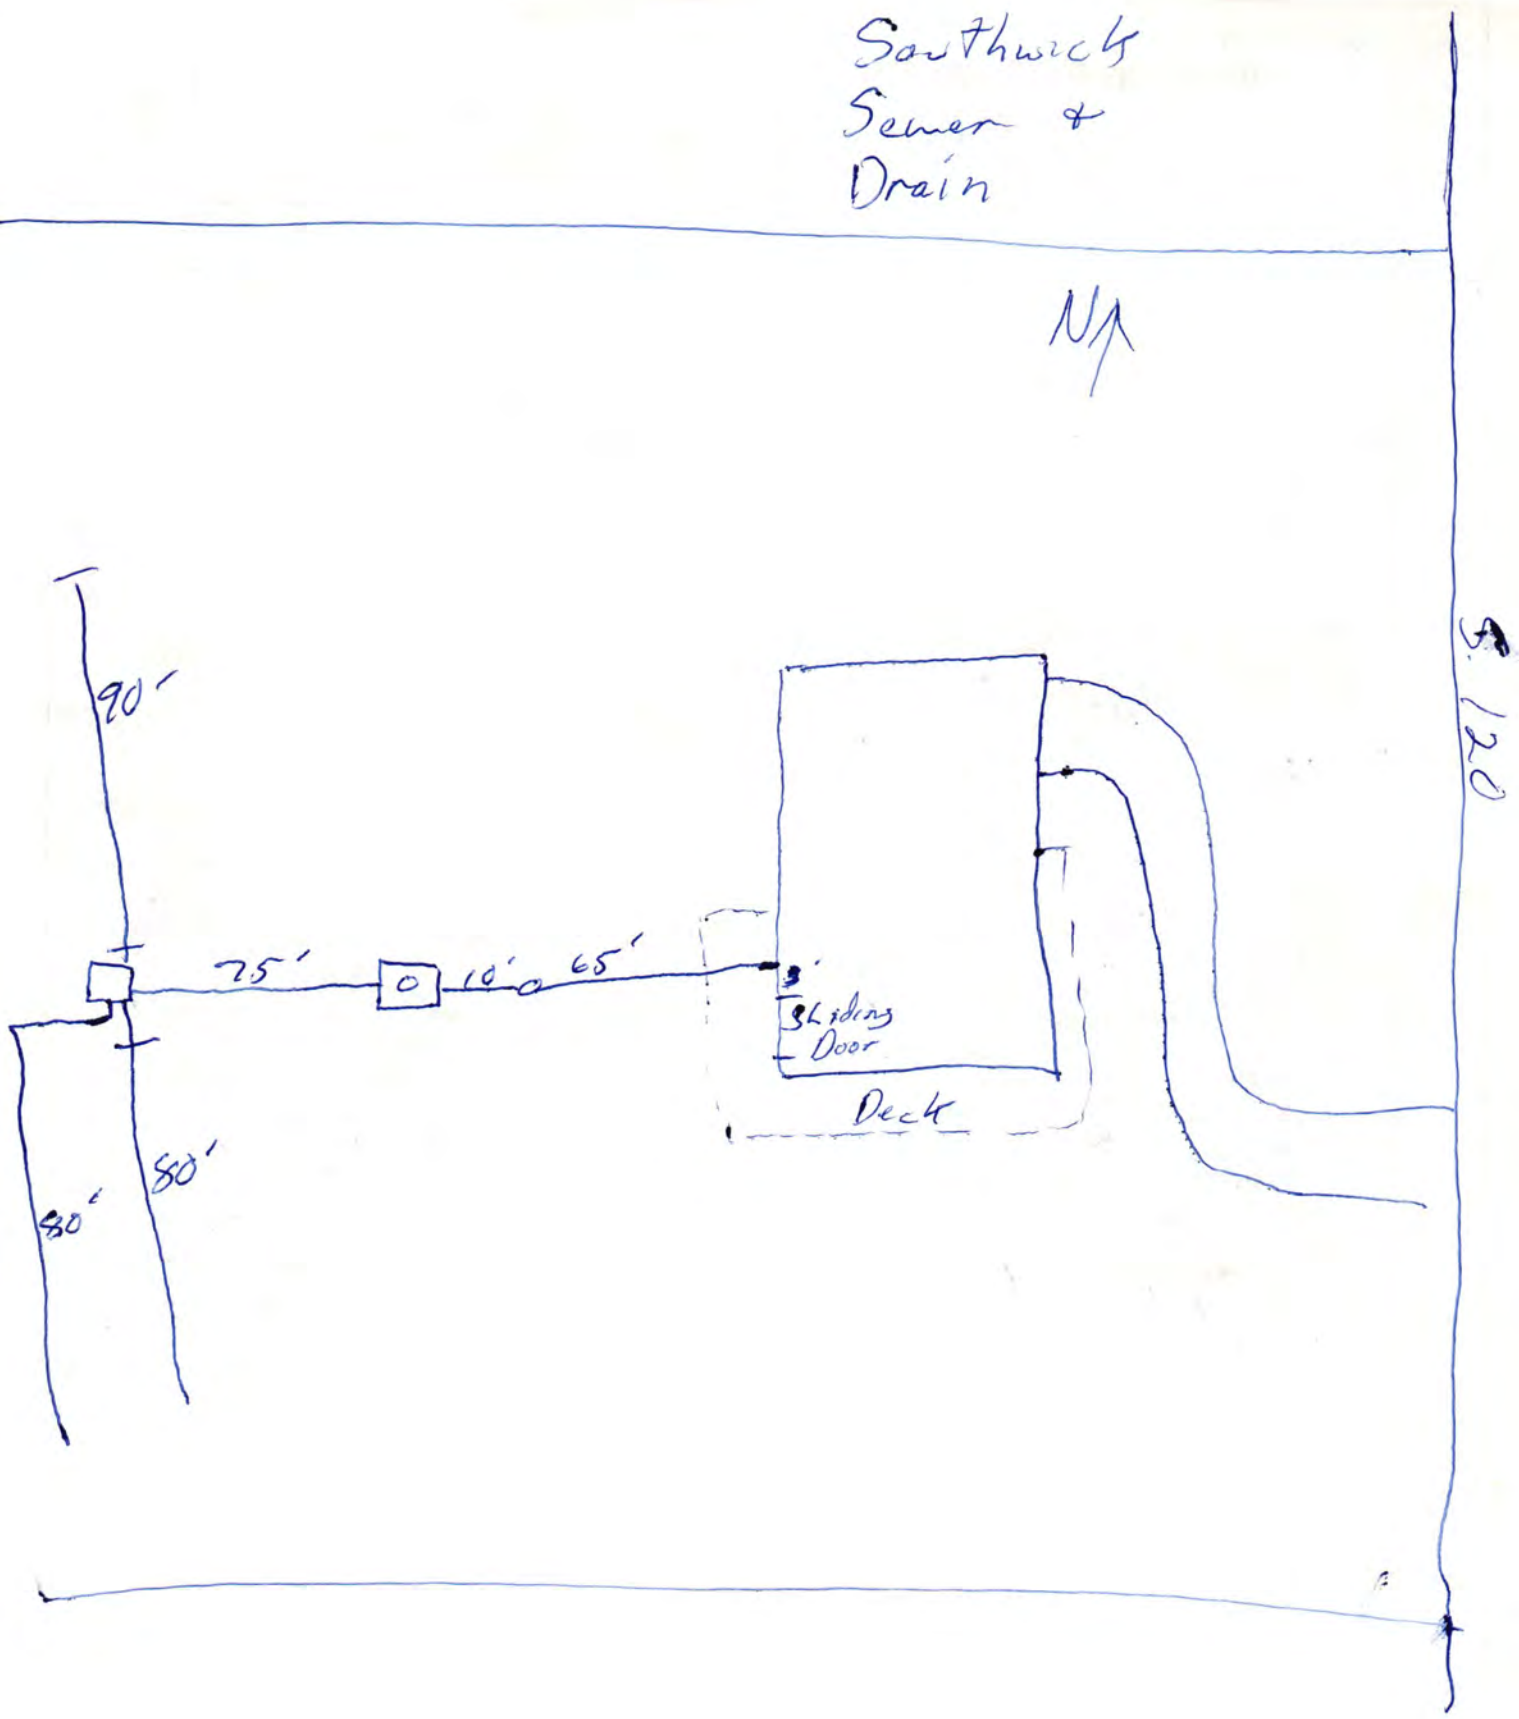

Part of Lot 8, Irregular Tracts of the Northeast 1/4 of Section 30, Township 9 North, Range 8 East of the 6th P.M., Lancaster County, Nebraska; more particularly described as follows:

Commencing at the East One Quarter corner of Section 30, T9N, R8E, of the 6th P.M., thence North along the East line of said North-East One Quarter of Section 30, a distance of Three Hundred Fifty (350) Feet, thence West parallel to the South line of said North-East One Quarter of Section 30 a distance of Thirty-Three (33) Feet to the point of beginning, thence West parallel to the South line of said North-East One Quarter of Section 30 a distance of Six Hundred Fifty (650) Feet, thence North parallel to the East line of said North-East One Quarter of Section 30 a distance of Three Hundred Fifty (350) Feet, thence East parallel to the South line of said North-East One Quarter of Section 30 a distance of Six Hundred Fifty (650) Feet, thence South parallel to the East line of said North-East One Quarter of Section 30 a distance of Three Hundred Fifty (350) Feet to the point of Beginning.
