LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1602-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

April 1, 1980 — THIS PERMIT EXPIRES

Richard A. Luecker — ISSUED TO

15630 Northwest 30th, Raymond, NE 68428 — ADDRESS

T12N, R6E, Section 32, Block 1, Lot 12, Addition Willard Estates — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 60.00

FILE NO. 1602-C

DATE: SEPTEMBER 28, 1979

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. ~~33~~ 12 ; Range 6 ; Section ~~33~~ 32 ;
   Block 1 : Lot 2 : Addition WILLARD ESTATES
   Street Address 15630 NW 30TH RAYMOND, NE 68428

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe BRICK RANCH

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Mrs. Richard A. Luecker
Signature of Applicant (Owner or Lessee)

15630 NW. 30th
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 10/1/79. Date Frwd. 10/1/79. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 9-28-79. Date Frwd. 9-28-79. ACTION: Approved ☒ Disapproved ☐ Signature: Sally S. Grant

3. City or County Engineer: Date Rec'd. 10-1-79. Date Frwd. 10-1-79. ACTION: ~~Approved~~ ☑ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: Feb. by: MM
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION ~~FINAL~~ Provisional* WRITTEN APPROVAL
Date: Feb. By: Ron Norgaard

* An experimental system

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 2-13-79

FILE NO. 1602-C


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank 70 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line ~~78~~ 55 ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line 175 ft.

B. SEPTIC TANK:
1. Material CONCRETE No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company PRECAST STEP)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 10 in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 30 in.
8. Distances to:
Well or Suction Line 78 ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line 175 ft.

C. DISTRIBUTION BOX:
1. Material CONCRETE; Number - available outlets 5.
2. Factory Built: Yes ☒ No ☐
(Company PRECAST STEP)
3. Distance from Septic Tank 14 ft.


D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or
Perforated Pipe 4".
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 2 ; Length of each line 100, 100, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 12 ft.
3. Trench dimensions: Width 8 ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: ROAD GRAVEL + SAND FILL
Depth of Material 24 in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

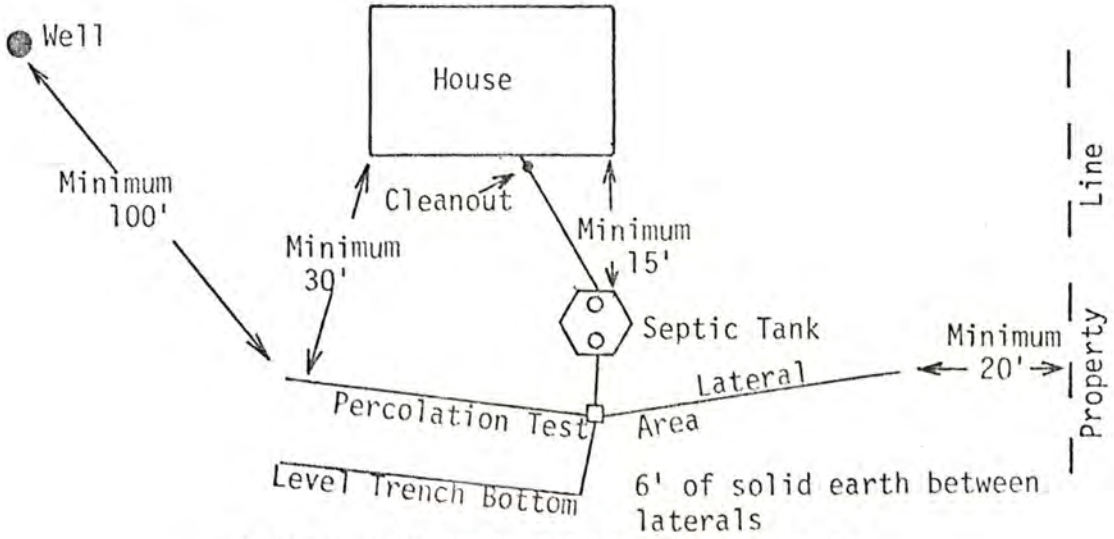

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 2-13-79 INSTALLER BRAD SOUTHWICK
792-2462

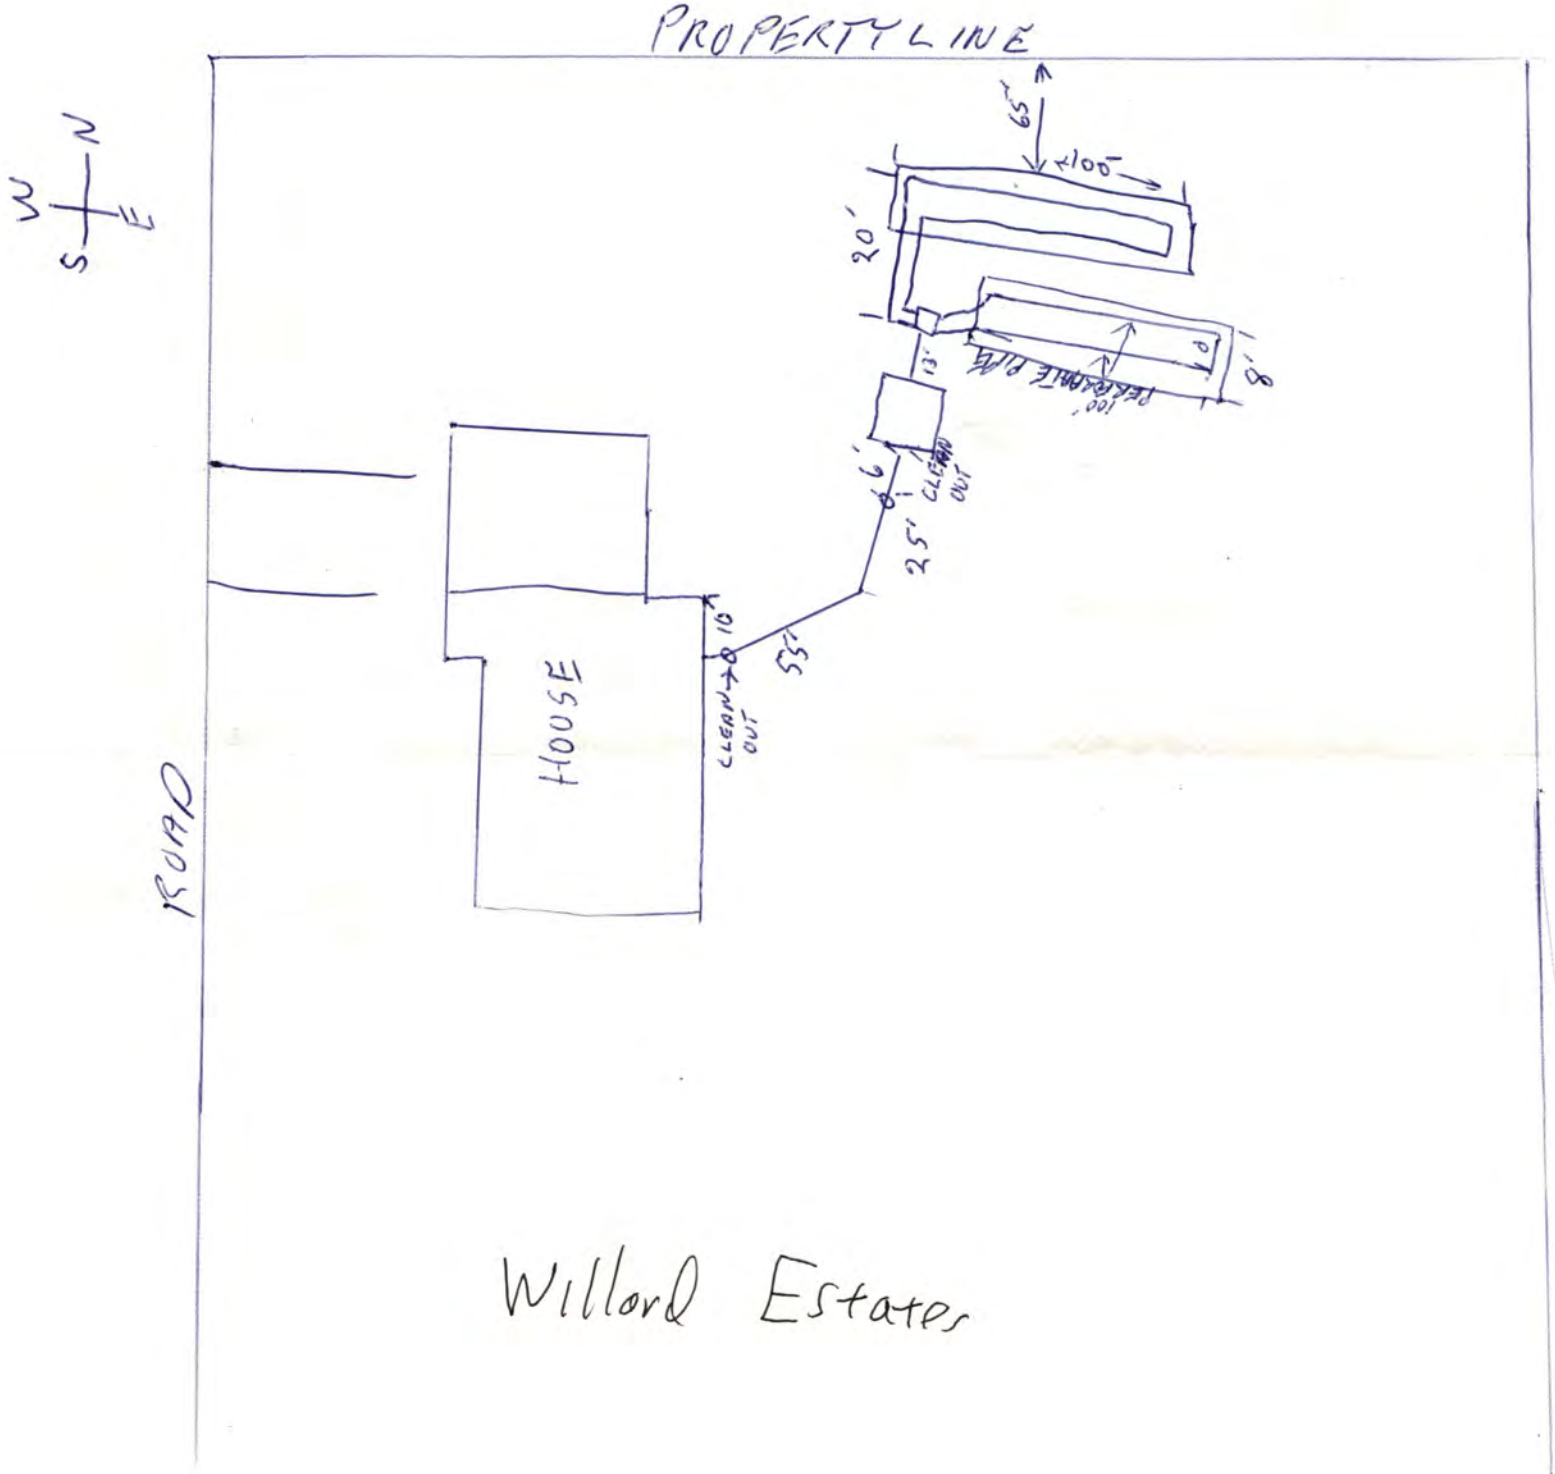

Willard Estates

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 St. Marys Avenue Phone (402) 474-1541 Lincoln, Nebraska 68502

REAL ESTATE TRANSFER

This form must be completed and returned to request a real estate transfer inspection.
MAKE CHECKS PAYABLE TO: *Lincoln-Lancaster County Health Department.*

☒ *Evaluation of the Individual Water System* Date: January 7, 1980
☐ *Evaluation of the Sewage Disposal System* ☒ *Enclosed is $45.00*

Legal description of property: TWP. 12 ; RANGE 6 ; SECTION 32
BLOCK 1 ; LOT 2 ; ADDITION Willard Estates
Street Address 15630 NW 30th Raymond, Ne
Directions to Property Go North on 14th St. to Raymond Rd. Turn West & go 3 miles. Turn into Willard Estates on the right side of road, and follow till you come to a field and can't go any further. We set right there on the east side of road.
Location of Well ~~North of the Garage~~ Front yard So of drive. *Tap Location:* *Inside* ☐ *Outside* ☐
Location of Sewage System NE of the well, & ~~house.~~ *Year Installed* 1979

	NAME	ADDRESS	PHONE
Present Owner:	Richard & Carol Luecker	15630 NW 30th Raymond, ne	783-3841
Tenant/Buyer:			
Return To:	[illegible]	[illegible]	[illegible]

NOTE: *Allow two weeks for processing. Incomplete information will delay processing.*

Signature of Applicant Carol Luecker *Address* 15630 NW 30th Raymond Ne 68428

HEALTH DEPARTMENT USE ONLY

Date Received 1/10/80 *Received $45.00* *Check* ☒ *Cash* ☐

PRELIMINARY STATUS--DATE 1-23-80

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM:		SITE VISIT:
Construction	☒	☐	Approved:	☐	Date 1/23/80 by DS
Bacteria	☒	☐	Provisional:	☒	Date 1/23/80 by D.S
Nitrate	☒	☐	Disapproved:	☐	Date 1/23/80 by D.S.

Comments: *This is an experimental sewage disposal system.

See Attached Letter ☐

FINAL STATUS

WATER SYSTEM:
Approved: ☒

SEWAGE DISPOSAL SYSTEM:
Approved: ☐ *Provisionsal Approval: ☒

APPROVED BY Doug Smith DATE 1/28/80

FN 20215-1079R
