FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1107-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 6-27-77

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 12N ; Range 6E ; Section SE¼ 32
Block 3 ; Lot 6 ; Addition WILLARD ESTATES
Street Address _____

2. Property Use: Residential _____ ☒ ; Commercial _____ ☐
No. of Bedrooms 3 . Describe: _____
Other Use _____ ☐
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: NA – ft.

Wesley Hoyenga

Richard Anderson
Signature of Applicant (Owner or Lessee)

1520 Pioneer Blvd.
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 7/15/77 . Date Frwd. 7/15/77 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: Date Rec'd. 7-15-77 Date Frwd. 7-15-77 . ACTION: Approved ☒ Disapproved ☐ Signature: Donald Dunn

3. City or County Engineer : Date Rec'd. 7/15/77 . Date Frwd. 7/15/77 . ACTION: Approved ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL In Raymond Jurisdiction

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1107-C

DATE: 6-27-77

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 12 N ; Range 6 E ; Section SE ¼ 32 ; Block 3 ; Lot 6 ; Addition Willard Estates .
   Street Address _____.

2. Property Use: Residential _____ ☒; Commercial _____ ☐
   No. of Bedrooms 3
   Describe: _____
   Other Use _____
   Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Richard Anderson
Signature of Applicant (owner or lessee)

1520 Pioneer Blvd. Lincoln 68502
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd; _____
   Filing Fee: $ 30.00

2. Site Visits:
   Date: 9-20-77 by: jw
   Date: _____ by: _____
   Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐ 7/15/77
   by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
   Date: 9-20-77 by: James Wewerka

FORM HD- 43(73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 475-6221)

FILE NO. 1107-C

PROPERTY WHERE SOIL TESTED:
Location: Township 12N ; Range 6E
Section & ¼ Sect. SE¼ 32
Property Dimensions: 238 ft. x 440 ft.
Area: _____ acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ☐; Silty Clay Loam ☐; Sandy Loam ☐
Silty Loam ☐; Clay Loam ☐; Sandy Clay ☐

Owner: Richard Anderson
Address 1520 Pioneer Blvd. Lincoln Nb

Dates of Tests: 6-6-77 to 6-7-77. Weather: Precip. dry Temp. 85°

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	32	6-6	9 AM	6-7	8:00	6-7	11:30	8	12:00	7⅞	30	⅛	
2	32						11:30	8	12:00	6⅜	30	1⅛	
3	32						11:40	6	12:10	5⅛	30	¾	
4	30						11:40	6	12:10	5⅛	30	⅝	
5	32						11:45	6	12:15	5¼	30	¾	
6	32						11:45	6	12:15	5	30	1	
							12:00	6	12:30	5½	30	½	

Dominico - Pottyes Plbg Co.
Signature of Person Conducting Test

Address 1520 Pioneer Blvd
Phone: 423-7021

Sum of Percolation Rates _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

REMARKS: Sharpsburg Silty Clay Loam. C.C.P.S.

DATE: July 11, 1977

Approved Percolation Rate(s)
A. 32 min./inch
B. _____ min./inch
C. _____ min./inch

Gerrold C. Hoad
Signature of Reviewing Official

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1107-C

SPECIFICATIONS

DATE: 6-27-77


A. BUILDING SEWER:
1. Material Cast Iron; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor 10 in.
3. Distance between dwelling and septic tank 40 ft.
4. Number of clean-outs -0-.
5. Distances To:
Well or Suction Line 110 ft.;
Stream — ft.; Pressure Line 40 ft.;
Property Line 70 ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material fiberglass No. of compartments one
2. Capacity 1000 gals.; Liquid depth ___ in.
3. Factory Built: Yes ☒ (Company Calvary)
No ☐
4. Manholes: Over Inlet; diam. ___ in.
Over Outlet; diam. ___ in.
Below Grade ___ in.
5. Inlet: Baffle ☐; or Tee ☒
6. Outlet: Baffle ☐; or Tee ☒
Depth of outlet below inlet 1 in.
7. Depth of top of tank below finished grade ___ in.
8. Distances To:
Well or Suction Line ___ ft.;
Stream ___ ft.; Pressure Line ___ ft.;
Property Line ___ ft.


C. DISTRIBUTION BOX
1. Material fiberglass; No. available outlets 6.
2. Factory Built: Yes ☒, (Company CALVARY) No ☐
3. Dimension: Length ___ in.; Width ___ in. Depth ___ in.
4. Distance from Septic Tank 10 ft.
5. Serial Distribution: Yes ☐, No ☐
(If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: 4" round perf. plastic pipe
2. Lateral Lines: Depth below grade 36 in.
Number 3; Length of each line ___ ft
Total length of Laterals 258 ft.;
Slope ___ in/100 ft. Diameter of pipe ___ in.; Shape ___
Material: concrete ☐; fiber asbestos ☐; clay ☐; other ___
Distance between lateral lines ___ ft.
3. Trench Dimensions: Depth ___ in.; Width 36 in.
4. Filter Material: ___.
Depth of material from trench bottom ___ in.
5. Distances To:
Well or Suction Line ___ ft.;
Stream ___ ft.; Pressure Line ___ ft.
Property Line ___ ft.
6. Percolation Rate: ___ minutes/inch

TYPICAL SKETCHES

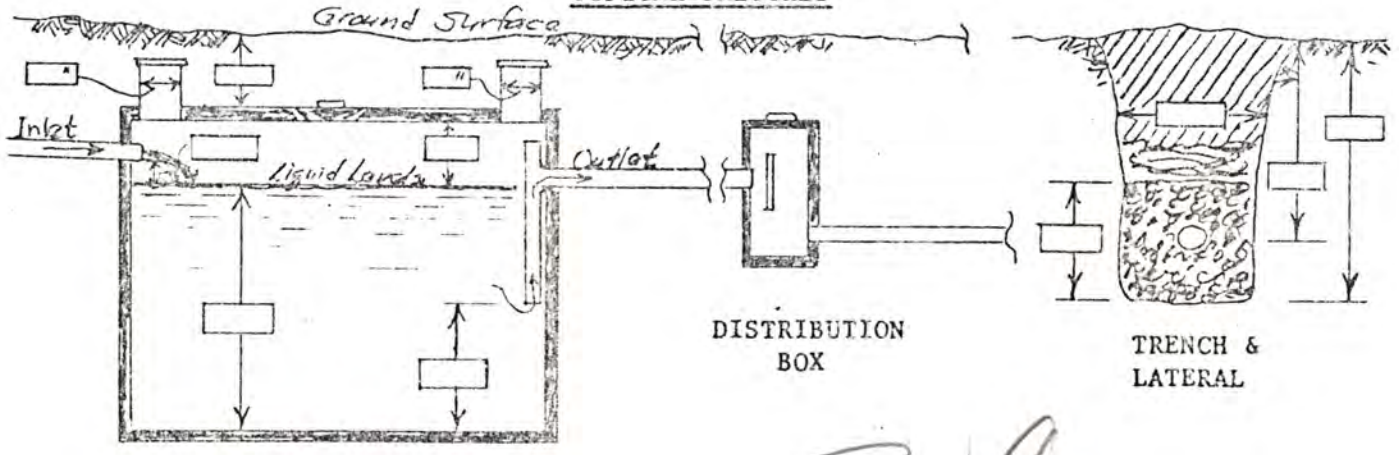

Richard Anderson
Signature of Applicant

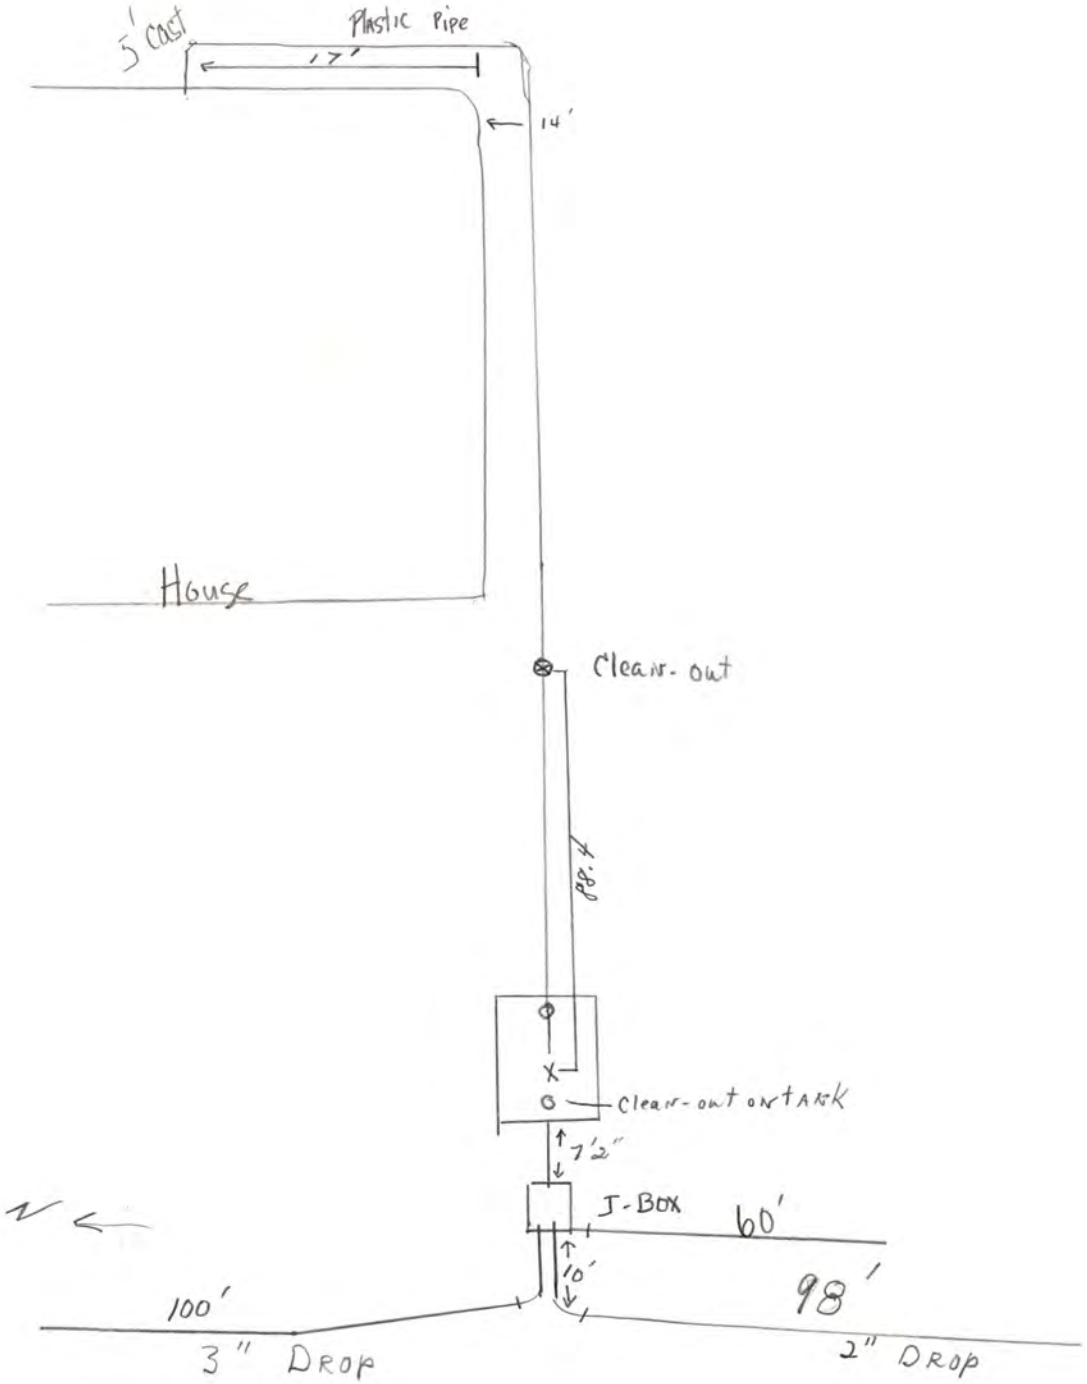


Richard Anderson / Raymond Road

Lot 6, BK 3 Willard Estates a sub of part of the SE. ¼ of sec. 32, T12N, R6E of the 6th p.m. Lancaster Co.

WILLARD ESTATES

THREE NORTHWEST OF THE DIAMOND ROAD

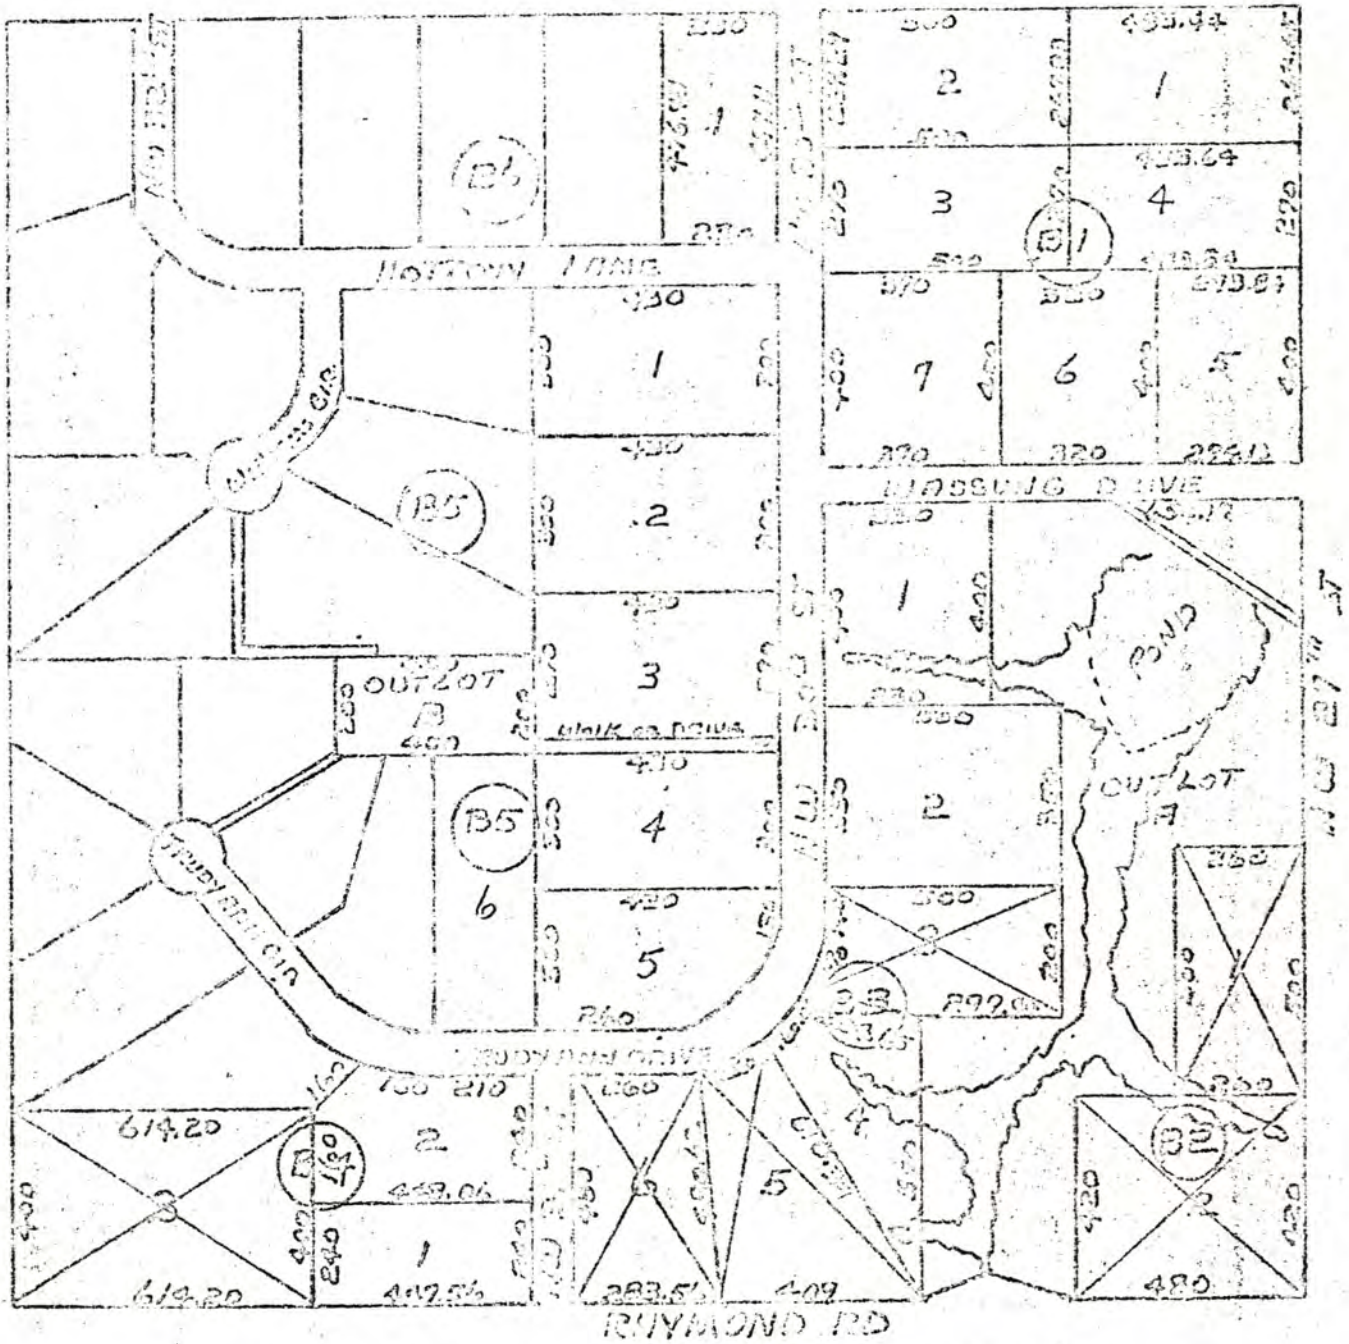

DEVELOPED BY WOODCRAFT HOMES SALES LIT

PHONE 488-1033

WOODCRAFT HOMES CORP.
3545 NO. 48 LINCOLN NE.

PHONE 466-2525
