LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1457-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

May 13, 1979 — THIS PERMIT EXPIRES

Thomas L. Flackman — ISSUED TO

Route 1, Box 11A, Davey, NE 68336 — ADDRESS

T12N, R6E, Section 28 W½ of NE¼ — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

FILING FEE: $ 30.00

FILE NO. 1457-C

DATE: 11-13-78

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 12N ; Range 6E ; Section 28 ; W¼ OF NE¼
   Block _____ : Lot 5 I.T. : Addition _____
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Thomas L. Blackmon
Signature of Applicant (Owner or Lessee)

Rt 1 Box 11A Davey, Nebr 68336
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 11/13/78. Date Frwd. 11/13/78. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 11-13-78. Date Frwd. 11-13-78. ACTION: Approved ☒ Disapproved ☐ Signature: Tom Baasch

3. City or County Engineer: Date Rec'd. 11-13-78. Date Frwd. 11-13-78. ACTION: Approved ☒ Disapproved ☐ Signature: Henry J. Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: Sept-78 by: RM
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: Sept-78 By: Ronald Wagner

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 11-13-78

FILE NO. 1457-C


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor [redacted] in., or below basement floor 24 in.
3. Distance between dwelling and septic tank 33 ft.
4. Number of clean-outs 2 .
5. Distances to:
Well or Suction Line 150 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1500 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre Cast Step)
4. Manholes: Over Inlet; diam. 12 in.
Over Outlet; diam. 12 in.
Riser Above ☐ Below ☒ Grade 12 in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line 150 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 6 .
2. Factory Built: Yes ☒ No ☐
(Company Pre Cast Step)
3. Distance from Septic Tank 10 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4 in .
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____ .
2. Lateral Lines:
Number 2 ; Length of each line 100 ft., _____ ft., _____ ft., _____ ft.;
Total length of laterals 100 ft.;
Distance between lateral lines _____ ft.
3. Trench dimensions: Width 36 in ft.;
Slope 4 in/100 ft.; Average Depth 18 in.
4. Filter Material: Gravel ,
Depth of Material 12 in.
5. Distances to:
Well or Suction Line 150 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

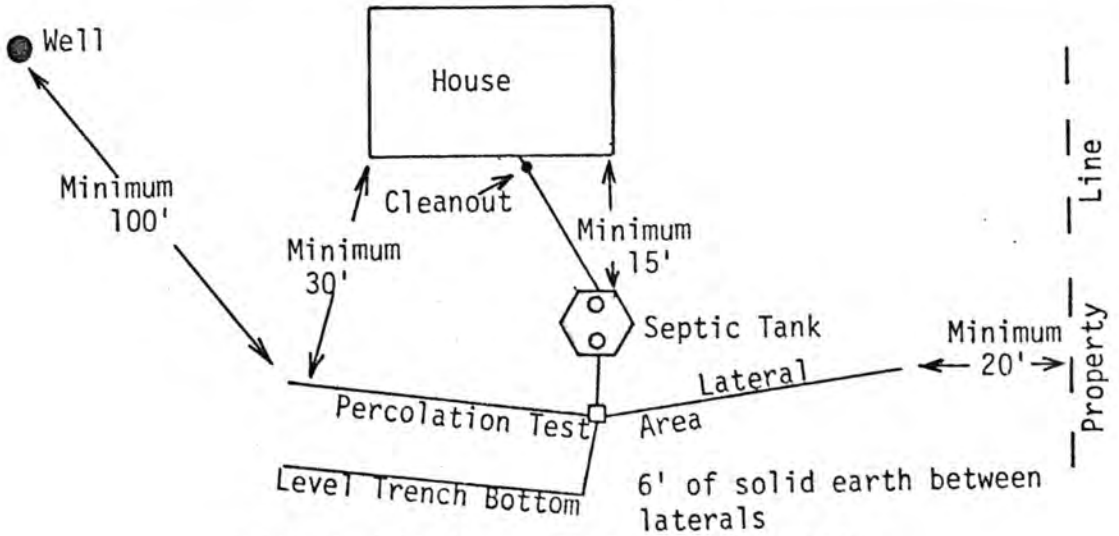

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 11-13-78 INSTALLER Tom Blackman

E

O Well

S

N

