LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 992-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION
TYPE OF PERMIT

June 30, 1977
THIS PERMIT EXPIRES

Roland Fenster
ISSUED TO

413 Laura Lane, Ceresco, NE
ADDRESS

T 12 N; R 6 E; Section 34
LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY | DATE | AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

Health
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 992-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 12-30-76

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

SEE ATTACHED

1. Legal description of property: Twp. 6N ; Range 12E ; Section 34
   Block _____; Lot _____; Addition _____ 5.02 ac.
   Street Address _____

2. Property Use: Residential _____ ☒ ; Commercial _____ ☐
   No. of Bedrooms 3 . Describe: _____
   Other Use _____ ☐
   Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: NA ft.

Roland Jenston
Signature of Applicant (Owner or Lessee)

441 S 54th Lincoln, Ne.
Address 413 Laura Lane Cerisco. Ne

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 12/30/76 . Date Frwd. 12/30/76 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: Date Rec'd. 1-7-77 . Date Frwd. _____ . ACTION: Approved ☒ Disapproved ☐ Signature: Tom Baasch

3. City or County Engineer: Date Rec'd. 12/30/76 . Date Frwd. 1/5/77 . ACTION: Approved ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 992-C

DATE: 12-30-76

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 10 N ; Range 6 E ; Section 34 ; Block ; Lot ; Addition .
Street Address .

2. Property Use: Residential ☒ ; Commercial ☐
No. of Bedrooms 3
Describe:
Other Use
Describe:

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Robert Forsles
Signature of Applicant (owner or lessee)

444 S 54th Lincoln, NE.
Address 413 Laura Lane Ccrsco. Ne

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd;
Filing Fee: $ 30.00

2. Site Visits:
Date: 5/25/77 by: J.C.H
Date: by:
Date: by:

3. Date: Approved ☒ ; Disapproved ☐ 12/30/76
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 5/25/77 by: Jerrold C. Hood

FORM HD-43 (73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 474-1541)

FILE NO. 992-C

PROPERTY WHERE SOIL TESTED:
Location: Township 6N : Range 12E
Section & ¼ Sect. NE¼ 34
Property Dimensions: 226 ft. x 1000 ft.
Area: _____ acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ; Silty Clay Loam ; Sandy Loam
Silty Loam ; Clay Loam ; Sandy Clay

Owner: Roland Fenster
Address: 4115 55th

Dates of Tests: 12-15 to 12-16. Weather: Precip. Dry Temp. 20°

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	32	12-15	10:00 AM	12-16	11:30 AM	12-16	4:00	6	4:30	5¼	30	¾	
2	32						4:00	6	4:30	4½	30	1½	
3	30						4:15	6	4:45	5¼	30	¾	
4	32						4:15	6	4:45	5	30	1	
5	31						4:15	6	4:45	5	30	1	
6	32						4:15	6	4:45	5¼	30	¾	

J.R. Pontico — Pontico Plbg Co.
Signature of Person Conducting Test

Address 1520 Pioneer Bl.
Phone 423-0121

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

REMARKS: Possible Morrill Clay Loam or Sharpsburg Silty Clay Loam (S.C.S.)
DATE: December 30, 1976

Approved Percolation Rate (a)
A. 32 min./inch
B. _____ min./inch
C. _____ min./inch

Gerald C. Wood
Signature of Reviewing Official

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. _____

SPECIFICATIONS

DATE: 12-30-76


A. BUILDING SEWER:
1. Material PVC 3034; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor 18 in.
3. Distance between dwelling and septic tank 75 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 500 ft.;
Stream — ft.; Pressure Line 500 ft.;
Property Line 175 ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Cement; No. of compartments _____.
2. Capacity 1000 gals.; Liquid depth ___ in.
3. Factory Built: Yes ☒ (Company Pre Cast)
No ☐
4. Manholes: Over Inlet; diam. 24 in.
Over Outlet; diam. ___ in.
Below Grade _____ in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet 1 in.
7. Depth of top of tank below finished grade ___ in.
8. Distances To:
Well or Suction Line 700 ft.;
Stream ___ ft.; Pressure Line 500 ft.;
Property Line 80 ft.

C. DISTRICTION BOX
1. Material Cement; No. available outlets 5.
2. Factory Built: Yes ☒, (Company Pre Cast) No ☐
3. Dimension: Length ___ in.; Width ___ in. Depth ___ in.
4. Distance from Septic Tank 10 ft.
5. Serial Distribution: Yes ☐, No ☒ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: _____
2. Lateral Lines: Depth below grade 36 in. Number 3; Length of each line ___ ft Total length of Laterals 258 ft.; Slope ___ in/100 ft. Diameter of pipe ___ in.; Shape _____ Material: concrete ☒; fiber asbestos ☐; clay ☐; other _____ Distance between lateral lines ___ ft.
3. Trench Dimensions: Depth 48 in.; Width 36 in.
4. Filter Material: gravel. Depth of material from trench bottom 24 in.
5. Distances To:
Well or Suction Line 700 ft.;
Stream — ft.; Pressure Line 500 ft.
Property Line 80 ft.
6. Percolation Rate: 32 minutes/inch

TYPICAL SKETCHES

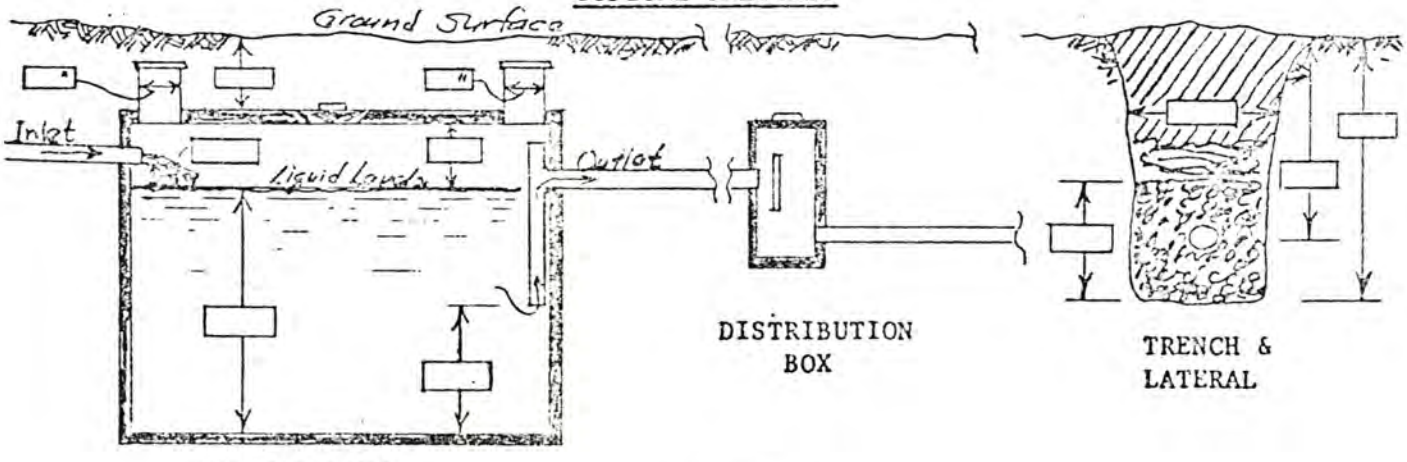

Signature of Applicant

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM

(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. _____

SPECIFICATIONS

DATE: 5-25-77


A. BUILDING SEWER:
1. Material PLASTIC; Diameter 4 in.
2. Distance above basement floor ____in.; or below basement floor ____in.
3. Distance between dwelling and septic tank 132 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 117 ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material CEMENT; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth 48 in.
3. Factory Built: Yes ☑ (Company PRECAST)
No ☐
4. Manholes: Over Inlet; diam. 7 in.
Over Outlet; diam. 7 in.
Below Grade 15 in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade 15 in.
8. Distances To:
Well or Suction Line 220 ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.


C. DISTRIBUTION BOX
1. Material CEMENT; No. available outlets 6.
2. Factory Built: Yes ☑, (Company PRECAST) No ☐
3. Dimension: Length 25 in.; Width 17 in. Depth 13 in.
4. Distance from Septic Tank 20 ft.
5. Serial Distribution: Yes ☐, No ☐ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: CEMENT LATERIALS
2. Lateral Lines: Depth below grade 18 in. Number ____; Length of each line ___ft Total length of Laterals 258 ft.; Slope 4 in/100 ft. Diameter of pipe ____ in.; Shape HALF MOON
Material: concrete ☑; fiber asbestos ☐; clay ☐; other ____
Distance between lateral lines 9 ft.
3. Trench Dimensions: Depth 36 in.; Width 36 in.
4. Filter Material: ROAD GRAVEL.
Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 225 ft.;
Stream ____ft.; Pressure Line ____ft.
Property Line ____ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

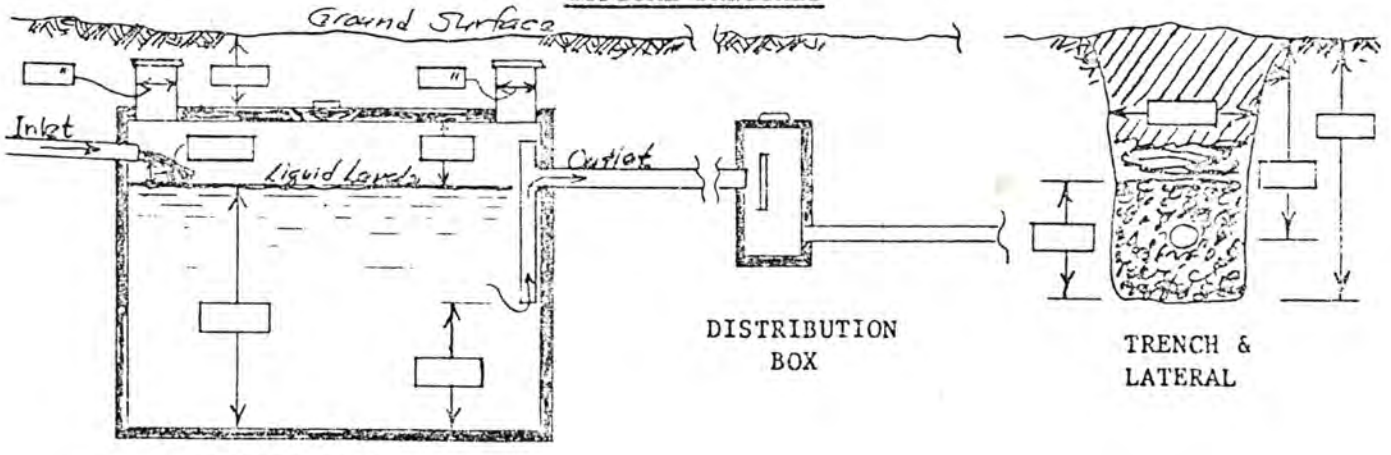

_____
Signature of Applicant

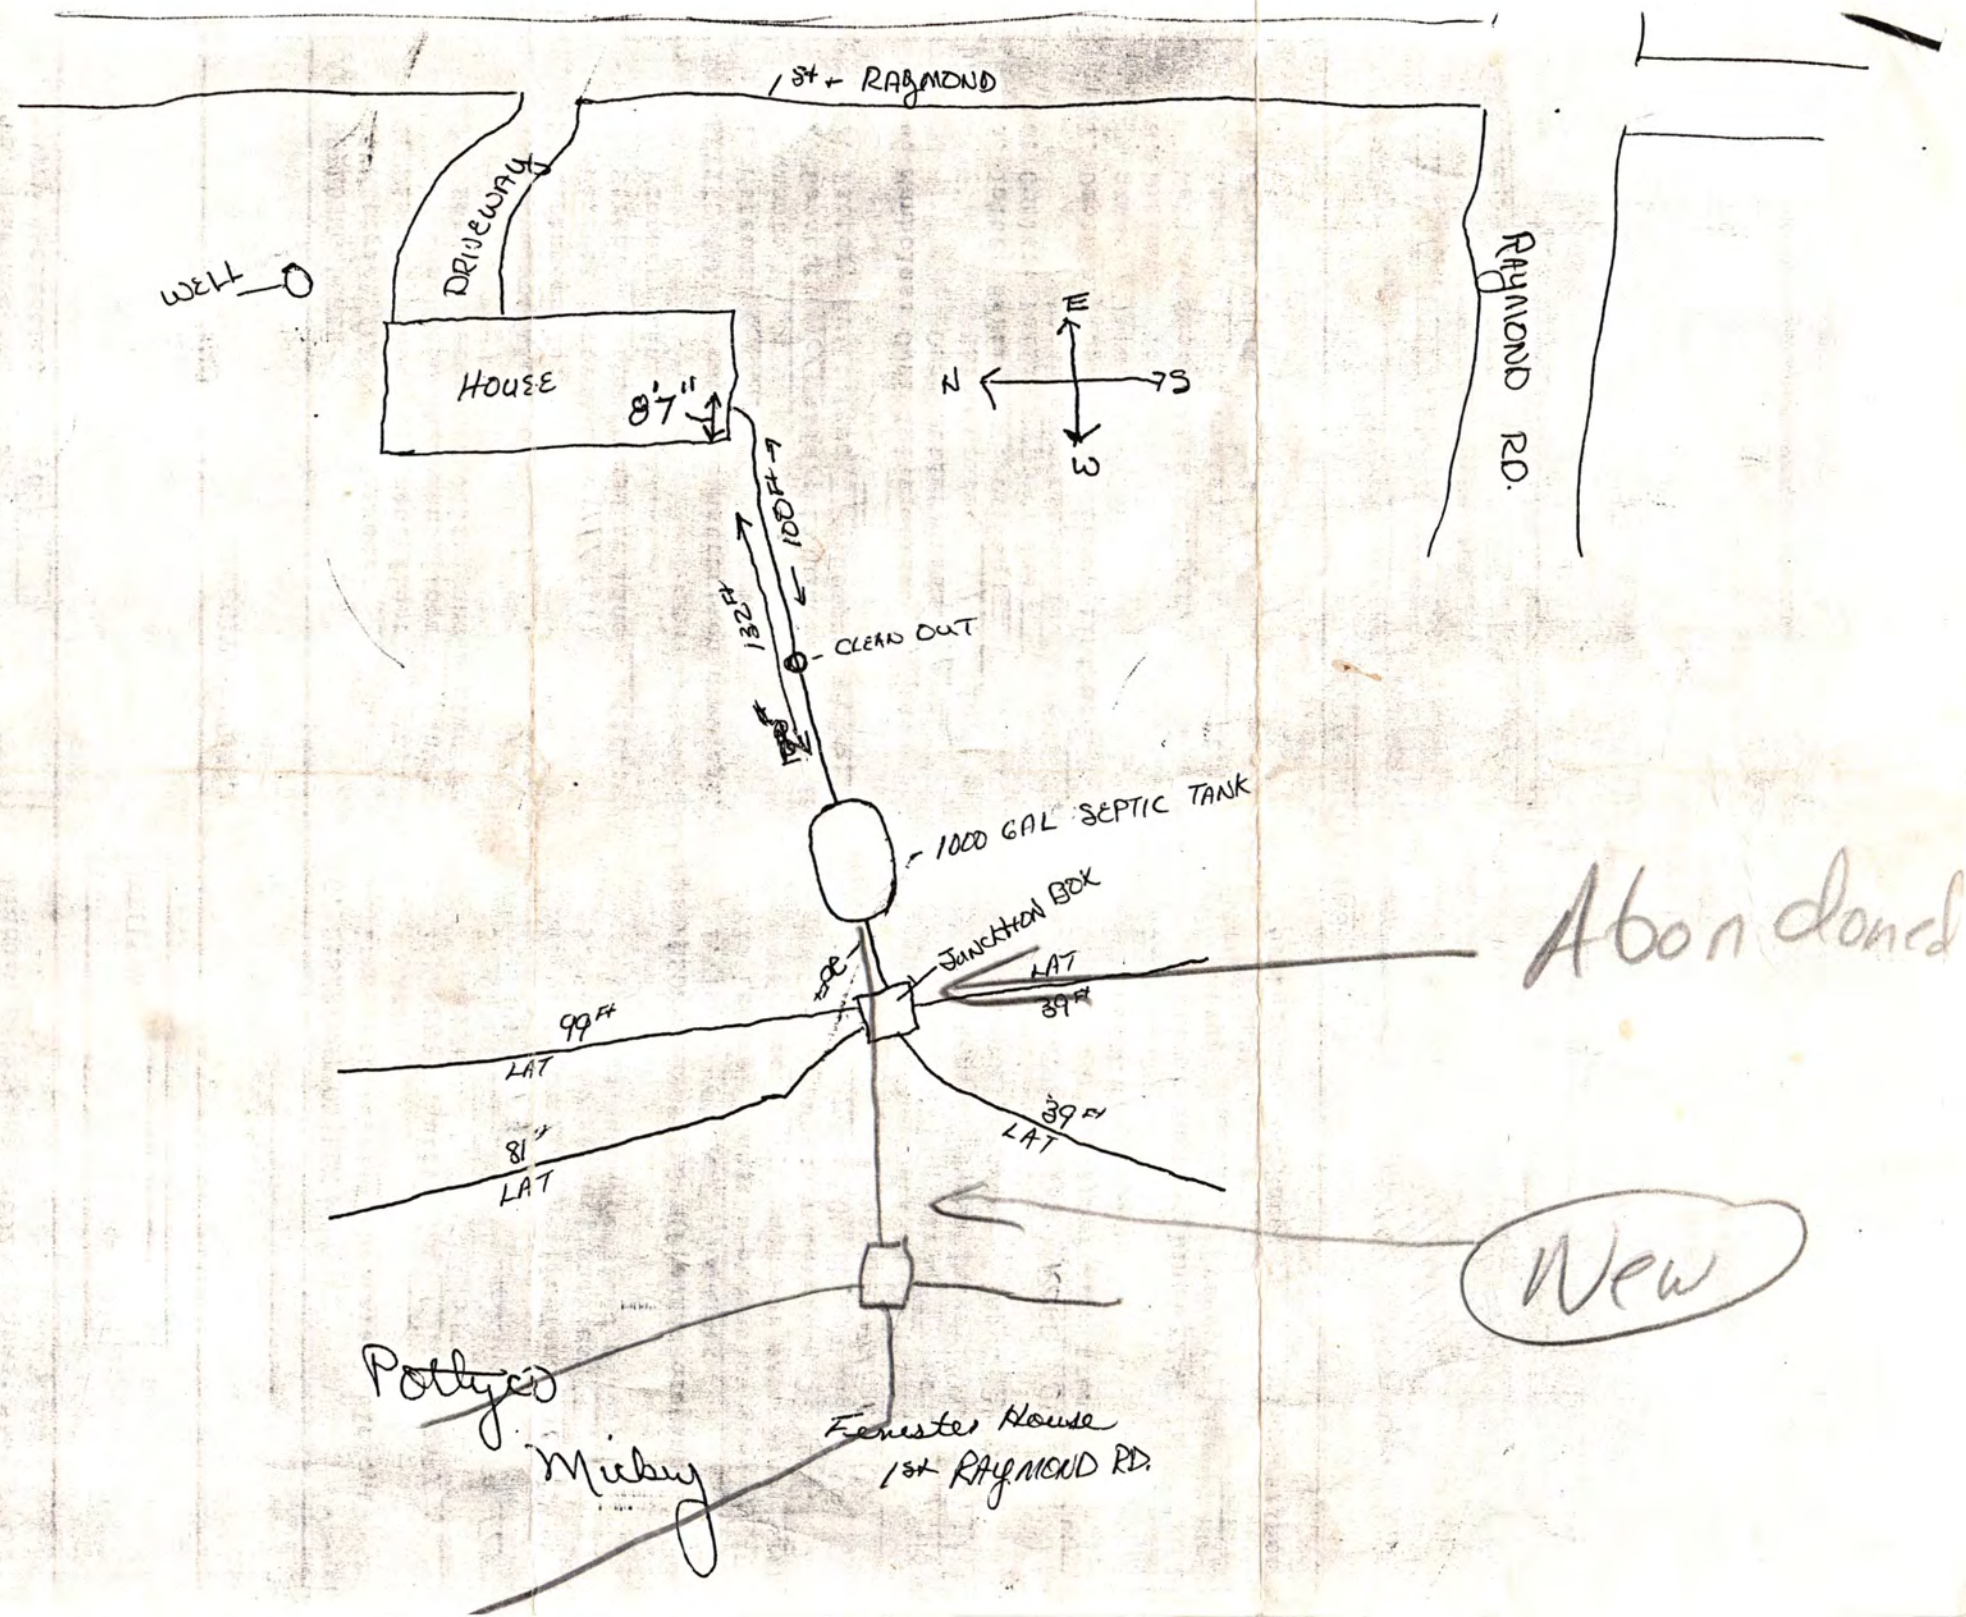
1st RAYMOND
DRIVEWAY
WELL
HOUSE
8'7"
RAYMOND RD.
E
N
S
W
100FT
132FT
CLEAN OUT
1000 GAL SEPTIC TANK
JUNCTION BOX
LAT
39FT
99FT
LAT
81"
LAT
39FT
LAT
Abandoned
New
Pottyco
Mickey
Fenester House
1st RAYMOND RD.

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. _____

SPECIFICATIONS

DATE: ~~8~~ 5-25-77


A. BUILDING SEWER:
1. Material PLASTIC; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor ___ in.
3. Distance between dwelling and septic tank 132 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 117 ft.;
Stream ___ ft.; Pressure Line ___ ft.;
Property Line ___ ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material CEMENT; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth 48 in.
3. Factory Built: Yes ☑ (Company PRECAST)
No ☐
4. Manholes: Over Inlet; diam. 7 in.
Over Outlet; diam. 7 in.
Below Grade 15 in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet ___ in.
7. Depth of top of tank below finished grade 15 in.
8. Distances To:
Well or Suction Line 220 ft.;
Stream ___ ft.; Pressure Line ___ ft.;
Property Line ___ ft.


C. DISTRIBUTION BOX
1. Material CEMENT; No. available outlets 6.
2. Factory Built: Yes ☑, (Company PRECAST) No ☐
3. Dimension: Length 28 in.; Width 12 in. Depth 13 in.
4. Distance from Septic Tank 20 ft.
5. Serial Distribution: Yes ☐, No ☐ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: CEMENT LATERIALS
2. Lateral Lines: Depth below grade 18 in.
Number ___; Length of each line ___ ft
Total length of Laterals 258 ft.;
Slope 4 in/100 ft. Diameter of pipe ___ in.; Shape HALF MOON
Material: concrete ☑; fiber asbestos ☐; clay ☐; other ___
Distance between lateral lines 9 ft.
3. Trench Dimensions: Depth 36 in.; Width 36 in.
4. Filter Material: ROAD GRAVEL.
Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 225 ft.;
Stream ___ ft.; Pressure Line ___ ft.
Property Line ___ ft.
6. Percolation Rate: ___ minutes/inch

TYPICAL SKETCHES

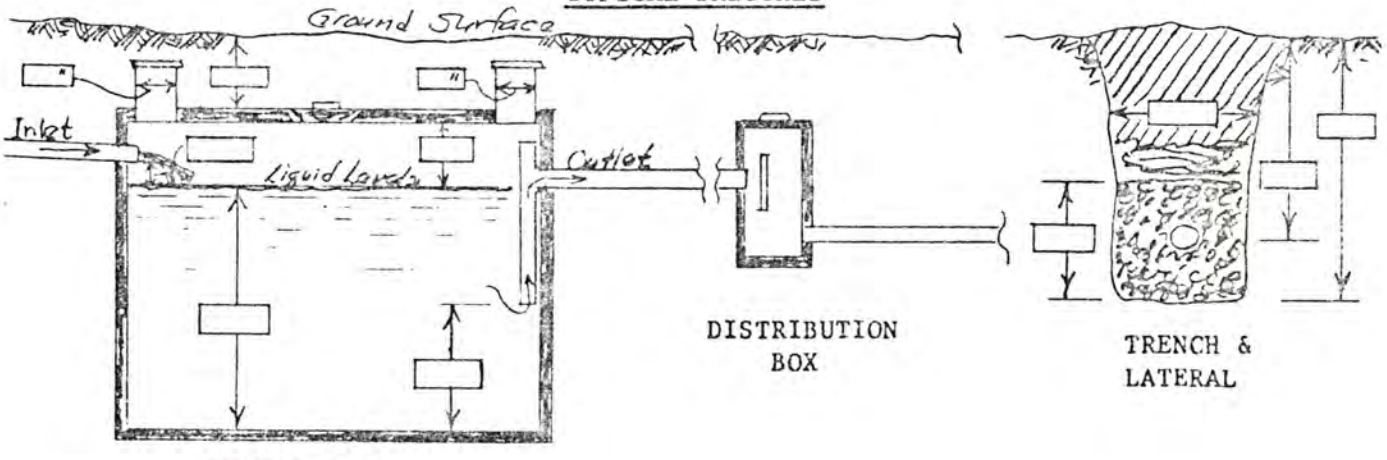

Signature of Applicant

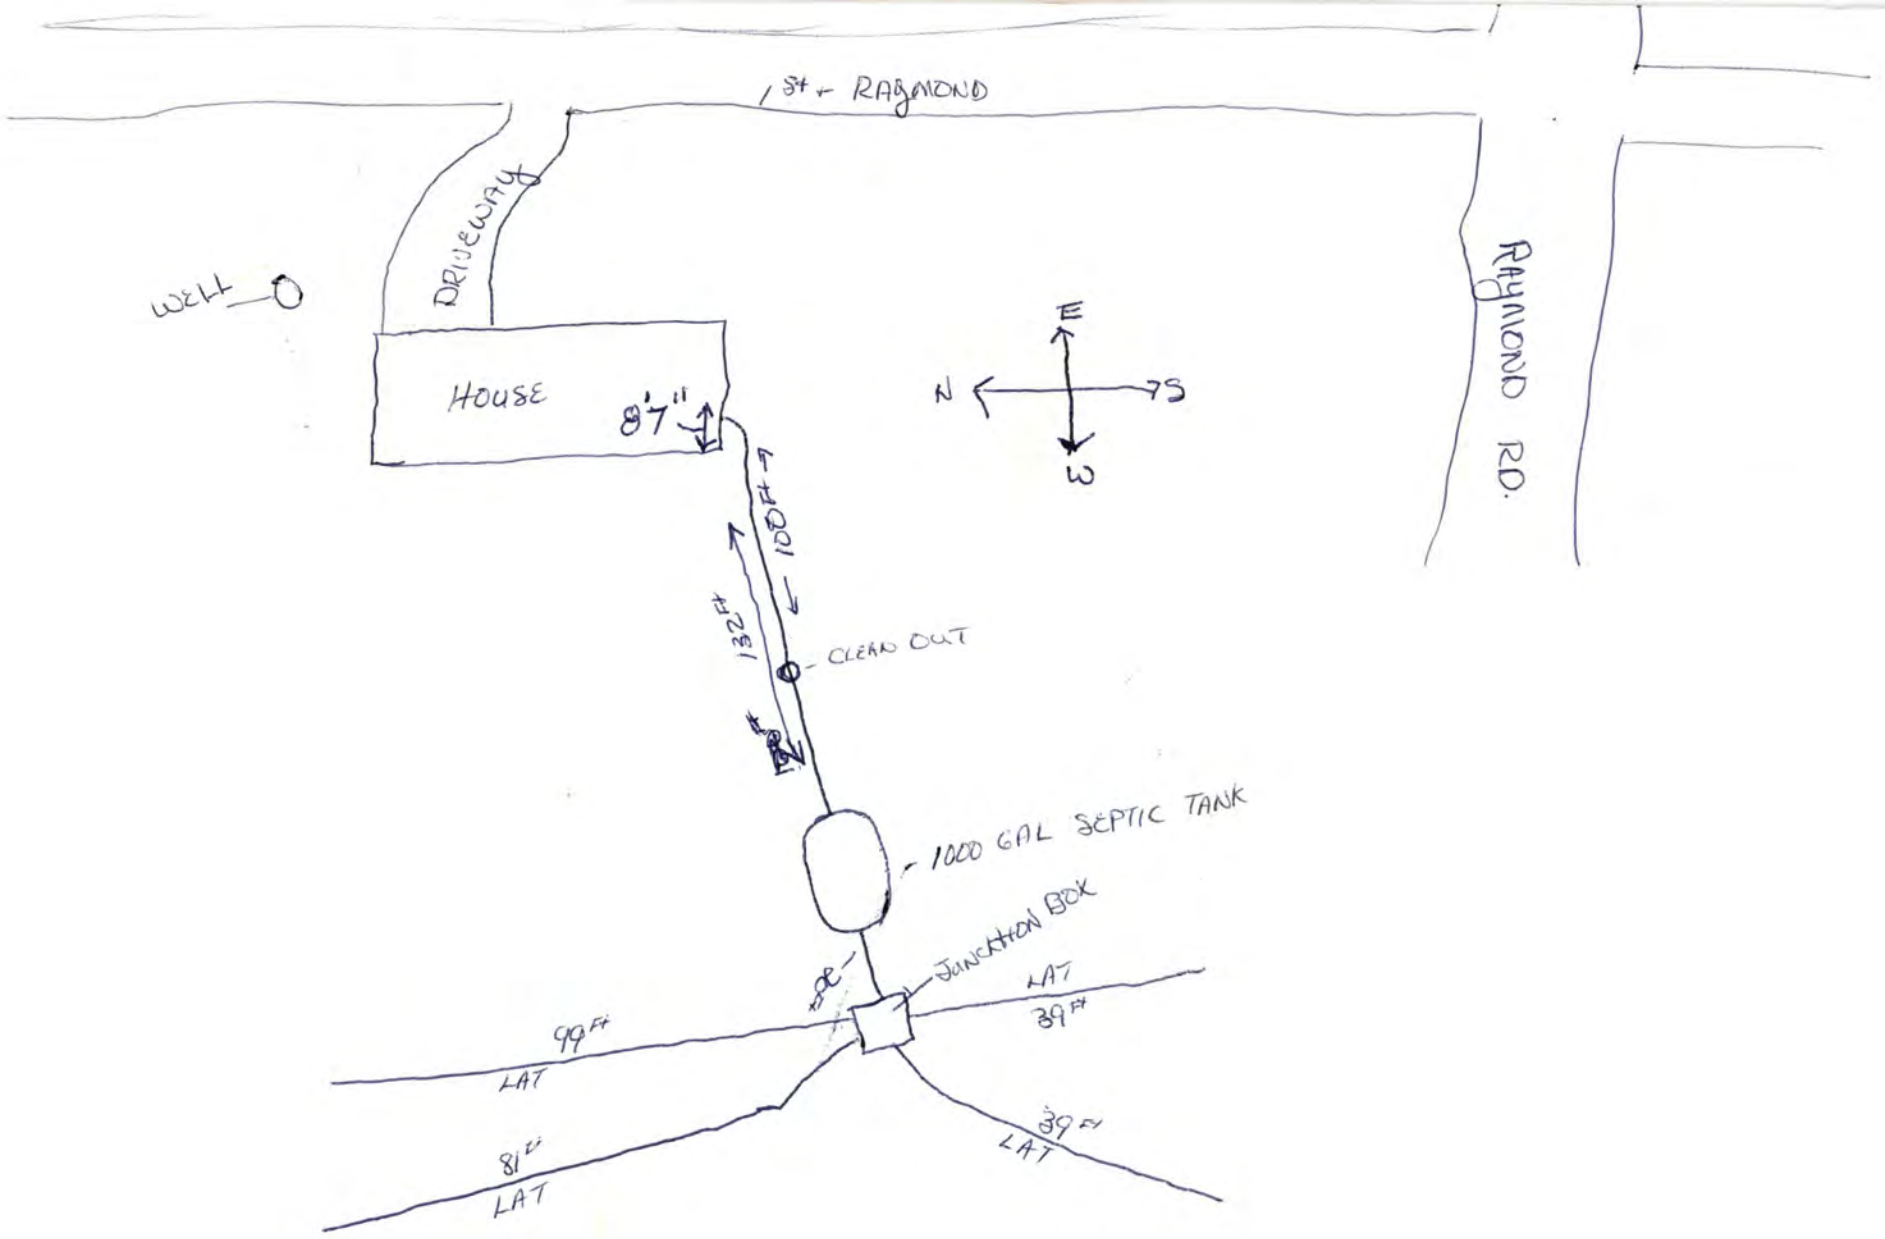


Pottyco

Micky

Fenester House
1st RAYMOND RD.

Rolland Fenister

PLOT PLAN

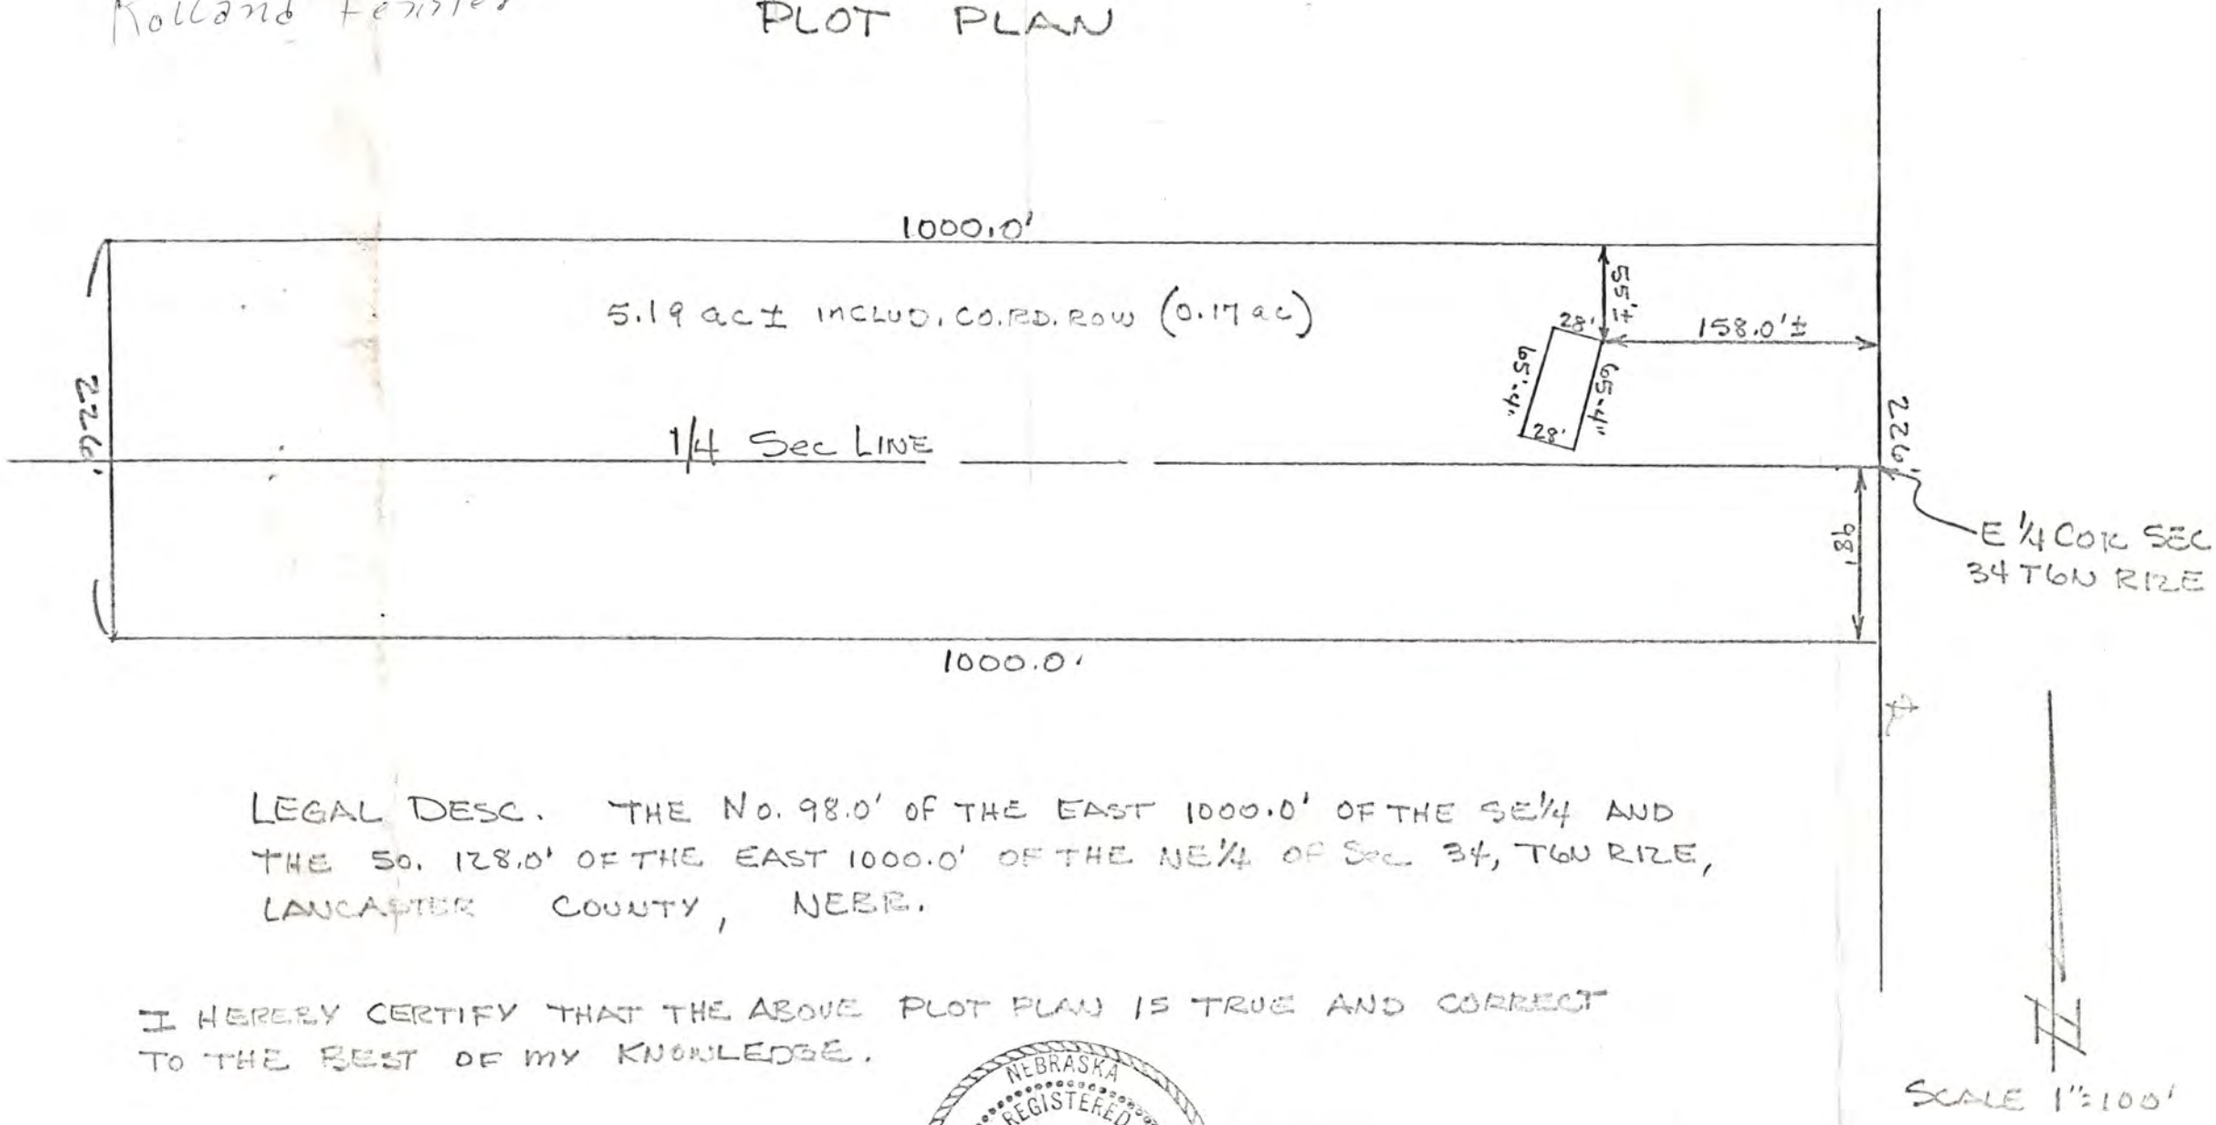

LEGAL DESC. THE NO. 98.0' OF THE EAST 1000.0' OF THE SE¼ AND THE SO. 128.0' OF THE EAST 1000.0' OF THE NE¼ OF Sec 34, T6N R12E, LANCASTER COUNTY, NEBR.

I HEREBY CERTIFY THAT THE ABOVE PLOT PLAN IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE.

NEBRASKA REGISTERED LS-252 LAND SUPVEYOR ROBERT B. BATES, JR.

Robert B. Bates
L.S. 252 NOV. 31 1976
