LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2098-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

DECEMBER 22, 1984 — THIS PERMIT EXPIRES

ELTON D. WALBRECHT, 19600 N.W. 126 ST., RT #1, BOX 50, RAYMOND, NE 6842 — ISSUED TO / ADDRESS

T12N; R5E; Sec 17; 19600 NW 126 St. — LEGAL DESCRIPTION

REMARKS: NON TRANSFERABLE ALTER, EXTEND OR REPAIR

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY	DATE	AMOUNT
DM	6-25-84	30.00

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 2098-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 6-21-84

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 12N ; Range R5E; Section 17 ;
Block ; Lot ; Addition
Street Address 19600 NW 126 St

2. Property Use: Residential ☒; Commercial ☐
No. Bedrooms 4
Describe
Other Use ☐
Describe

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: New Distribution Box, New Laterals from Septic to add 2 New Laterals

5. Work to be done by: Owner ☐ ; or Contractor ☒, Dayton Gillen
Contractor's Name

6. Estimated cost of project:

a. Materials	$
b. Labor	$
c. Other	$
TOTAL	$

Elton D. Waelbrecht
Signature of Applicant (owner or lessee)

19600 N.W. 126th RT. 1 - Box 50
Address
Raymond Nebr. 68428

(Do not write below this line)

REVIEWING ACTION


1. Date Rec'd: 6-22-84
Filing Fee: $ 20.00

2. Site Visits:
Date: 6-22-84 by: JM
Date: by:
Date: by:

3. Date: Approved ☒; Disapproved ☐
by: Jerrold E. Head

4. INSTALLATION FINAL WRITTEN APPROVAL*
Date: 6-22-84 by: Lon Mayuard

* Approval for subsurface laberal only - sewerline was covered without inspection

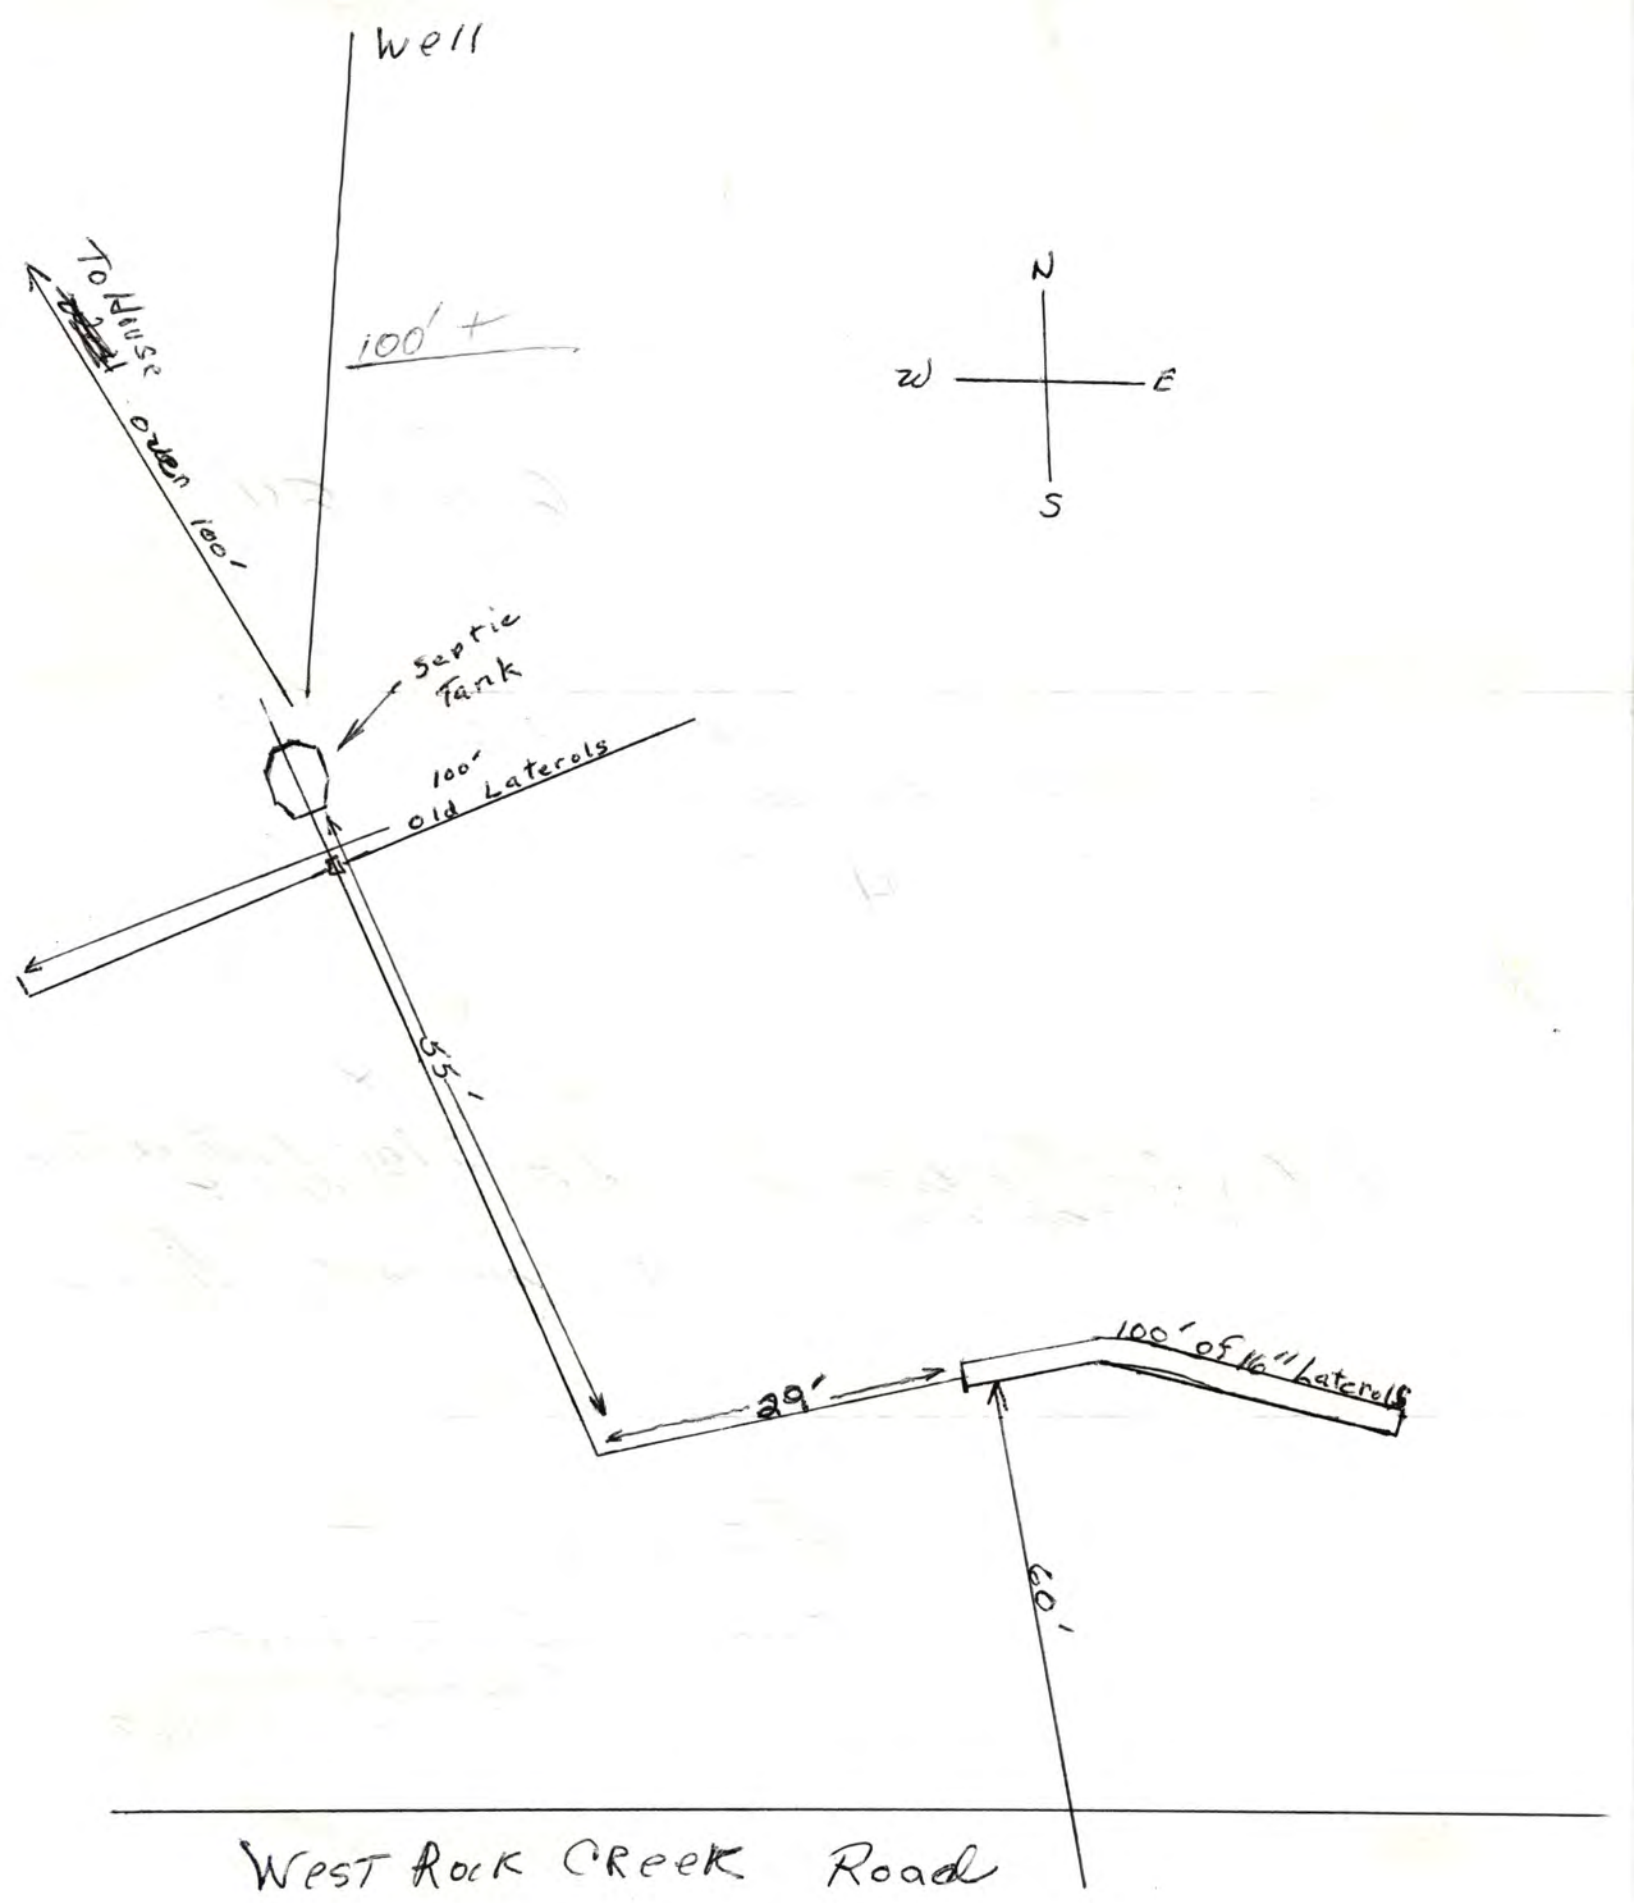
well
100' +
To House
100'
N
W
E
S
Septic Tank
100' old Laterals
55'
29'
100' of 1½" Laterals
60'
West Rock Creek Road

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1700-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — March 23, 1981

TYPE OF PERMIT — THIS PERMIT EXPIRES

ELTON D. WALBRECHT 19500 NW 126th, (Walton Const., 5100 N 48) Lincoln NE

ISSUED TO — ADDRESS

T12N, R5E, Section 17 SW¼

LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

FILING FEE: $ 60.00

FILE NO. 1700-C

DATE: Sept 19 1980

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 12N ; Range 5E ; Section 17 SW¼ 80 ACRES
   Block _____ : Lot _____ : Addition _____
   Street Address 19500 N.W. 126TH ST.

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: N/A ft.

Elton D. Walbrecht
Signature of Applicant (Owner or Lessee)

19500 N.W. 126th St.
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 9/23/80. Date Frwd. 9/23/80. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 9/24/80. Date Frwd. 9/24/80. ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer: Date Rec'd. 9-23-80. Date Frwd. 9-23-80. ACTION: ~~Approved~~ ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 9/25/80 by: L.C.H. too deep
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ By: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1700-C

PROPERTY WHERE SOIL TESTED:

Location: Township Lancaster; Range _____; Section & ¼ Section _____.
Property Dimensions: 350 ft. x 400 ft. Area: 80 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☒ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: Sept. 18, 1980 to Sept 19 1980. Weather: Precip. 0 Temp. 70.

OWNER: ELTON D. WALBRECHT

Address: 19,500 N.W. 126

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36"	9/18	9:15	9/19	9:36	9/19	9:30	6"	10:30	2 ½"	10"	3 ½"	10 / 3½"
2	36"	9/18	9:17	9/19	9:36	9/19	9:31	6"	10:31	2 ¼"	10	3 ¾"	10/ 3¾"
3	36"	9/18	9:18	9/19	9:37	9/19	9:31	6"	10:41	3 "	10	3 "	10/ 3"
4	36"	9/18	9:20	9/19	9:37	9/19	9:32	6"	10:42	2 ½"	10	3 ½"	10/ 3½"
5	36"	9/18	9:22	9/19	9:38	9/19	9:32	6"	10:42	2 "	10	4 "	10/ 4"
6	36"	9/18	9:23	9/19	9:38	9/19	9:33	6"	10:43	2 3/8"	10	3 5/8"	10/ 3⅝"

Sum of Percolation Rates: 21.33
Average of Rates: 3.55
Mean of Rates: _____

Claude L. Walton
Signature of Person Conducting Test

Address 5100 North 48th Lincoln Neb Phone 464-5797

(Do not write below this line)

REVIEWING ACTION

Remarks: Recheck soil on site
Soil Type (SCS): Very sandy 9/25/80
Date: _____

Approved Percolation Rate (a)
A. 8 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 1700-C

Indicate on sketch if residence and well are exisiting or proposed.

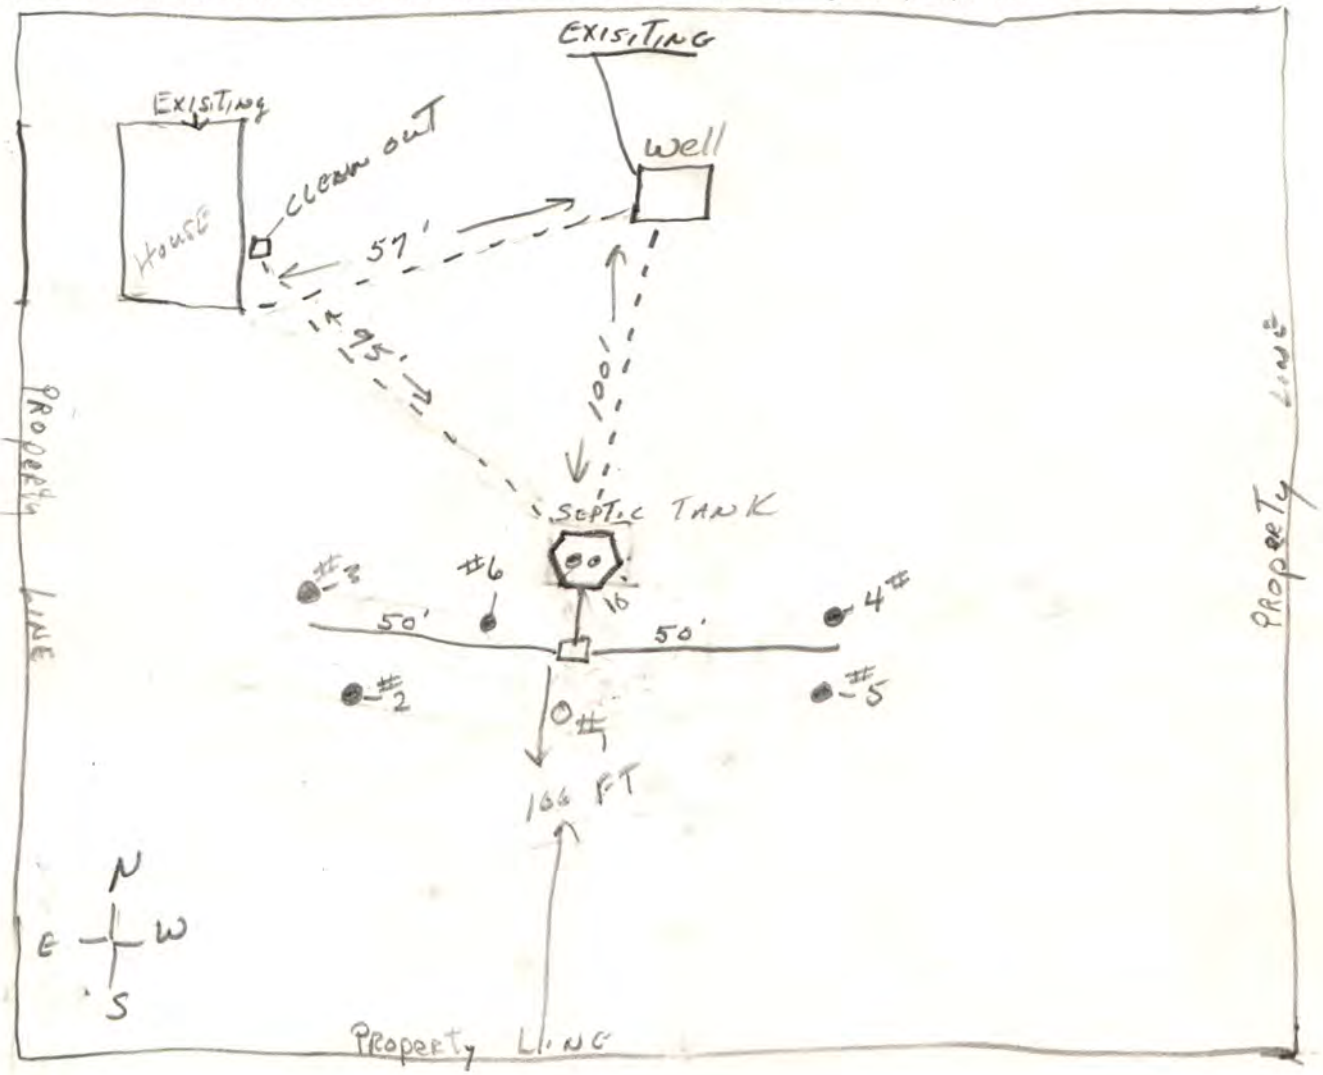

REVIEWING ACTION

Remarks: _____

_____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals 152 ft.
3. With a Trench Width of 36 in.
4. Total Area of Lateral needed 455 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: Sept 19 1988

FILE NO. 1700-C


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank 95 ft.
4. Number of clean-outs 1.
5. Distances to:
Well or Suction Line 100 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 100 ft.

B. SEPTIC TANK:
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Precast Co.)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line 100 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 100 ft.

C. DISTRIBUTION BOX:
1. Material Concrete; Number - available outlets _____.
2. Factory Built: Yes ☒ No ☐
(Company Precast Co.)
3. Distance from Septic Tank 10 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or Perforated Pipe X.
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 1; Length of each line 50, 50, _____, _____, _____ ft.;
Total length of laterals 100 ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 30" ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: Gravel
Depth of Material 12" in.
5. Distances to:
Well or Suction Line 100 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 100 ft.

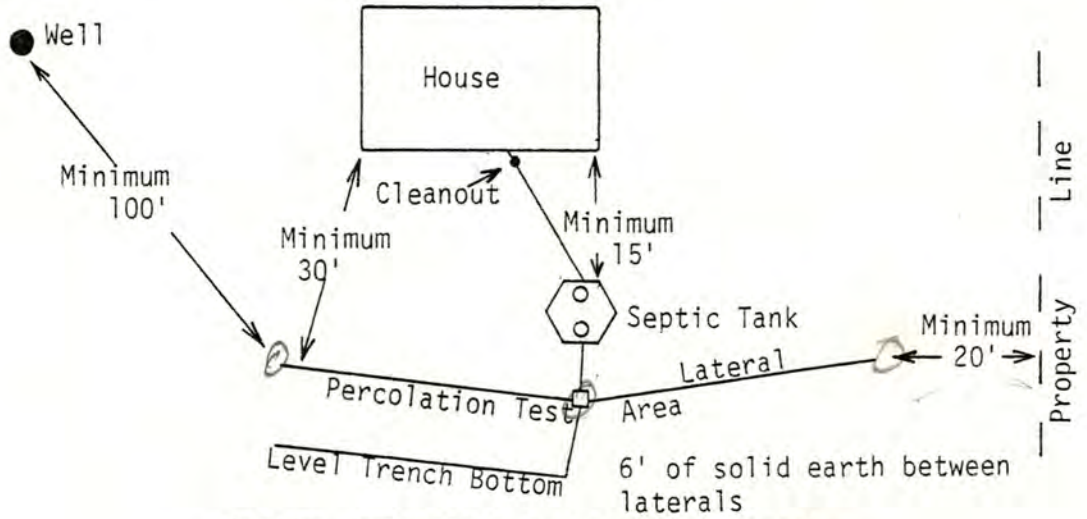

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN
