FORM HD-30(67) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 385-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with Lincoln City Ordinance No. 9150, as described herein:

1. Legal description of property: Twp. 10 N; Range 5 E; Section 35; SE 1/4
Block ____; Lot 12 IT; Addition ____;
Street Address ____.

2. Property Use: Residential ____ [X]; Commercial ____ [ ]
No. of Bedrooms 3. Describe: ____
Other Use ____ [ ]
Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank [X]; Other [ ]

4. Distance to public sewer: ____ ft.

Sharon A. Genthe
Signature of Applicant (owner or lessee)

3818 N.W. 51
Address Lincoln, Nebraska 68524

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 1/9/74. ACTION: Approved ___ [X] Disapproved [ ]
Date Frwd. 1/9/74. Signature: Jerrold C. Hook

2. Supt. Bldg. Insp.: Date Rec'd. ____. ACTION: Approved ___ [ ] Disapproved [ ]
Date Frwd. ____. Signature: ____

3. ~~City~~ COUNTY Engineer: Subd. Permit #174 Date Rec'd. 1-11-74. ACTION: Approved ___ [X] Disapproved [ ]
Date Frwd. 1-11-74. Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL ____

FINAL ACTION ON SITE CLEARANCE: Approved [ ] Disapproved [ ]

Date Applicant Notified: ____ Signature ____

FORM HD-32(67) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 385-C

DATE: _____

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with Lincoln City Ordinance No. 9150, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 10 N; Range 5E; Section 35; SE¼
Block _____; Lot 12IT; Addition _____;
Street Address _____.

2. Property Use: Residential _____ [X]; Commercial _____ [ ]
No. of Bed Rooms 3 Describe: _____
Other Use _____ [ ]
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank [X]; Other [ ]

4. Plans and Specifications of Proposed System. (See FORM HD-32a(67) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-33(67) SOIL ABSORPTION TEST DATA REPORT, attached hereto.)

Sharon A. Gruber
Signature of Applicant (owner or lessee)

3818 N.W. 51
Address Lincoln, Nebraska 68524

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd: _____
Filing Fee: $30.00

2. Date Site Clearance _____

3. Site Visits:
Date: _____ by: _____
Date: _____ by: _____
Date: _____ by: _____

4. Date: Approved [X]; Disapproved [ ]: 1/9/74
by: Jerrold C. Hood

5. BUREAU OF LICENSES & PERMITS
Date Notified: _____
Date Issued: _____ Serial _____

6. INSTALLATION FINAL WRITTEN APPROVAL
Date: 9/3/74 by: Jerrold C. Hood

FORM HD-33(67) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 432-7611)

FILE NO. 385-C

PROPERTY WHERE SOIL TESTED:
Location: Township 10
Section & ¼ Sect. 35 SE ¼
Property Dimensions 250.8 ft. x 200 ft.
Area: 1.15 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ☐; Silty Clay Loam ☐; Sandy Loam ☐
Silty Loam ☐; Clay Loam ☐; Sandy Clay ☐

Owner: Larry R. Gentke
Address 3831 Dunn Ave.

Dates of Tests: 7-13-73 to 7-14-73. Weather: Precip. ____ Temp. 80 F.

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
Hole No.	Hole Depth (in.)	Pre-Saturation Period Start Date (Mo. Day)	Pre-Saturation Period Start Time (Hr. Min.)	Pre-Saturation Period End Date (Mo. Day)	Pre-Saturation Period End Time (Hr. Min.)	Percolation Readings Start Date (Mo. Day)	Percolation Readings Start Time (Hr. Min.)	Percolation Readings Start Water Level (in.)	Percolation Readings End Time (Hr. Min.)	Percolation Readings End Water Level (in.)	Results Elapsed Time (Min.)	Results Water Level Drop (in.)	Results Percolation Rates (Min./inch)
1	36"	7/13	5:00	7/13	9:00	7/14	5:15	6"	9:15	4 3/4"	30 min	1 1/4"	
2	36"	7/13	5:00	7/13	9:00	7/14	5:15	6"	9:15	4 3/4"	30 min	1 1/4"	
3	36"	7/13	5:00	7/13	9:00	7/14	5:15	6 1/8"	9:15	5"	30 min	1 1/8"	
4	36"	7/13	5:01	7/13	9:01	7/14	5:15	6"	9:15	4 7/8"	30 min	1 1/8"	
5	36"	7/13	5:01	7/13	9:01	7/14	5:15	6"	9:15	4 1/4"	30 min	1 3/4"	
6	36"	7/13	5:01	7/13	9:01	7/14	5:15	6"	9:15	4 1/2"	30 min	1 1/2"	

Sum of Percolation Rates
Average of Rates: 1.3333"/30 min
Mean of Rates:

Larry R Gentke
Signature of Person Conducting Test

Address 3831 Dunn Ave. - Lincoln
Phone: 423-4577

(Do not write below this line)

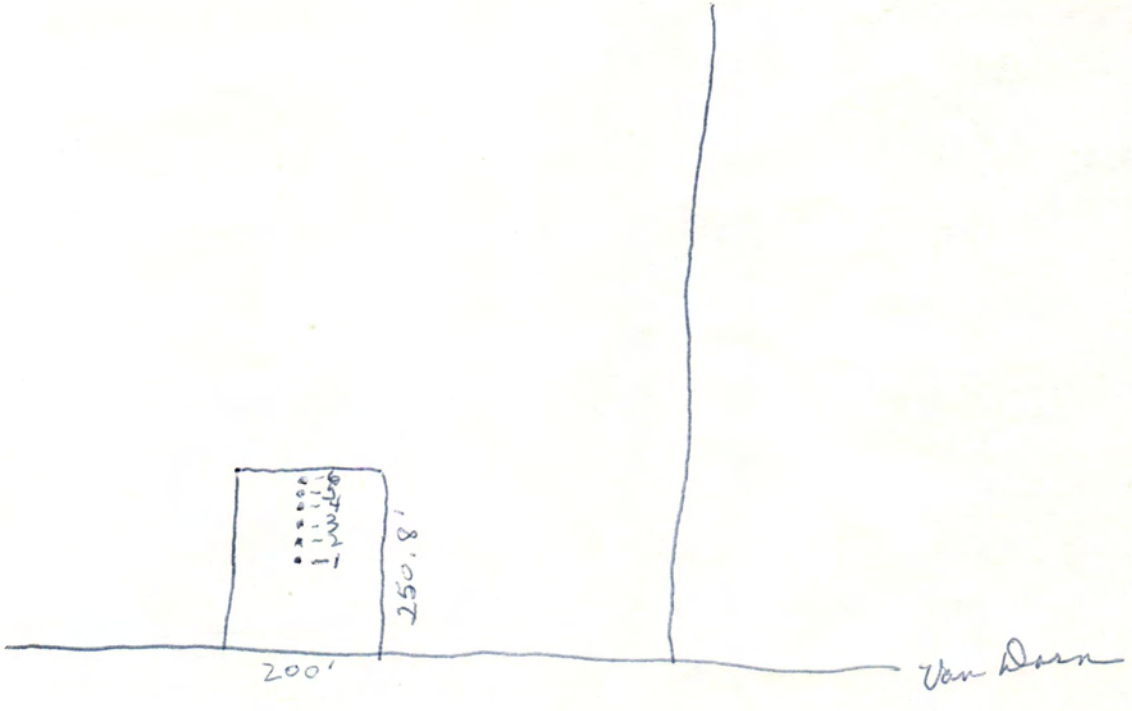
REVIEWING ACTION

REMARKS: _____

Approved Percolation Rate(s)
A. 2 3 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: January 9, 1974

Gerald C. Hood
Signature of Reviewing Official


250.8'
200'
Van Dorn

FORM HD-33(67) SOIL ABSORPTION
TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 432-7611)

FILE NO. _____

PROPERTY WHERE SOIL TESTED:
Location: Township 10
Section & ¼ Sect. SE¼ Sec. 35
Property Dimensions: 200 ft. x 217.8 ft.
Area: 1 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ☐; Silty Clay Loam ☒; Sandy Loam ☐
Silty Loam ☐; Clay Loam ☐; Sandy Clay ☐

Owner: Larry R. Genthe
Address 3831 Dunn Ave

Dates of Tests: June 7, 1973 to June 8, 1973. Weather: Precip. clear Temp. 85° F.

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
Hole No.	Hole Depth (in.)	Pre-Saturation Period Start Date (Mo. Day)	Pre-Saturation Period Start Time (Hr. Min.)	Pre-Saturation Period End Date (Mo. Day)	Pre-Saturation Period End Time (Hr. Min.)	Percolation Readings Start Date (Mo. Day)	Percolation Readings Start Time (Hr. Min.)	Percolation Readings Start Water Level (in.)	Percolation Readings End Time (Hr. Min.)	Percolation Readings End Water Level (in.)	Results Elapsed Time (Min.)	Results Water Level Drop (in.)	Results Percolation Rates (Min./inch)
1	38	6/7	3:36	6/7	7:41	6/8	5:15	6"	9:15	4⅝"	30 min	1⅜"	
2	38	6/7	3:38	6/7	7:40	6/8	5:16	6⅜"	9:15	5½"	30 min	⅝"	
3	38	6/7	3:39	6/7	7:42	6/8	5:16	6"	9:17	5¼"	30 min	¾"	
4	38	6/7	3:40	6/7	7:43	6/8	5:17	6¼"	9:18	4⅝"	30 min	5/8"	
5	38	6/7	3:42	6/7	7:45	6/8	5:17	6"	9:20	5¼"	30 min	¾"	
6	38	6/7	3:43	6/7	7:46	6/8	5:18	6"	9:21	5⅛"	30 min	⅛"	

Sum of Percolation Rates _____
Average of Rates: _____
Mean of Rates: _____

Mrs. Larry R. Genthe
Signature of Person Conducting Test

Address 3831 Dunn Ave. Lincoln, Nebr. 68502
Phone: 423-4577

(Do not write below this line)

REVIEWING ACTION

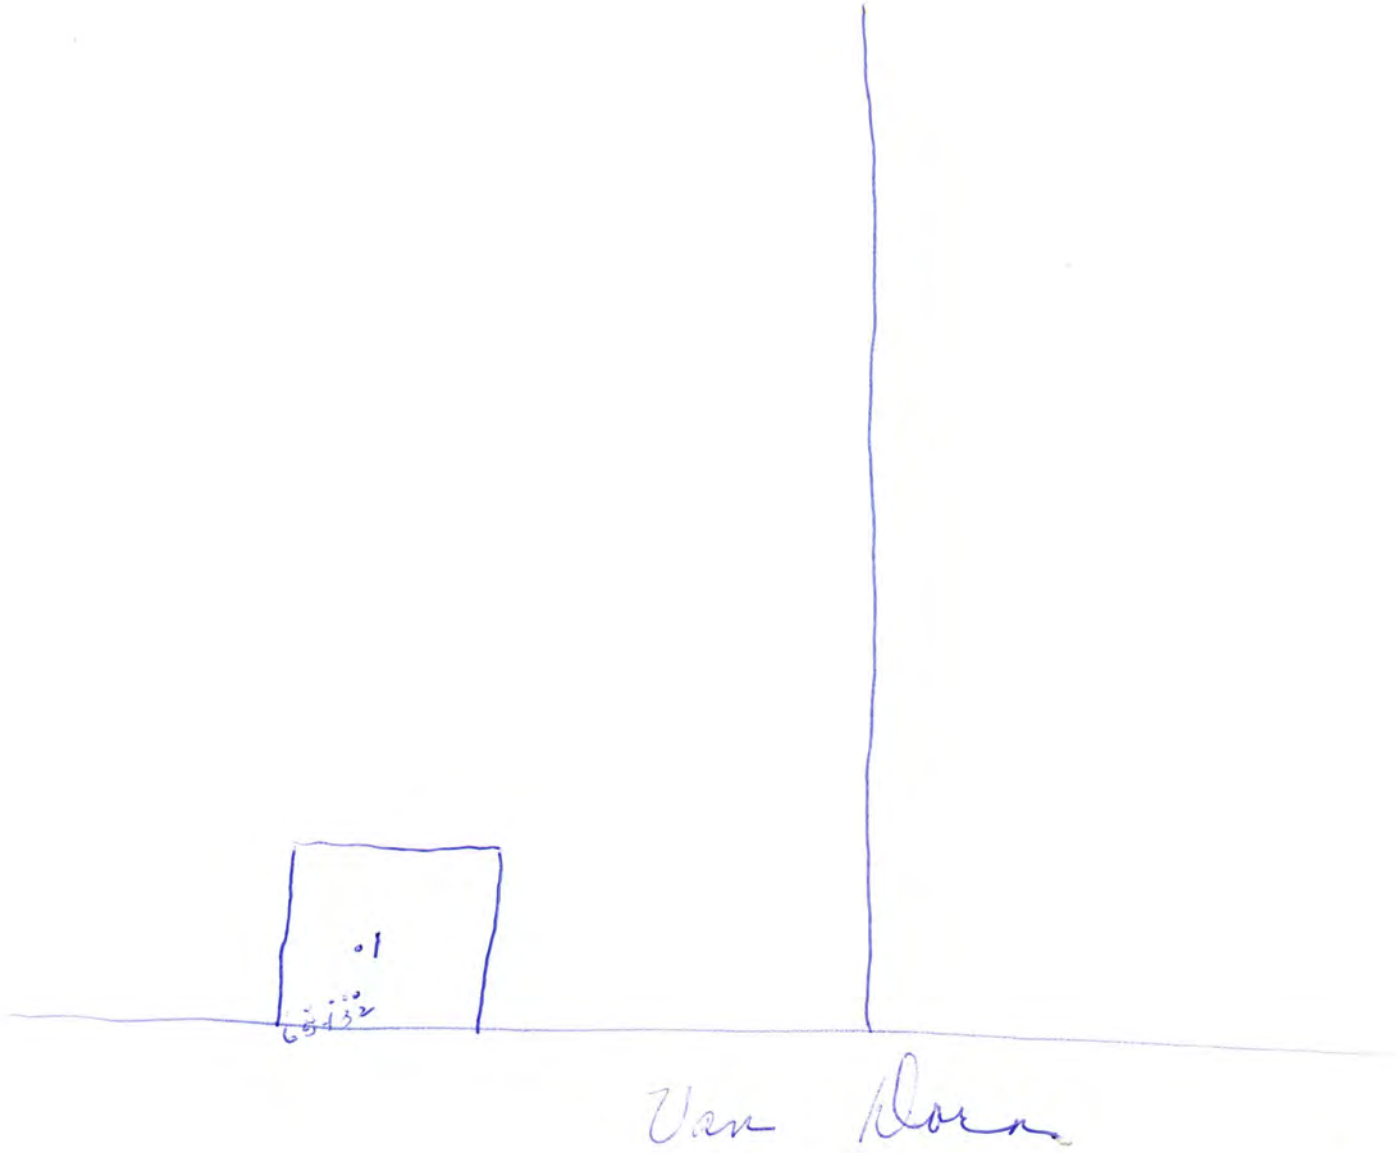
REMARKS: _____

Approved Percolation Rate(s)
A. 44 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: June 18, 1973

Jerrold C. Wood
Signature of Reviewing Official

223' lateral in 4' wide trench


Van Doren

FORM HD-32a(67) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 385-C

SPECIFICATIONS

DATE: _____

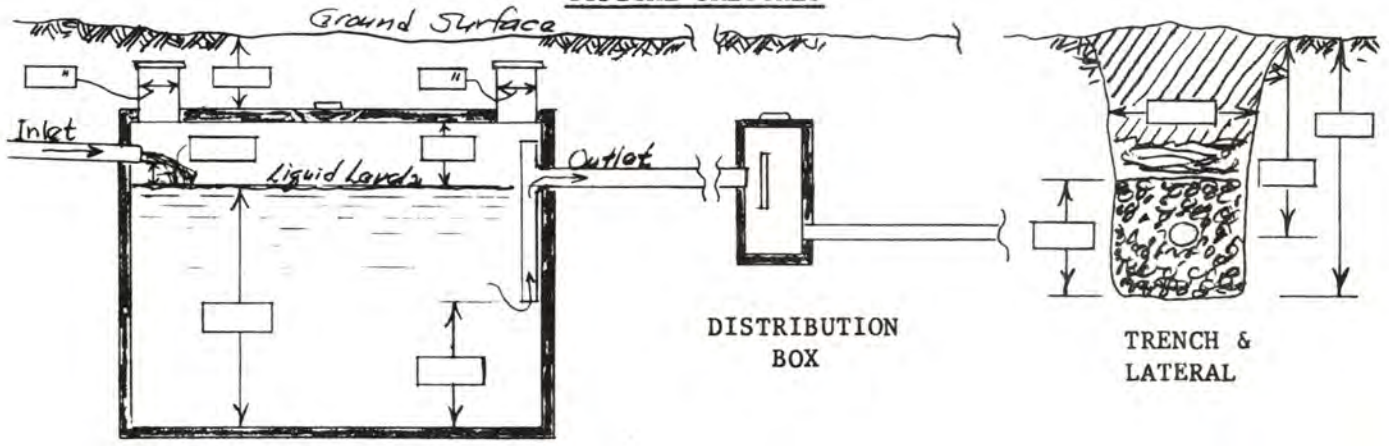
A. BUILDING SEWER:
1. Material _____; Diameter ____ in.
2. Distance above basement floor ____in.; or below basement floor ____in.
3. Distance between dwelling and septic tank ____ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Concrete No. of compartments Single.
2. Capacity 1000 gals.; Liquid depth ____ in.
3. Factory Built: Yes ☒ (Company Pre-Cast Stop)
No ☐
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 6 in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☒
Depth of outlet below inlet 1 in.
7. Depth of top of tank below finished grade ____in.
8. Distances To:
Well or Suction Line 81 ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line 20 ft.

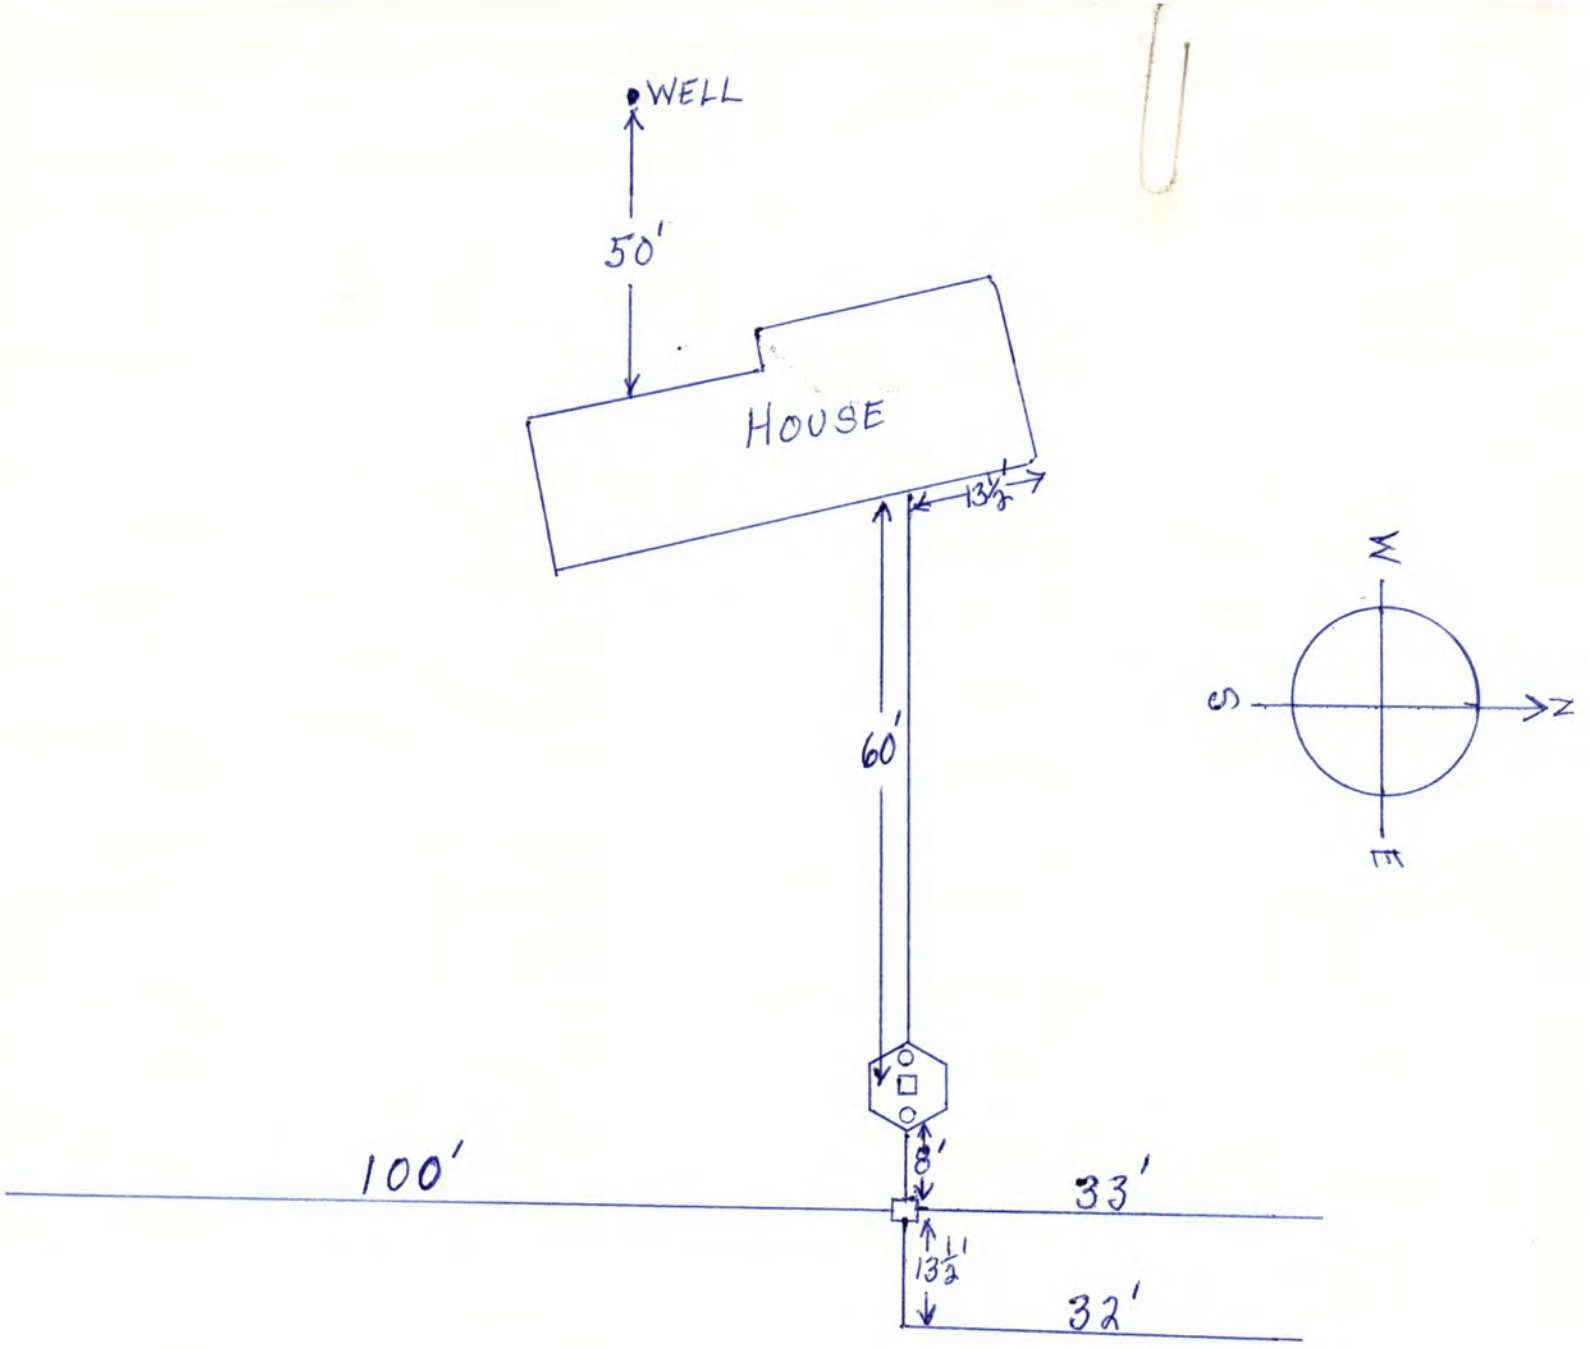
C. DISTRICTION BOX
1. Material Concrete; No. available outlets 5.
2. Factory Built: Yes ☒, (Company Pre Cast Stop)
_____ No ☐
3. Dimension: Length ____in.; Width ___in.
Depth ____in.
4. Distance from Septic Tank ____ft.
5. Serial Distribution: Yes ☐, No ☒
(If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: Half Moon
2. Lateral Lines: Depth below grade ___in.
Number 2; Length of each line 84 ft
Total length of Laterals 168 ft.;
Slope 4 in/100 ft. Diameter of pipe ____ in.; Shape ⌒
Material: concrete ☒; fiber asbestos ☐; clay ☐; other _____
Distance between lateral lines 6 ft.
3. Trench Dimensions: Depth 36 in.;
Width 48 in.
4. Filter Material: Gravel.
Depth of material from trench bottom _____in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream _____ft.; Pressure Line ____ft.
Property Line ____ft.
6. Percolation Rate: 23 minutes/inch

TYPICAL SKETCHES



Sharon A. Gunthe
Signature of Applicant


WELL
50'
HOUSE
13½'
60'
N
S
E
W
100'
8'
33'
13½'
32'

006

Lincoln-Lancaster County Health Department

2200 St. Mary's Avenue, Lincoln, Nebraska 68502 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☐ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☒ Evaluation of the Individual Water System ☒ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address _____

Twp 10N Range 5E Section 35 1/4 ____ 1/4 ____ Block ____ Lot 127 Addition _____

Directions to Property WEST VAN DORN. 3 MILE WEST OF PIONEER PARK NORTH ENTRANCE. BEIGE HOUSE NORTH SIDE OF ROAD

Location of Well 50 FT WEST OF HOUSE Tap Location: Inside ☐ Outside ☐

Location of Sewage System 57 FT. EAST OF HOUSE Year Installed 1974

	NAME	ADDRESS	PHONE
Present Owner:	LARRY & SHARON GENTHE	ROUTE #6 LINCOLN, NE 68522	438-2339
Tenant/Buyer:	LARRY & SHARON GENTHE	ROUTE #6 LINCOLN, NE 68522	438-2339
Return to:	Commercial Federal	13/4 O St. Lincoln, NE 68508	473-0707

Signature of Applicant Larry R Genthe Address Route #6 Lincoln Ne 68522 Date 9/7/93

HEALTH DEPARTMENT USE ONLY

Date Received 9/10/93 Received $150.00 Check ☒ Cash ☐

PRELIMINARY STATUS--By Jerrold C. Hood **DATE:** 9/10/93

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM	Additional Site Visits
Construction	☐	☒	Approved ☒	Date 9/14/93 by J.C.H.
Bacteria	☒ 0 /ml	☐ ____ /ml	Provisional ☐	Date ___/___/___ by ____
Nitrate	☒ <0.1 ppm	☐ ____ ppm	Disapproved ☐	Date ___/___/___ by ____

Comments: WIRING CONDUIT IS BROKEN COMING INTO WELL HEAD. PELLET DROP TUBE IS BROKEN OFF IN WELL HEAD. Corrected 9/14/93 J.C.H.

See Attached Letter ☐

FINAL STATUS

WATER SYSTEM: Approved: ☒ **SEWAGE DISPOSAL SYSTEM** Approved: ☒ Provisional Approval: ☐

Approved by Jerrold C. Hood R.E.H.S. Date 9/16/93

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

187
