FILE NO. 151

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

November 18, 1970 — THIS LICENSE OR PERMIT EXPIRES

Bernard L. Hirsch — LICENSEE OR PERMITTEE

1628 North 57 — ADDRESS

T 10N; R 6E; Section 30; Lot 26 — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: Non-Transferable

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
143-1535	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-30(67) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 151

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with Lincoln City Ordinance No. 9150, as described herein:

1. Legal description of property: East 330 ft. of Lot 26 SW 1/4 of SE 1/4
Twp. 10N ; Range 6E ; Section 30 ;
Block ____; Lot ____; Addition ____;
Street Address R.R.6 .

2. Property Use: Residential ____ [X]; Commercial ____ [ ]
No. of Bedrooms 3 . Describe: ____
Other Use ____ [ ]
Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank [X]; Other [ ]

4. Distance to public sewer: several miles ft.

Bernard L. Hirsch
Signature of Applicant (owner or lessee)

1628 No. 57 Lincoln
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 5/18/70 . ACTION: Approved [ ] Disapproved [X]
Date Frwd. 5/18/70 . Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: Date Rec'd. 5-18-70 . ACTION: Approved [ ] Disapproved [X]
Date Frwd. 5-18-70 . Signature: Charles L. By Bob Hunt

3. City Engineer: Date Rec'd. 5-18-70 . ACTION: Approved [ ] Disapproved [X]
Date Frwd. 5-18-70 . Signature: J. Blessing

REMARKS OR REASONS FOR DISAPPROVAL ____

FINAL ACTION ON SITE CLEARANCE: Approved [ ] Disapproved [ ]

Date Applicant Notified: ____ Signature ____

FORM HD-32(67) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 151

DATE: May 18, 1970

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with Lincoln City Ordinance No. 9150, as described in this application and the annexed forms attached hereto.

1. Legal description of property: East 330 ft. of Rot 26, SW¼, SE¼ Twp. 10N; Range 6E; Section 30; Block ____; Lot ____; Addition ____; Street Address R.R.6.

2. Property Use: Residential ____ [X]; Commercial ____ [ ]
No. of Bed Rooms Three Describe: ____
Other Use ____ [ ]
Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank [X]; Other [ ]

4. Plans and Specifications of Proposed System. (See FORM HD-32a(67) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-33(67) SOIL ABSORPTION TEST DATA REPORT, attached hereto.)

Bernard R. Hirsch
Signature of Applicant (owner or lessee)

1628 No. 57, Lincoln
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd: ____
Filing Fee: $30.00 ____

2. Date Site Clearance ____

3. Site Visits:
Date: ____ by:
Date: 8/18/70 by: L.C.H.D.
Date: ____ by: ____

4. Date: Approved [X]; Disapproved [ ]: 5/18/70
by: Jerrold C. Hood

5. BUREAU OF LICENSES & PERMITS
Date Notified: ____
Date Issued: ____ Serial ____

6. INSTALLATION FINAL WRITTEN APPROVAL
Date: 8/18/70 by: Jerrold C. Hood

FORM HD-33(67) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 432-7611)

FILE NO. 151

PROPERTY WHERE SOIL TESTED:
Location: Township 10
Section & ¼ Sect. SW¼, SE¼ Sec. 30
Property Dimensions: 330 ft. x 660 ft.
Area: 5 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay [ ]; Silty Clay Loam [ ]; Sandy Loam [ ]
Silty Loam [ ]; Clay Loam [X]; Sandy Clay [ ]

Owner: _____
Address _____

Dates of Tests: 5-15-70 to 5-16-70. Weather: Precip. PT. CLDY Temp. 80 F.

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
Hole No.	Hole Depth (in.)	Pre-Saturation Period Start Date (Mo. Day)	Pre-Saturation Period Start Time (Hr. Min.)	Pre-Saturation Period End Date (Mo. Day)	Pre-Saturation Period End Time (Hr. Min.)	Percolation Readings Start Date (Mo. Day)	Percolation Readings Start Time (Hr. Min.)	Percolation Readings Start Water Level (in.)	Percolation Readings End Time (Hr. Min.)	Percolation Readings End Water Level (in.)	Results Elapsed Time (Min.)	Results Water Level Drop (in.)	Results Percolation Rates (Min./inch)
1	34	5-15	3:30 PM	5-15	5:30	5-16	3:30					1/4	
2	35	5-15	3:30	5-15	5:30	5-16	3:30					1 1/4	
3	34	5-15	3:30	5-15	5:30	5-16	3:30					1 1/4	
4	33	5-15	3:30	5-15	5:30	5-16	3:30					1/2	
5	33	5-15	3:30	5-15	5:30	5-16	3:30					1/4	
6	32	5-15	3:30	5-15	5:30	5-16	3:30					0	

Bernard R. Hirsch
Signature of Person Conducting Test

Address 1628 No. 57
Phone: Hirsch 466-7421

Sum of Percolation Rates
Average of Rates:
Mean of Rates:

(Do not write below this line)

REVIEWING ACTION

REMARKS: _____

Approved Percolation Rate(s)
A. 40 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: May 18, 1970

Gerrold C. Hood
Signature of Reviewing Official

FORM HD-32a(67) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 151

SPECIFICATIONS

DATE: May 18, 1970


A. BUILDING SEWER:
1. Material Clay; Diameter 4" in.
2. Distance above basement floor ___ in.; or below basement floor 10 in.
3. Distance between dwelling and septic tank 45 ft.
4. Number of clean-outs 1.
5. Distances To:
   Well or Suction Line 50 ft.;
   Stream ___ ft.; Pressure Line ___ ft.;
   Property Line ___ ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material fiberglass; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ___ in.
3. Factory Built: Yes [X] (Company CORRIGATED FIBERGLASS)
   No [ ]
4. Manholes: Over Inlet; diam. ___ in.
   Over Outlet; diam. ___ in.
   Below Grade ___ in.
5. Inlet: Baffle [ ]; or Tee [ ]
6. Outlet: Baffle [ ]; or Tee [ ]
   Depth of outlet below inlet ___ in.
7. Depth of top of tank below finished grade 30 in.
8. Distances To:
   Well or Suction Line 50 ft.;
   Stream ___ ft.; Pressure Line ___ ft.;
   Property Line ___ ft.


C. DISTRICTION BOX
1. Material CON; No. available outlets 5.
2. Factory Built: Yes [X], (Company PRE CAST STED No [ ]
3. Dimension: Length ___ in.; Width ___ in. Depth ___ in.
4. Distance from Septic Tank ___ ft.
5. Serial Distribution: Yes [ ], No [X] (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: HALF ROUND
2. Lateral Lines: Depth below grade ___ in.
   Number 3; Length of each line 100 ft
   Total length of Laterals 210 ft.; CONNECTED
   Slope 4 in/100 ft. Diameter of pipe 16 in.; Shape O
   Material: concrete [ ]; fiber GLASS [X]
   asbestos [ ]; clay [ ]; other ___
   Distance between lateral lines ___ ft.
3. Trench Dimensions: Depth 60 in.; Width 48 in.
4. Filter Material: GRAVEL.
   Depth of material from trench bottom ___ in.
5. Distances To:
   Well or Suction Line 100 ft.;
   Stream ___ ft.; Pressure Line ___ ft.
   Property Line ___ ft.
6. Percolation Rate: 40 minutes/inch

TYPICAL SKETCHES

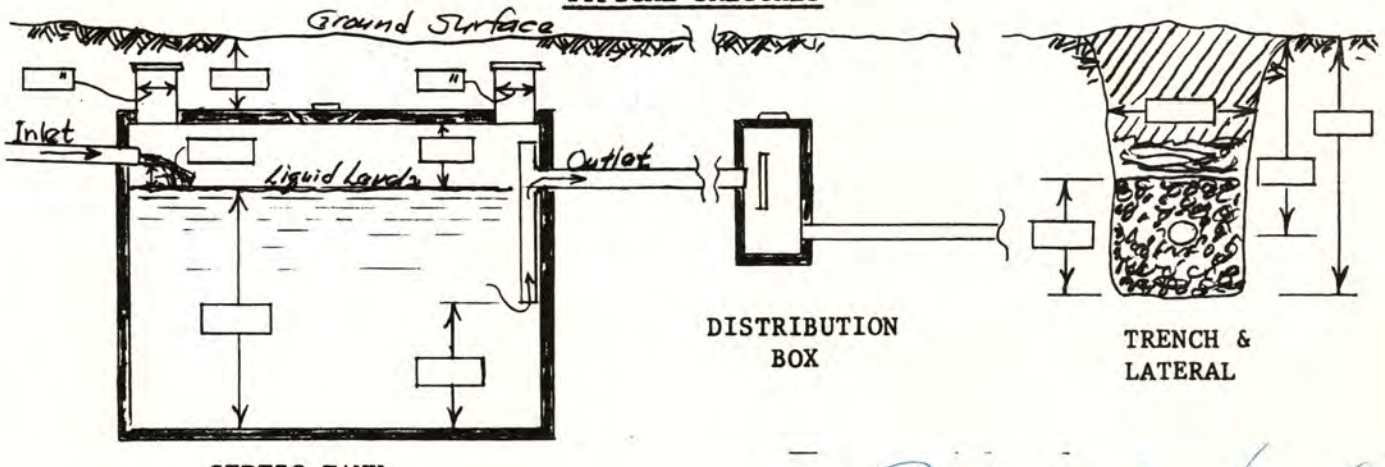

Bernard L. Hirsch
Signature of Applicant

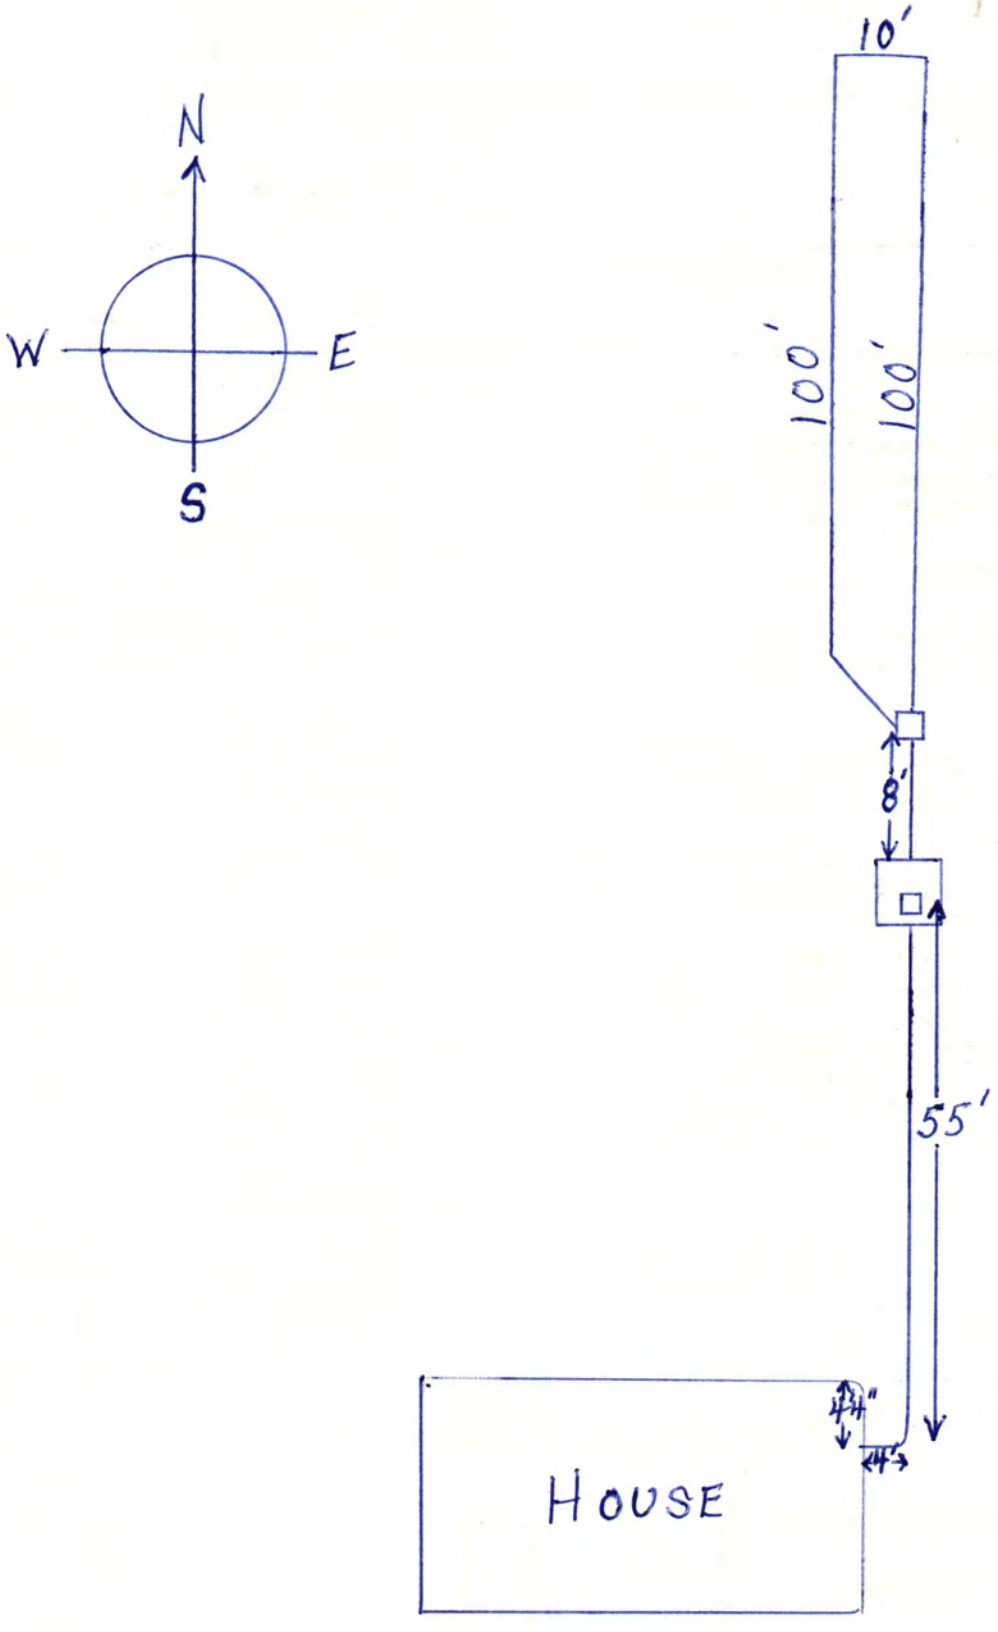
N
W
E
S
10'
100'
100'
8'
55'
4"
4"
HOUSE
