LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET
NON TRANSFERABLE

ENVIRONMENTAL HEALTH DIVISION
Lincoln, NE 68510-1514

(402) 441-8000

PERMIT

Permit

SEWAGE INSTALLATION
SEPTIC SYSTEM

No. 97380160401

Issued 06/26/97
Expires 12/26/97
Revenue Code 18754

Establishment

LEONARD DAHLGREN
T10N R6E SEC 30
CUSHMAN ADDITION
4313 W O STREET

FEES: $150.00

Permittee

LEONARD DAHLGREN
4301 W O ST
LINCOLN NE 68528

TOTAL $150.00

Issued By M. Jane Ford
Health Director

4936

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

A

Permit Number:

Sewage Disposal System

Request for Site Clearance and Permit

Include Form B, Form C and Applicable Fees with this Application.

☒ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

PLEASE PRINT OR TYPE

A. System Location (Indicate correct number and street)

Address 4313 West "O" (no rural route) City Lincoln NE, Zip 68528

Legal Description NE 1/4 (1/4) 30 (Section) 10N (Township) 6E (Range) All Block 4 Except East 100' Cushman Add. (Subdivision / Addition) (Block) (Lot)

Geographical Location (if known): Longitude _____ Latitude _____

☐ Check if system mail address is not the same as the owner's address

B. Owner

Name Leonard L. Dahlgren Signature Leonard L Dahlgren

Address 4301 West O City/State/Zip Lincoln, Nebr. 68528

☐ Check if owner designed system Home Phone 475-6634 Work Phone _____

C. Contractor

Name Friesen ex Company Name _____

Address 1961 pleasant hill Rd. City/State/Zip Lincoln NE

☐ Check if contractor designed system Work Phone 423-7076

D. Engineer/Installer ☐ Check and complete if engineer designed system

Designer Name _____ Firm _____ Work Phone _____

E. This System Will Serve a

☒ Residential Dwelling Number of Bedrooms _____ Is there a Whirlpool Bathtub YES NO

☐ Commercial Establishment/Other Facility Specify _____

Design flow in gallons per day _____ Type of Wastewater: ☐ Domestic ☐ Non-Domestic.

DO NOT WRITE BELOW THIS LINE

Approval Process ☒ Municipal Code 24.38 ☐ County Resolution No. 2832

1. **Health Department** Date rec'd 6/27/97 Date frwd 6/27/97 **ACTION** ☒ Approved ☐ Disapproved Signature Jerrold C. Hood
2. **Supt. Bldg. Insp. or Village Clerk** Date rec'd _____ Date frwd _____ **ACTION** ☐ Approved ☐ Disapproved Signature _____
3. **City or County Engineer** Date rec'd _____ Date frwd _____ **ACTION** ☐ Approved ☐ Disapproved Signature _____

Installation Final Written Approval

By Jerrold C. Hood

Date JULY 7, 1997

Business Office Use Only

Date Rec'd 6/27/97

Amt Paid 150 ⁰⁰

Rec'd By LS Cash/Check No. 13071

FORM 23-100 10-96 White - Health Dept. Yellow - Engineer Pink - Bldg. Inspector

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Sewage Disposal System

Preliminary Plan Specifications

Draw a plot plan showing system location, lines, distribution box, tank and laterals, percolation test hole locations, well, residence, compass direction and property lines. Indicate on drawing if residence and well are existing or proposed.

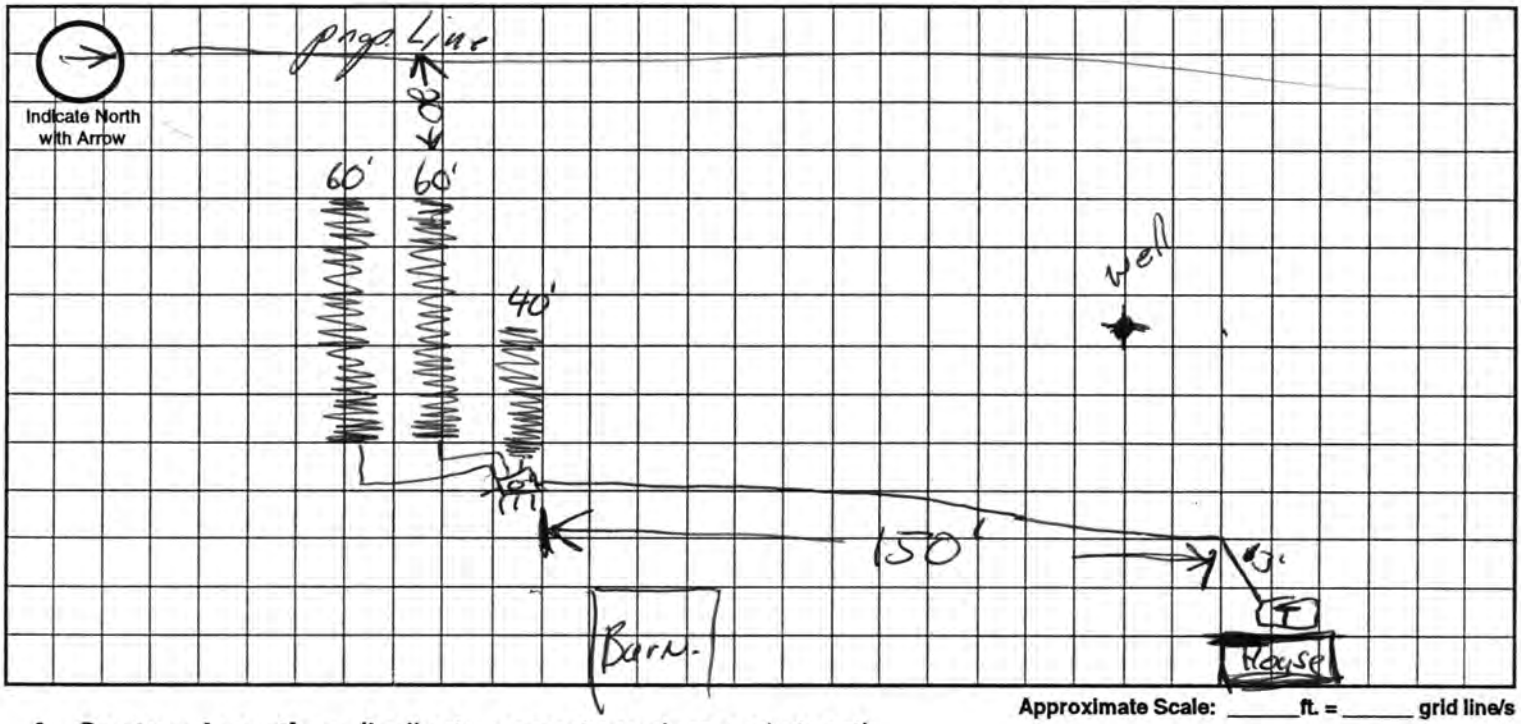

Approximate Scale: _____ ft. = _____ grid line/s

A. System Location (Indicate correct number and street)

Address (no rural route) 4313 West. O City Lincoln NE, Zip _____

B. Proposed Septic Tank/s

Tank Material: ☐ Concrete ☐ Plastic ☐ Other _____

C. Proposed Absorption System (See Form B for Percolation Information)

Percolation Rate _____ (min. per inch) Soil Type: _____ Land Slope: _____ %

Type of Absorption System: ☑ Trench ☐ Bed ☐ Other _____

Total Square Feet of Field Required: _____ sq. ft.

Type of Lateral: ☑ Half-Moon ☐ Perforated Pipe ☐ Other Lateral Material: _____

Capacity of Septic Tank _____ gals Number of Absorption Beds: _____ Number of Distribution Laterals per Bed _____

Total Length of Laterals 160 ft. Number of Trenches 3 Trench Width 4'

D. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	25 ☐	20 ☐	15 ☐	25 ☐	☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	30 ☐	20 ☐	30 ☐	40 ☐	☐
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

E. Required Signatures

Home Building Contractor _____ Date _____

Installer _____ Date _____

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System

As Built Plans & Specifications

Date _____

System Location (Indicate correct number and street)

Address 4313 West O (no rural route) City Lincoln NE, Zip _____

A. Building Sewer

1. Material: ~~plastic~~
   Diameter: _____ in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: _____ ft.
4. Number of clean-outs: _____
5. Distances to: well or suction line _____ ft.
   stream _____ ft.
   pressure line _____ ft.
   property line _____ ft.

B. Septic Tank

1. Material: _____
   Number of compartments: _____
2. Capacity: _____ gal.
3. Factory built: ☐ Yes ☐ No
4. Manholes: Over inlet, diameter _____ in.
   Over outlet, diameter _____ in.
   Riser: ☐ above ☐ below grade _____ in.
5. Inlet: ☐ baffle ☐ tee
6. Outlet: ☐ baffle ☐ tee
7. Depth to top of tank, below unfinished grade: _____ in.
8. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.

C. Distribution Box

1. Material: plastic
   Number available outlets: 7
2. Factory built: ☑ Yes ☐ No
3. Distance from septic tank: 170' ft.

D. Absorption Field

(Provide as-built drawings on back of this form)

1. Type: ☑ Half rounds ☐ Perforated pipe
   Diameter of half round: 12"
   or perforated pipe: _____
   Material: ☐ fiberglass ☑ plastic ☐ concrete
   ☐ other _____
2. Lateral lines: Number 3
   Length of each line: ~~40~~ 60 ft. 60 ft.
   60 ft. _____ ft., _____ ft.
3. Trench dimensions: Width 4 ft.
   Slope 2- in/100 ft.
   Average depth 36 in
4. Filter material: Gravel
   Depth of material 20+ in.
5. Distances to: Well or suction line 100+ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line 20 ft.

Indicate North with Arrow

Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

