LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

3140 "N" STREET Lincoln, NE 68510-1514 (402) 441-8000

NON TRANSFERABLE

PERMIT

No. 94380121001

Permit
SEWAGE INSTALLATION

Issued 08/22/94
Expires 02/22/95
Revenue Code 18754

Establishment
JIM BESCHEINEN
T11N R6E SEC 35
400 HUMPHREY STREET

FEES: $150.00

TOTAL $150.00

Permittee
JIM BESCHEINEN
5111 JUDSON ST
LINCOLN NE 68504

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE: 8-18-94

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 11N ; Range 6E ; Section 35 ;
   Block_____ : Lot_____ : Addition See Attached
   Street Address 400 Humphrey

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe_____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐

4. Distance to public sewer: _____ft.

Jim Beschorner
Signature of Applicant (Owner or Lessee)

5111 Judson
Address

430-6500 Cellular
466-5763 Home

(Do not write below this double line)

1. Health Department: Date Rec'd. 8/19/94. Date Frwd. 8/19/94. ACTION: Approved ☑ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 8/19/94. Date Frwd. 8/19/94. ACTION: Approved ☒ Disapproved ☐ Signature: Gary Lyon
3. City or County Engineer: Date Rec'd._____. Date Frwd._____. ACTION: Approved ☑ Disapproved ☐ Signature: Stephen J. Fitz

REMARKS OR REASONS FOR DISAPPROVAL_____

Site Visits:
Date: 9-9-94 by: RM
Date:_____ by:_____
Date:_____ by:_____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 9-9-94 By: Ron Mayard

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township _____; Range _____; Section & ¼ Section _____.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☑ ; Clay Loam ☐ .
Dates of Tests: 8/13/94 to 8/14/94. Weather: Precip dry Temp. 90°.

OWNER: _____

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	28	8/13	10:00	8/14	10:00	8/14	12:00	6"	12:30	4¾	30	1¼	
2	30	"	"	"	"	"	"	"	"	5	"	1	
3	26	"	"	"						4½		1½	
4	30	"	"	"						5		1	
5	24	"	"	"						4¼		1¾	
6	28	"	"	"						4½		1½	

John A Stuhmyer
Signature of Person Conducting Test

Address 9811 N.W. 40th Phone 437-6023

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Approved Percolation Rate (a)
A. 23 min./inch
B. _____ min./inch
C. _____ min./inch

Remarks: _____
Soil Type (SCS): Sharpsburg Silty Clay Loam
Date: August 19, 1994

Gerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. _____

Indicate on sketch if residence and well are exisiting or proposed.

REVIEWING ACTION

Remarks: _____

Date: August 19, 1994

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed 665 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 9-9-94

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material C ; Diameter ____ in.
2. Distance above basement floor ____ in., or below basement floor ____ in.
3. Distance between dwelling and septic tank 147 ft.
4. Number of clean-outs 2.
5. Distances to: Well or Suction Line 97 ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐ (Company ____)
4. Manholes: Over Inlet; diam. ____ in. Over Outlet; diam. ____ in. Riser Above ☐ Below ☐ Grade 0 in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to: Well or Suction Line 129 ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.


C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets ____.
2. Factory Built: Yes ☑ No ☐ (Company ____)
3. Distance from Septic Tank 4.5 ft.


D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☒ Diameter of Half Round ____ or Perforated Pipe ____. Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other ____.
2. Lateral Lines: Number 2 ; Length of each line ____, 100, 75, ____, ____ ft.; Total length of laterals 175 ft.; Distance between lateral lines 20 ft.
3. Trench dimensions: Width 4 ft.; Slope 0-6 in/100 ft.; Average Depth 24 in.
4. Filter Material: ____ Depth of Material ____ in.
5. Distances to: Well or Suction Line more than 100 ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

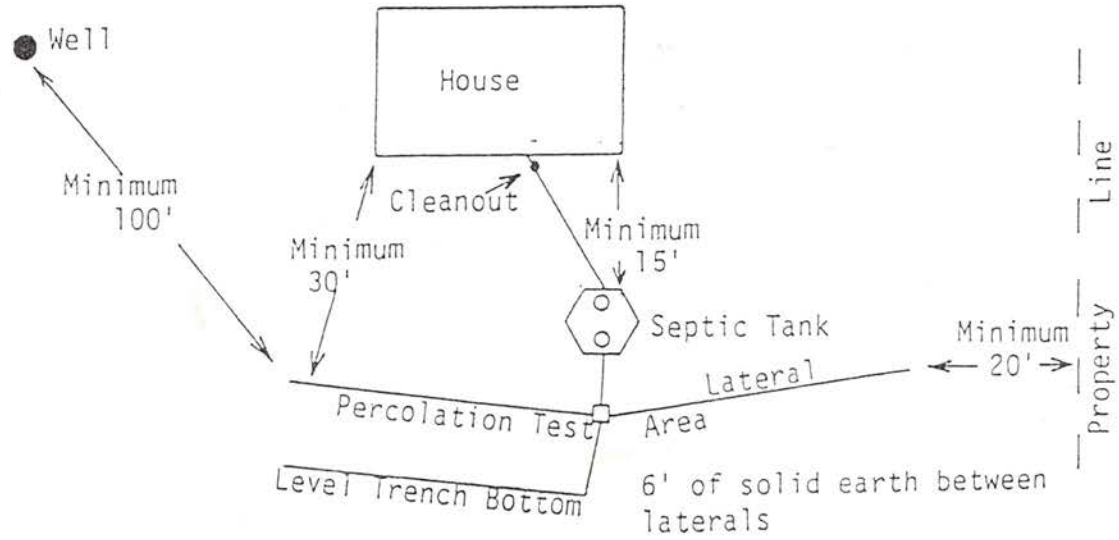

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

N

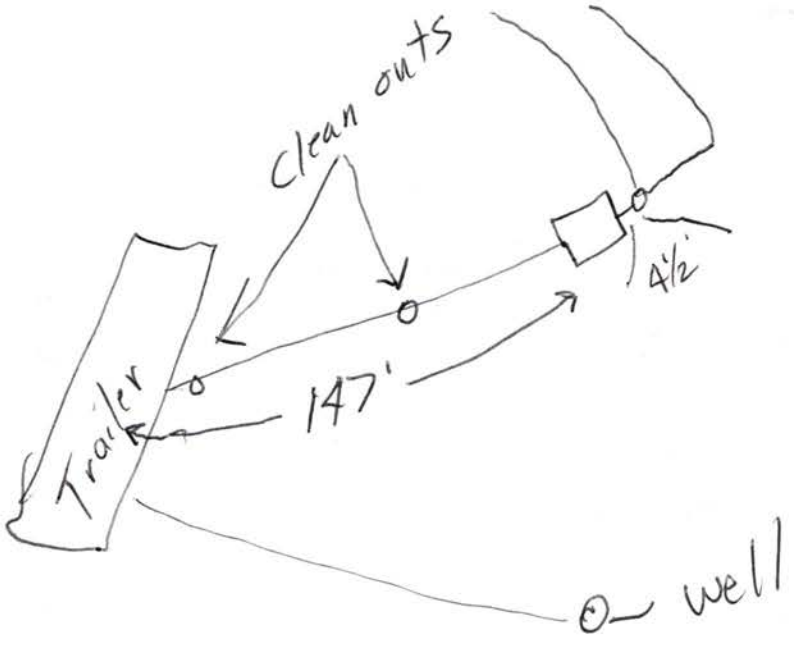

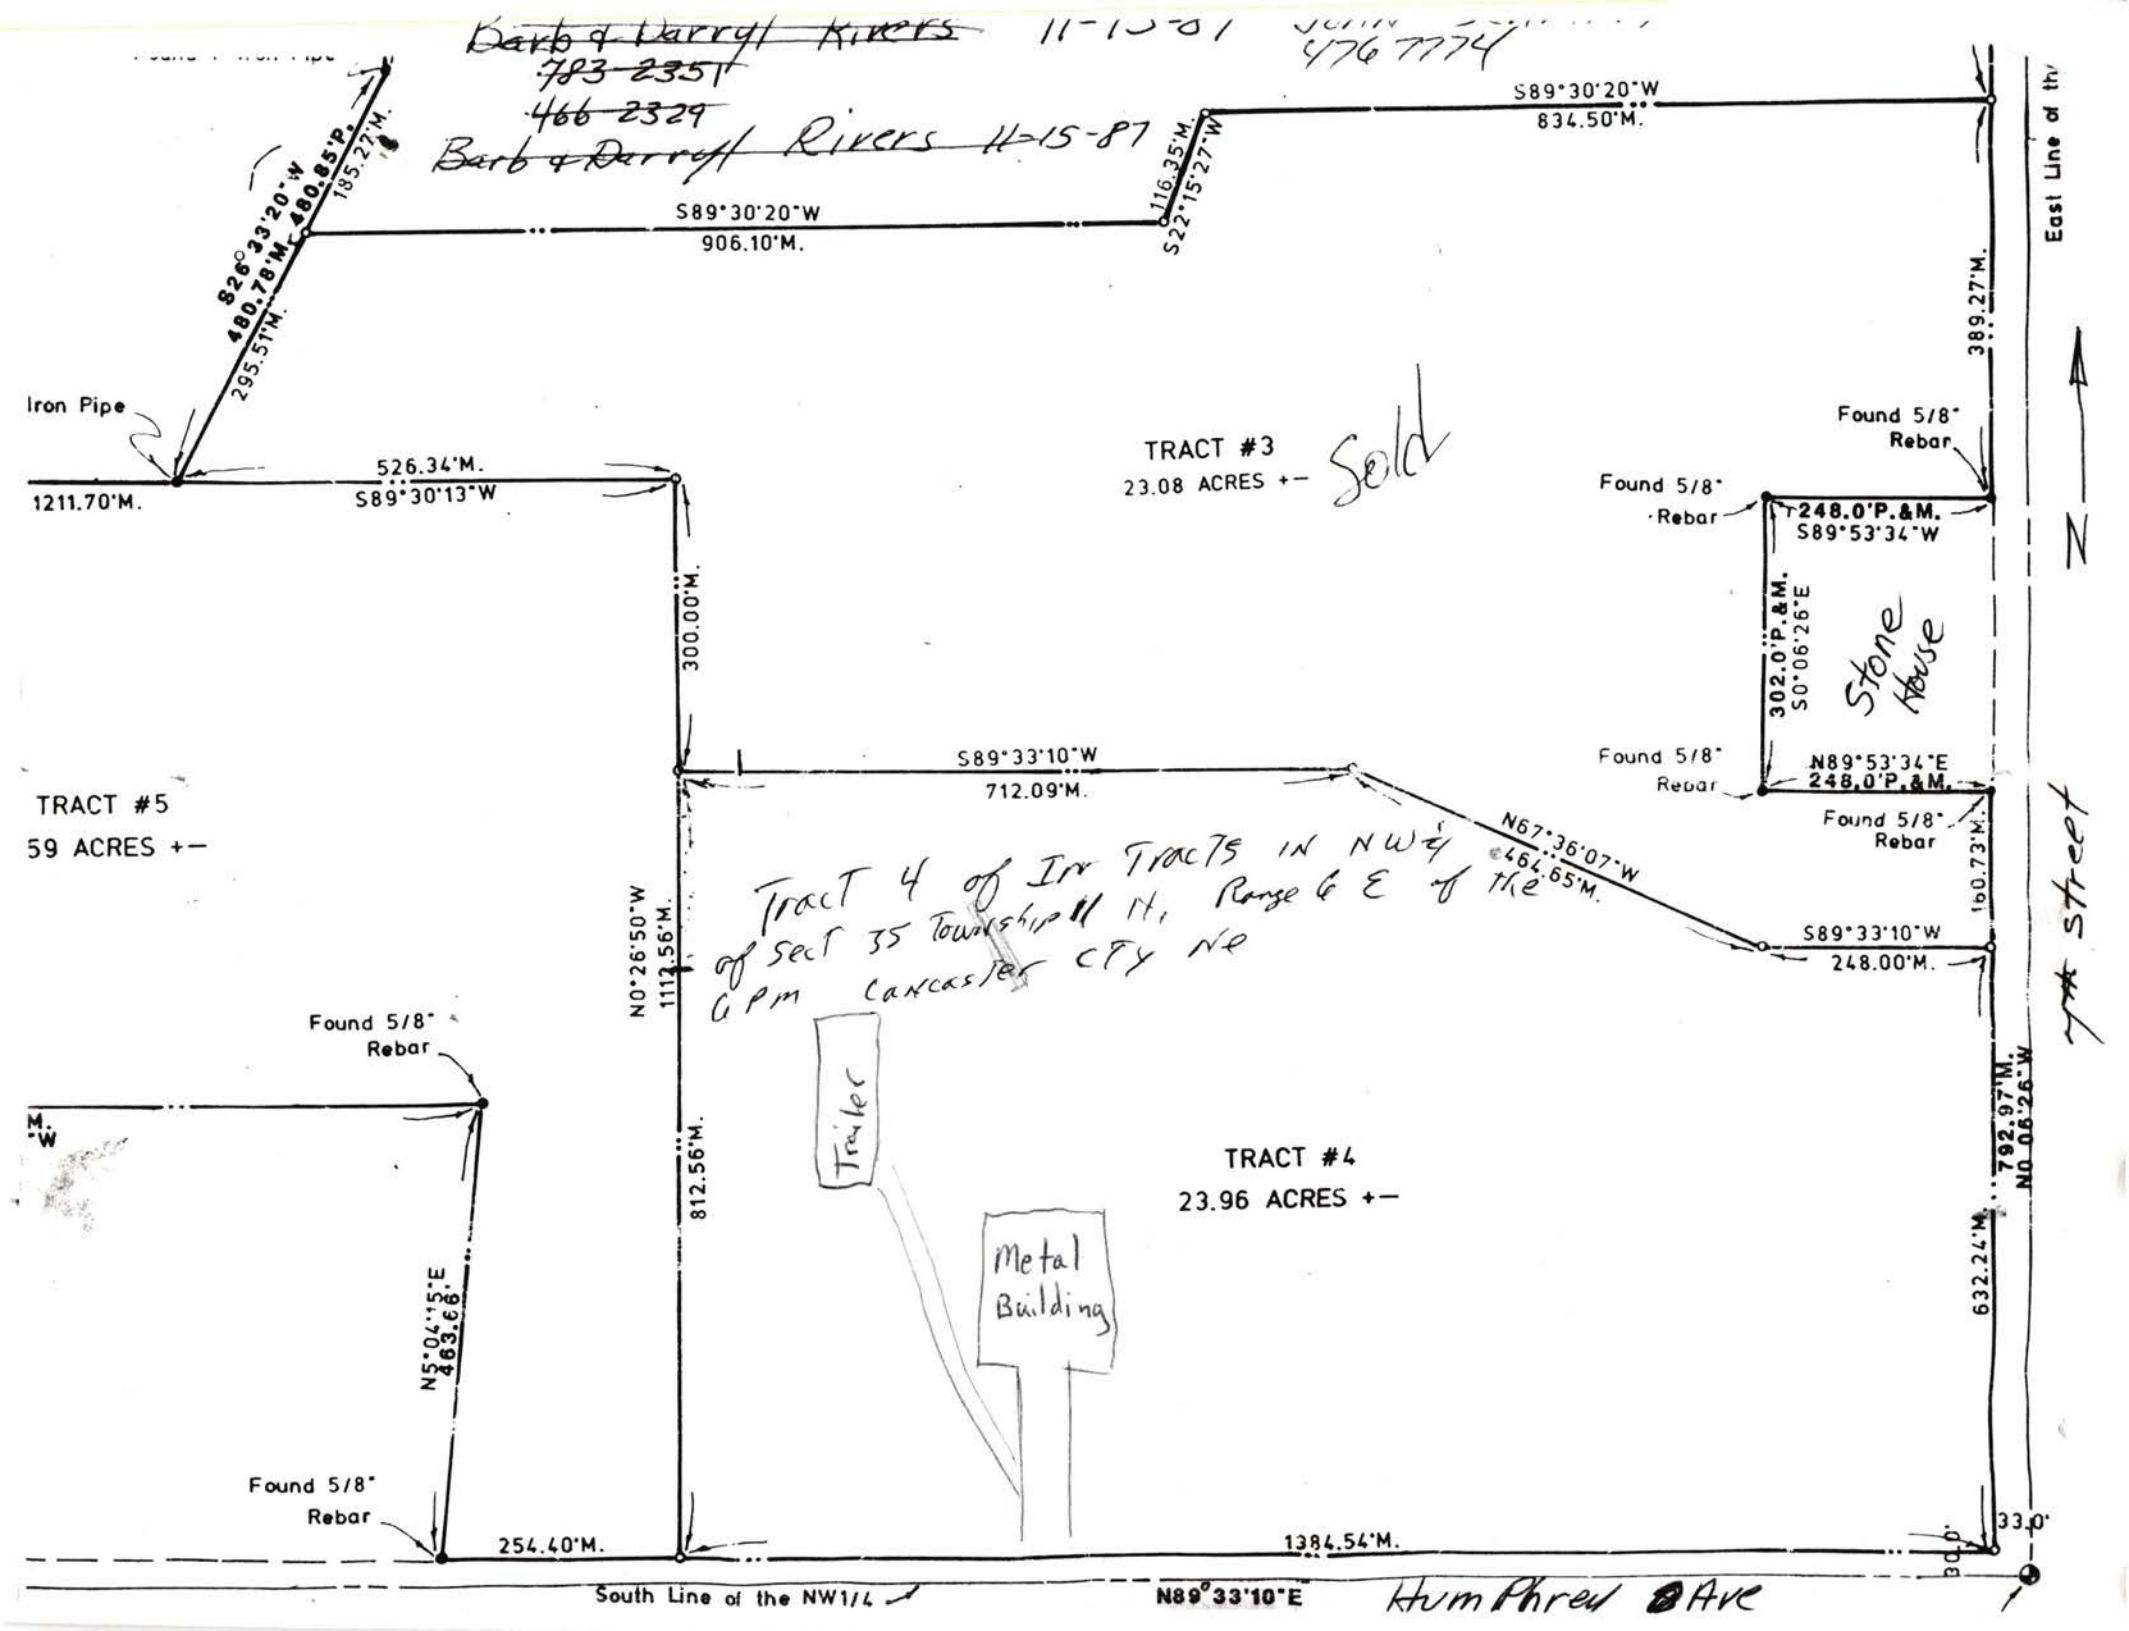
~~Barb & Darryl Rivers~~ 11-15-87
~~783-2351~~
~~466-2329~~
~~Barb & Darryl Rivers 11-15-87~~
476 7774
S89°30'20"W
834.50'M.
East Line of the
S89°30'20"W
906.10'M.
116.35'M.
S22°15'27"W
185.27'M.
S26°33'20"W
480.78'M. 480.85'P.
295.51'M.
389.27'M.
Iron Pipe
TRACT #3
23.08 ACRES +-
Sold
Found 5/8" Rebar
526.34'M.
S89°30'13"W
1211.70'M.
Found 5/8" Rebar
248.0'P.&M.
S89°53'34"W
302.0'P.&M.
S0°06'26"E
Stone House
300.00'M.
S89°33'10"W
712.09'M.
Found 5/8" Rebar
N89°53'34"E
248.0'P.&M.
Found 5/8" Rebar
160.73'M.
N67°36'07"W
464.65'M.
TRACT #5
59 ACRES +-
Tract 4 of Irr Tracts in NW¼ of Sect 35 Township 11 N, Range 6 E of the 6 PM Lancaster CTY NE
N0°26'50"W
1112.56'M.
S89°33'10"W
248.00'M.
Found 5/8" Rebar
Trailer
TRACT #4
23.96 ACRES +-
Metal Building
812.56'M.
792.97'M.
N0°06'26"W
632.24'M.
N5°04'15"E
483.66'
Found 5/8" Rebar
254.40'M.
1384.54'M.
33.0'
33.0'
South Line of the NW1/4
N89°33'10"E
Humphrey Ave
N
71st Street
