FILE #2450

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION	AUGUST 9, 1987
TYPE OF LICENSE OR PERMIT	THIS LICENSE OR PERMIT EXPIRES
PHIL WHITEFOOT — 5101 "J" STREET	LINCOLN, NE 68510
LICENSEE OR PERMITTEE	ADDRESS
TION: R7E: Sec 14: SE¼: Lot 36 I.T.: 9300 Holdrege	
NAME OF ESTABLISHMENT, IF ANY	ADDRESS

REMARKS: NON TRANSFERABLE NEW CONSTRUCTION

PERMIT	ACCOUNTING NUMBER	TOTAL
$ 60.00	018754	$ 60.00

Valid Receipt Only if Machine Receipted In This Space

Serial No. — Date and Amount

APPLICATION

HEALTH

ISSUING OFFICER OR DEPARTMENT

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2450

DATE: 1-30-87

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 10 N ; Range 7 E ; Section 14 SE/4;
   Block _____ : Lot 36 I.T. : Addition _____
   Street Address 9300 Holdrege

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: NA ft.

Phil Whitehurst Brad Smithurst
Signature of Applicant (Owner or Lessee)

5101 J St Hickman, Ne 68372
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. ~~2/9/87~~ . Date Frwd. ~~2/9/87~~ . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 2/9/87 . Date Frwd. 2/9/87 . ACTION: Approved ☒ Disapproved ☐ Signature: Walt Kelly

3. City or County Engineer: Date Rec'd. 2/9/87 . Date Frwd. 2/9/87 . ACTION: Approved ☒ Disapproved ☐ Signature: Dennis Bartels

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: Jan-87 by: rm
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: Feb-9-87 By: Ron Maynard

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. 2450

PROPERTY WHERE SOIL TESTED:

Location: Township 10N; Range 7-E; Section & ¼ Section 14 SE 1/4
Property Dimensions: 380 ft. x 540 ft. Area: 5.217 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐; Silty Clay Loam ☒; Sandy Loam ☐; Silt Loam ☐; Clay Loam ☐.
SHC
Dates of Tests: 11-28-86 to 11-29-86. Weather: Precip. Ø Temp. 60.

OWNER: Philip Whitefoot
Address: 5101 J st. Lincoln Ne. 68510

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End		Elapsed	Water	Percolation
Hold No.	Hole Depth (in.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Water Level (in.)	Time (Hr./Day)	Water Level (in.)	Time (Min.)	Level Drop (in.)	Rates (Min./in.)
1	36"	11/28	11:00 AM	11/28	6:00 PM	11/29	3:30 PM	6"	4:00 PM	3½	30	2½	12
2										4½		1½	20
3										4¼		1¾	17.15
4										5		1"	30
5										2¼		3¾	8
6										1⅞		4⅛	7.27

Philip Whitefoot
Signature of Person Conducting Test

Address 5101 J st. Lincoln Ne 68510 Phone 483-1810

Sum of Percolation Rates: 94.42
Average of Rates: 15.74
Mean of Rates:

(Do not write below this line)

REVIEWING ACTION

Remarks: Probably a little fast for Marshall Silty Clay Loam
Soil Type (SCS): Marshall Silty Clay Loam
Date: FEBRUARY 9, 1987

Approved Percolation Rate (a)
A. 12 min./inch
B. _____ min./inch
C. _____ min./inch

Gerald C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. 2450


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Fiberglas; No. of compartments 1.
2. Capacity 1,000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Corr A Glas)
4. Manholes: Over Inlet; diam. 12 in.
Over Outlet; diam. 12 in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☒
7. Depth of top of tank below finished grade 24 in.
8. Distances to:
Well or Suction Line 155 ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Plastic; Number - available outlets _____.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank 8 ft.


D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4".
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 4; Length of each line 100, 80, 80, 65, _____ ft.;
Total length of laterals 325 ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 3 ft.;
Slope 4.5 in/100 ft.; Average Depth 38 in.
4. Filter Material: Road Gravel
Depth of Material 15-18 in.
5. Distances to:
Well or Suction Line 160 ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

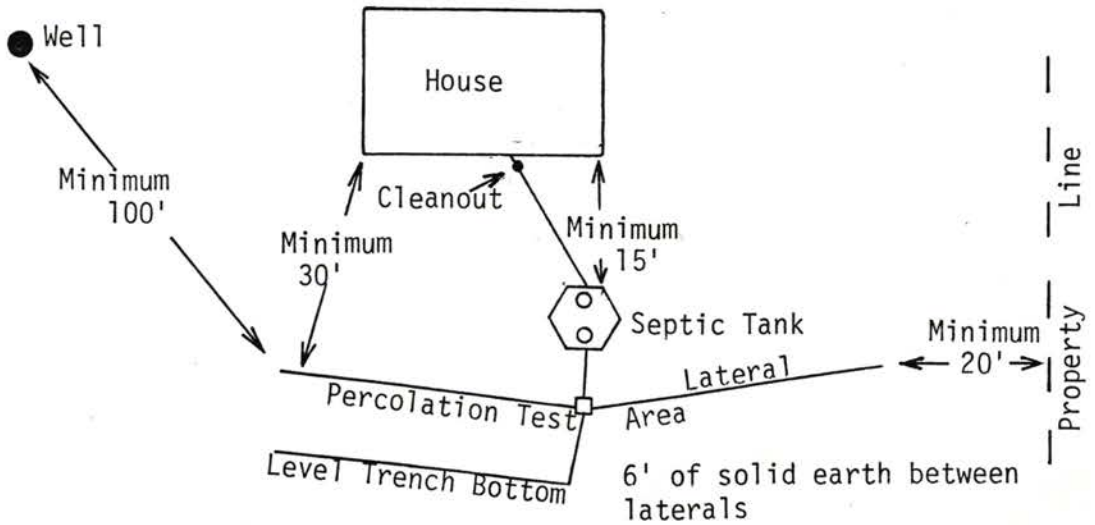

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN


AS BUILT DRAWING OF SYSTEM

DATE 1-30-87 INSTALLER Southwick Sewer & Drain

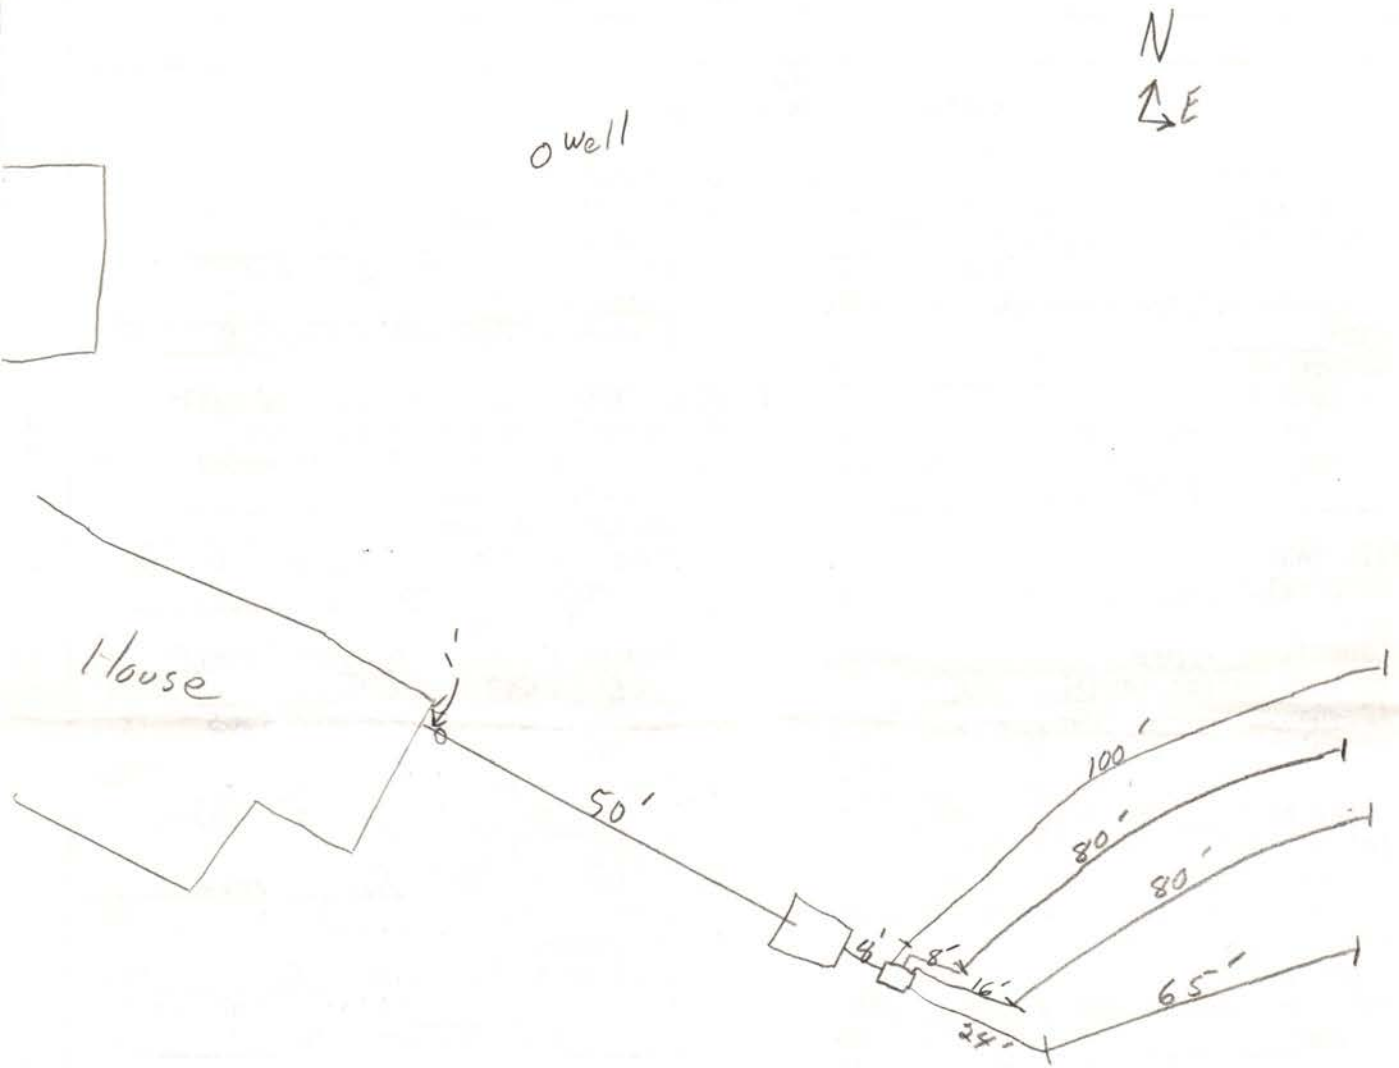

W-179

N

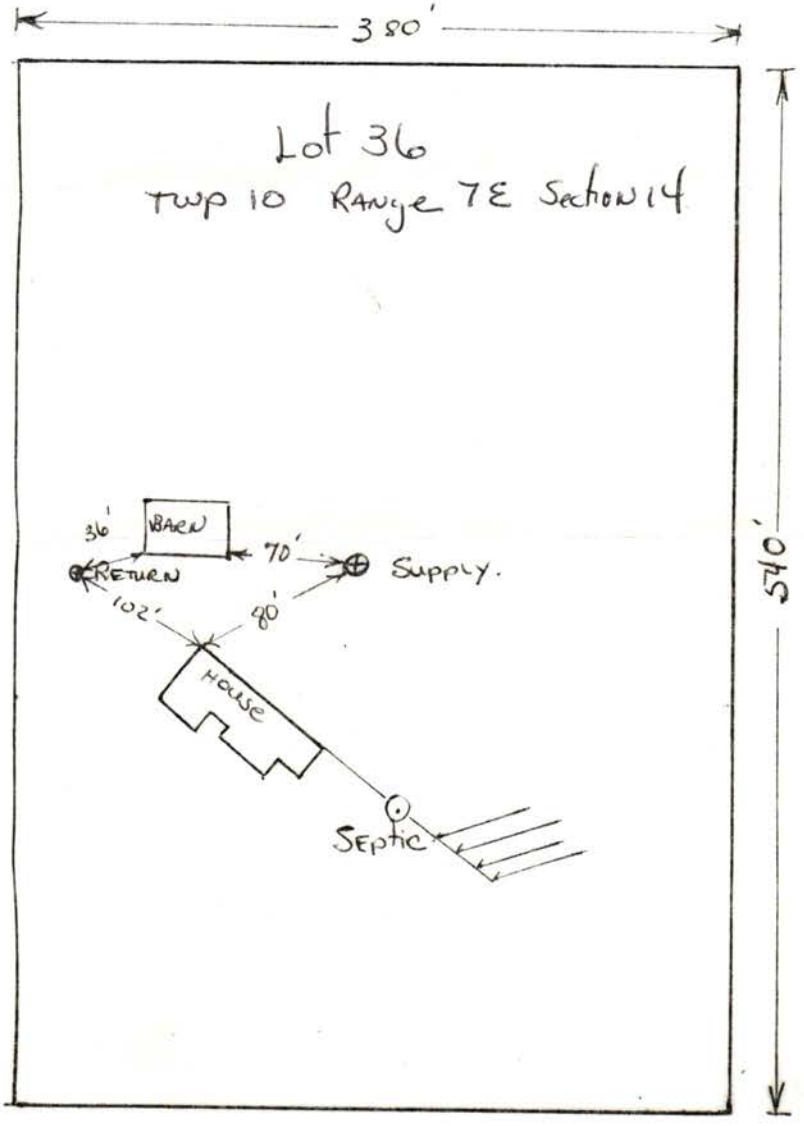

P. Whitefoot
