LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET ENVIRONMENTAL HEALTH DIVISION Lincoln, NE 68510-1514 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit

SEWAGE SYSTEM REPAIR

No. 95390048701

Issued 12/21/95
Expires 06/21/96
Revenue Code 18754

Establishment

BRAD SOUTHWICK
T11N R6E SEC 16
LOT 1
10600 NW 27 STREET

FEES: $50.00

TOTAL $50.00

Permittee

BRAD SOUTHWICK
17201 S 72 ST
HICKMAN NE 68372

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

Lincoln-Lancaster County HEALTH DEPARTMENT

3140 "N" STREET LINCOLN, NE 68510-1514

FILE NO. _____

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 12-12-95

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☐, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 11N ; Range 6E ; Section 16 SW¼ ;
Block _____ ; Lot 1 ; Addition _____
Street Address 10600 NW. 27th St.
David Steinheider

2. Property Use: Residential _____ ☐; Commercial _____ ☐
No. Bedrooms 3 Describe _____
Other Use ☐
Describe _____

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: Installed 65' subsurface lateral 3 ft wide

5. Work to be done by: Owner ☐ ; or Contractor ☐ , _____
Contractor's Name

6. Estimated cost of project:

a. Materials	$	
b. Labor	$	
c. Other	$	
TOTAL	$ >400	00

Brad Southwick
Signature of Applicant (owner or lessee)

17201 S. 72nd
Address Hickman, NE 68372

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd: 12-14-95
Filing Fee: $ 450 ck

2. Site Visits:
Date: 12-13-95 by: mm
Date: _____ by: _____
Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐
by: Ron Magnuson

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 12-15-95 by: Ron Magnuson

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

Lincoln-Lancaster County Health Dept.
3140 "N" Street
Lincoln, NE 68510

D

DATE: 12-12-95

FILE NO: _____

10600 NW 27 Lincoln

Dave Steinheider


SPECIFICATIONS AS BUILT

A. BUILDING SEWER: Sch 40
1. Material PVC ; Diameter 4" in.
2. Distance above basement floor _____ in., or below basement floor 9 in.
3. Distance between dwelling and septic tank 60 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line > 50 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line > 20 ft.


B. SEPTIC TANK:
1. Material C-Crete ; No. of compartments _____.
2. Capacity Approx 1100 gals.;
3. Factory Built: Yes ☐ No ☒
(Company _____)
4. Manholes: Over Inlet; diam. 10 in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☒ Grade 4 in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☒
7. Depth of top of tank below finished grade 30 in.
8. Distances to:
Well or Suction Line > 50 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line > 20 ft.

C. DISTRIBUTION BOX: (2)
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank 15 + 42 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4" .
Material: fiberglass ☐ ; plastic ☒ (2)
concrete ☐ ; other orangeburg (2) .
2. Lateral Lines:
Number 4 ; Length of each line 60 , 60 , 40 , 65 , _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines _____ ft.
3. Trench dimensions: Width _____ ft.; Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: _____
Depth of Material _____ in.
5. Distances to:
Well or Suction Line > 100 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line > 20 ft.

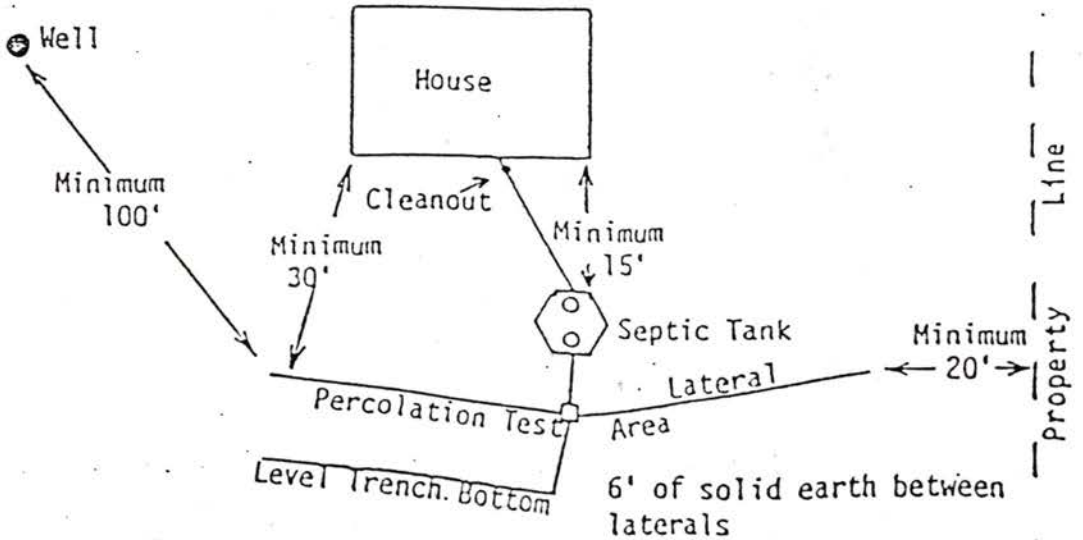

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

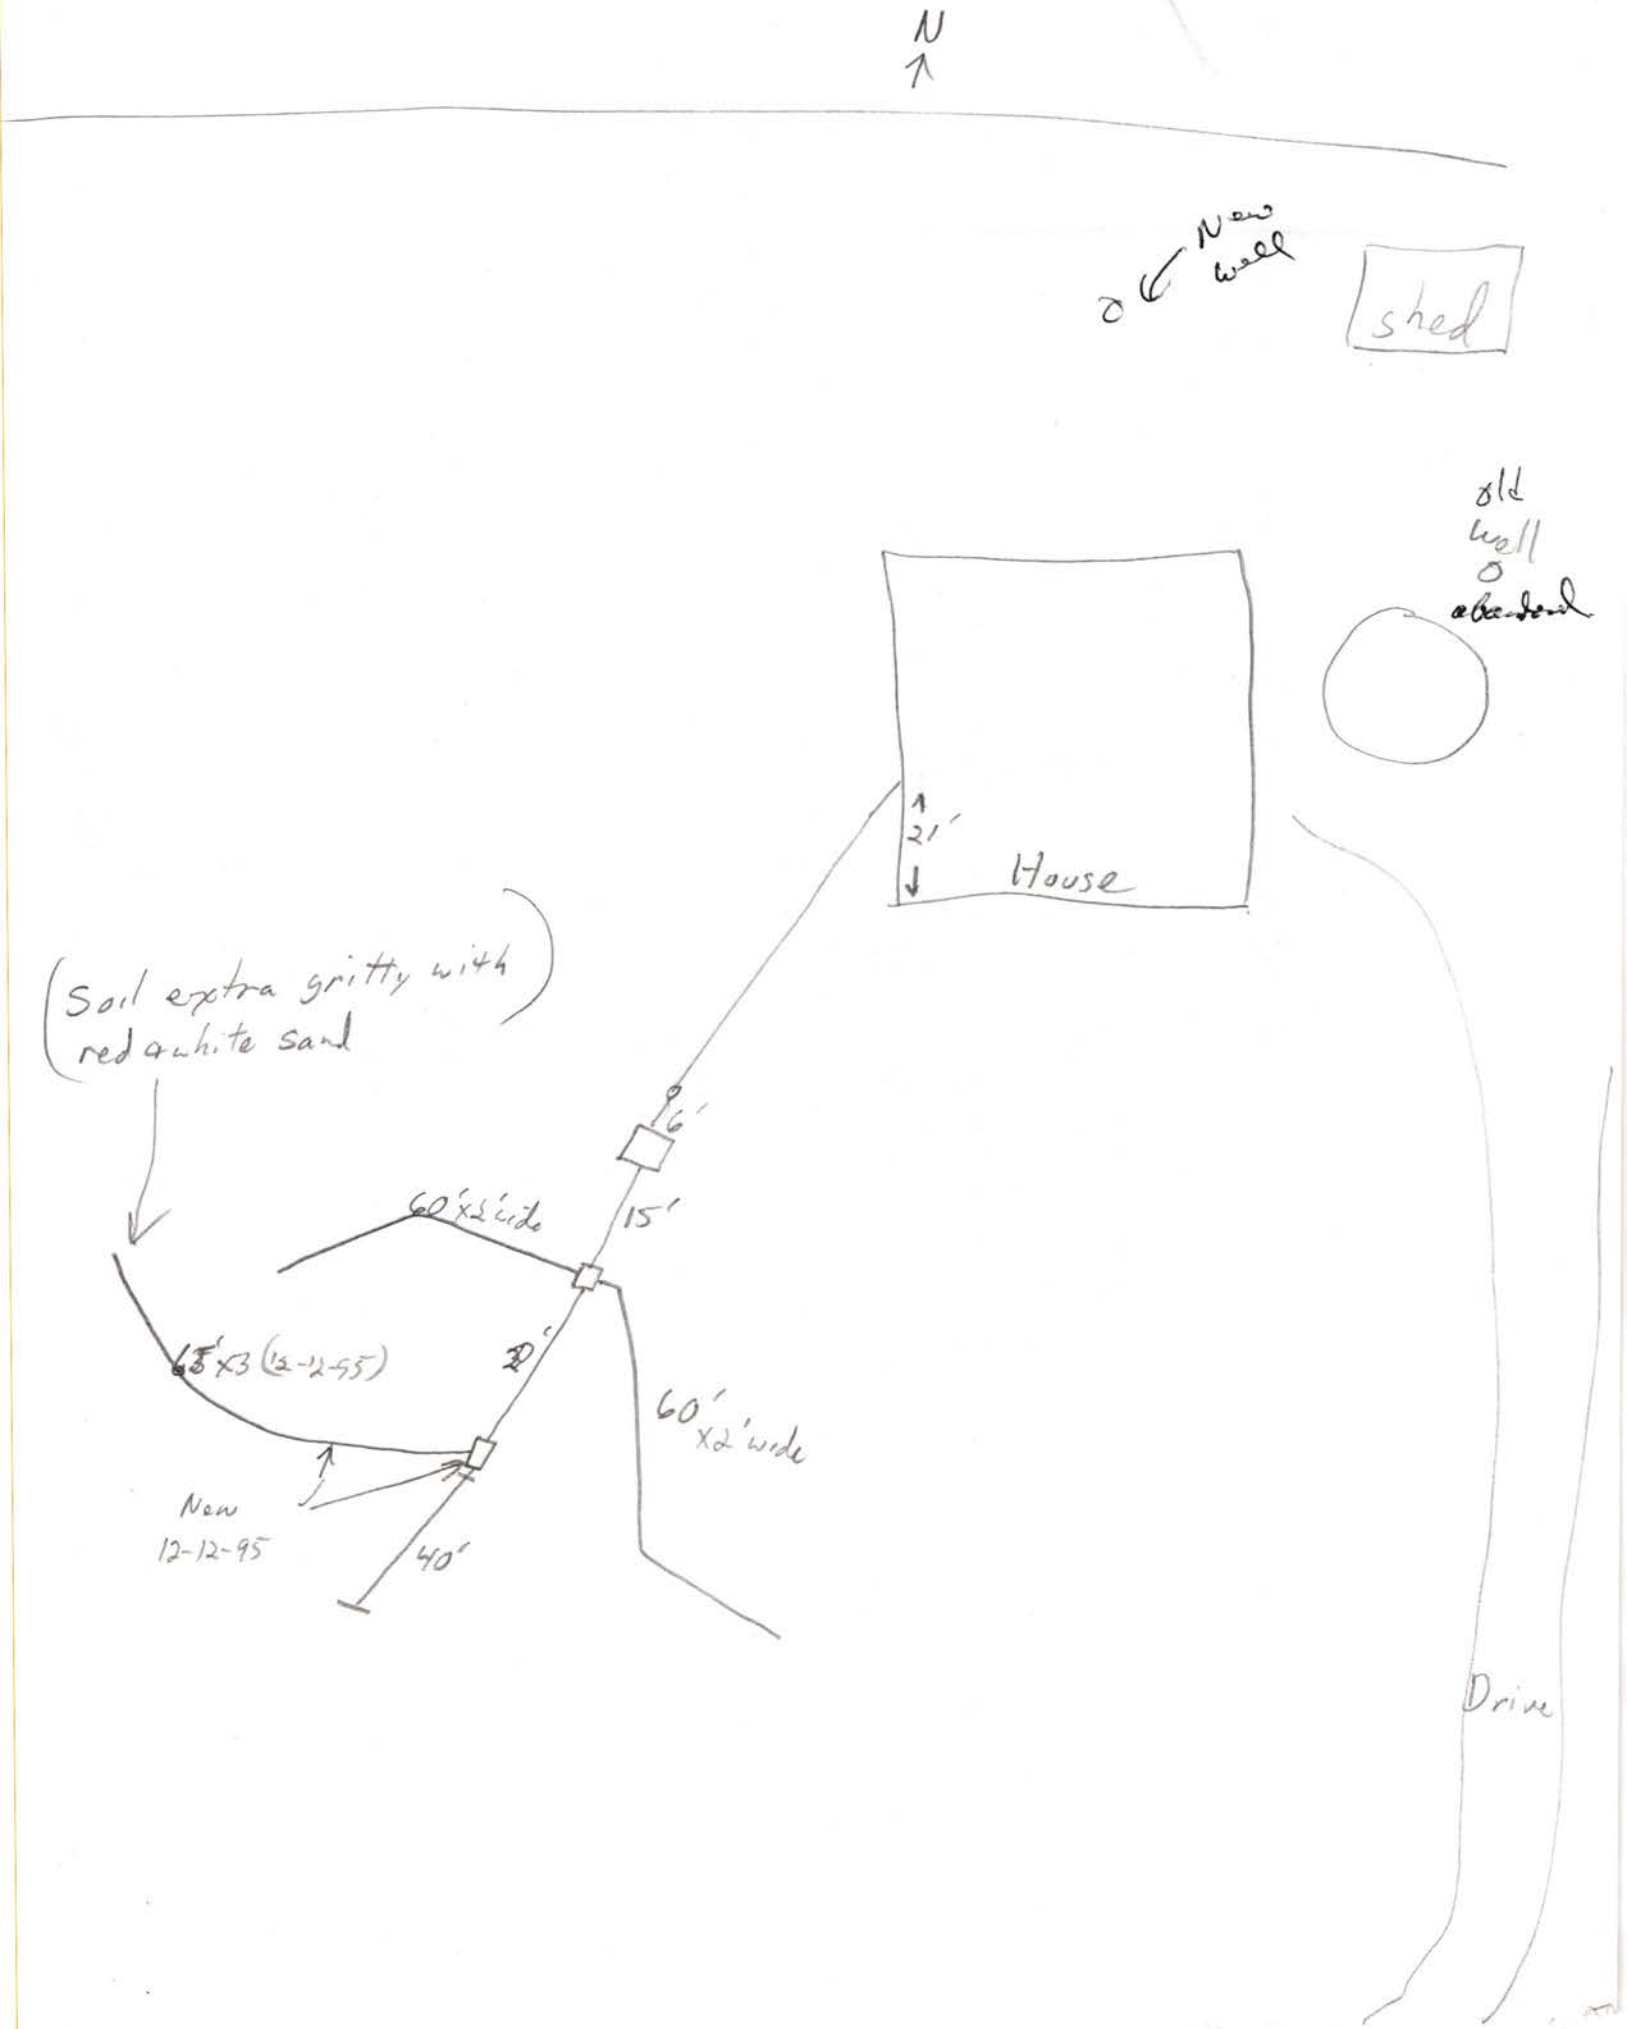
N
New well
shed
old well abandoned
House
21'
(Soil extra gritty with red white sand)
6'
15'
60' x 2' wide
20'
60' x 2' wide
New 12-12-95
40'
Drive



W. Blue Rd

NW 22nd — septic Repair

Lincoln-Lancaster County Health Department

3140 "N" ST. **2200 St. Mary's Avenue, Lincoln, Nebraska 68502 Phone: 441-8022**

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☒ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☐ Evaluation of the Individual Water System ☒ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address 10600 N.W. 27th ST - LINCOLN

Twp 11N Range 6E Section 16 1/4 SW 1/4 ___ Block ___ Lot 1 Addition ___

Directions to Property N.W. 27th & BLUFF RD - 3+ MILES No. of KAWASAKI PLANT - SITS BACK ON HILLSIDE ON EAST SIDE OF ROAD. YELLOW HOUSE - LONG DRIVEWAY

Location of Well NE Corner of House Tap Location: Inside ☐ Outside ☒ No of Windmills

Location of Sewage System West side of House (SW) Year Installed Laterals Added 3 years ago

(laterals run N W & SE)

	NAME	ADDRESS	PHONE
Present Owner:	DAVID STEINHEIDER	10600 N.W. 27th ST. LINCOLN, NE	470-3160 Home 434-1730 Ofc
Tenant/Buyer:	DURWARD & ARLENE SMITH	921 Cobblestone Drive Lincoln, NE 68510	486-1940 Home
Return to:	LARRY OWEN FAX 436-3399 (Fax 486-3633 Helen Tyler 436-3232 of WHY USA Harrington Realty	107 Hedgewood Drive LINCOLN, NE 68510	483-4141

Signature of Applicant Arlene Smith Address 921 Cobblestone Dr. Lincoln, NE 68510 Date 11/28/95

HEALTH DEPARTMENT USE ONLY

Date Received 11/29/95 Received $150.00 Check ☒ 3966 Cash ☐

PRELIMINARY STATUS--By Ron Marquart **DATE:** 11/29/95

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM	Additional Site Visits
Construction	☒	☒ corrected	Approved ☐	Date 12/11/95 by mm
Bacteria	☒ 0 /ml	☐ ___ /ml	Provisional ☒	Date 12/14/95 by mm
Nitrate	treated ☒ 0.3 ppm	☒ 14.6 ppm	Disapproved ☒ corrected	Date ___/___/___ by ___

Comments: An additional 65 Ft of subsurface lateral 3 ft wide has been installed to correct a sewage disposal violation of the original septic system. There is no record of permit or inspection of the original septic system. Thus, a provisional approval ☐ See Attached Letter

---

FINAL STATUS

WATER SYSTEM: Approved:* ☒ **SEWAGE DISPOSAL SYSTEM** Approved: ☐ Provisional Approval: ☒

Approved by Ron Marquart, RS Date 12/18/95

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

* Approval applies to treated water only for nitrate. Raw water must not be used for infant feeding.
