LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1737-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION
TYPE OF PERMIT

May 9, 1981
THIS PERMIT EXPIRES

William Benischek RR# 5, Lincoln Ne
ISSUED TO ADDRESS

T11N, R6E, Section NW ¼ SECTION 17
LEGAL DESCRIPTION

REMARKS: Must not be in 100 year flood plain and must meet special construction standards-----Contact Health Dept. for Standards

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY DATE AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $60.00

FILE NO. 1737-C

DATE: December 3, 1980

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: SEE ATTACHED
   Twp. 11N ; Range 6 E ; Section NW ¼ Sec 17
   Block _____ : Lot _____ : Addition _____
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

X Merrill K. Bruscke
Signature of Applicant (Owner or Lessee)

RR #5, Lincoln, Nebraska
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 12/9/80. Date Frwd. 12/9/80.
   ACTION: Approved ☐ Disapproved ☒ MUST MEET SPECIAL CONSTRUCTION X
   Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 12-9-80. Date Frwd. _____.
   ACTION: Approved ☒ Conditional Disapproved ☐
   Signature: Gary Sherman

3. City or County Engineer: Date Rec'd. 12-9-80. Date Frwd. 12-9-80.
   ACTION: Approved ☒ Disapproved ☐
   Signature: Henry Krafft

REMARKS OR REASONS FOR DISAPPROVAL LOCATED IN AREA THAT IS OCCASIONALLY FLOODED.

Site Visits:
Date: 1-26-81 by: DM * *Shallow lateral installation
Date: _____ by: _____
Date: _____ by: _____

Note: Must be out of 100 yr. Flood or Elevated to avoid impairment of S.W.S.

INSTALLATION FINAL WRITTEN APPROVAL
Date: 1-27-81 By: Ron Morgan

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20105-0477 FERGUSON
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 11 N ; Range 6 E ; Section & ¼ Section 17 NW ¼
Property Dimensions: _____ ft. x _____ ft. Area: 9.06 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☒ ; Clay Loam ☐ .
Dates of Tests: 12-2-80 to 12-3-80. Weather: Precip. 0 Temp. 30°.

OWNER: X [illegible] Rt #5
Address: Lincoln, Nebraska

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	32"	12-2	4³⁰ PM	12-3	8³⁰ AM	12-3	8³⁰ AM	12"	12⁰⁰ N	7	30	1½	
2										1		2½	
3										5		1½	
4										8		1	
5										2		1½	
6										10		1	
	REFILLED HOLES					#1	10³⁰ AM		#2	9³⁰ AM			
						#3	10⁰⁰ AM		#4	10³⁰ AM			
						#5	9³⁰ AM		#6	11⁰⁰ AM			

Dennis LaPoe
Signature of Person Conducting Test

Address ACE CAST STEP CO. Phone 464-0638

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: DANGER OF FLOODING
Soil Type (SCS): Kennebec Silt Loam
Date: December

Approved Percolation Rate (a)
A. 20 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. _____

Indicate on sketch if residence and well are exisiting or proposed.

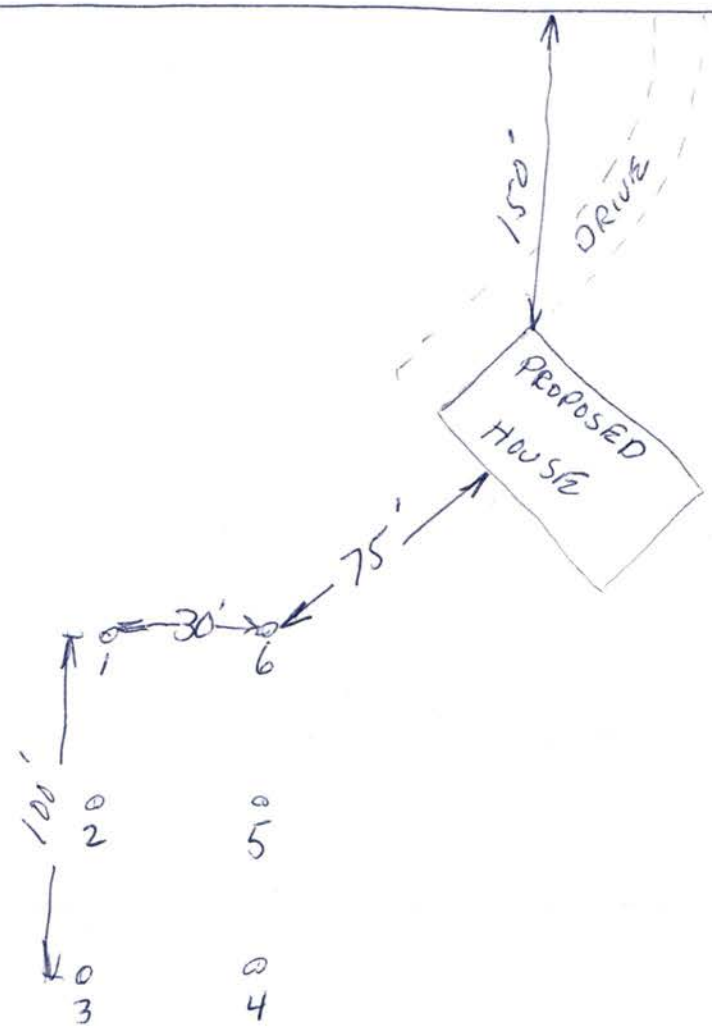

REVIEWING ACTION

Remarks : _____

Date: December 10, 1980

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals 157 ft.
3. With a Trench Width of ~~48~~ in.
4. Total Area of Lateral needed ~~630~~ sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: December3, 1980

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.


B. SEPTIC TANK:
1. Material CONC; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company PRE CAST STEP)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 6 in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.


C. DISTRIBUTION BOX:
1. Material CONC; Number - available outlets 5.
2. Factory Built: Yes ☒ No ☐
(Company PRE CAST STEP)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 20" or Perforated Pipe _____.
Material: fiberglass ☐; plastic ☐; concrete ☒ ; other _____.
2. Lateral Lines:
Number ___; Length of each line _____, _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ___ ft.
3. Trench dimensions: Width 4' ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: ROAD GRAVEL
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

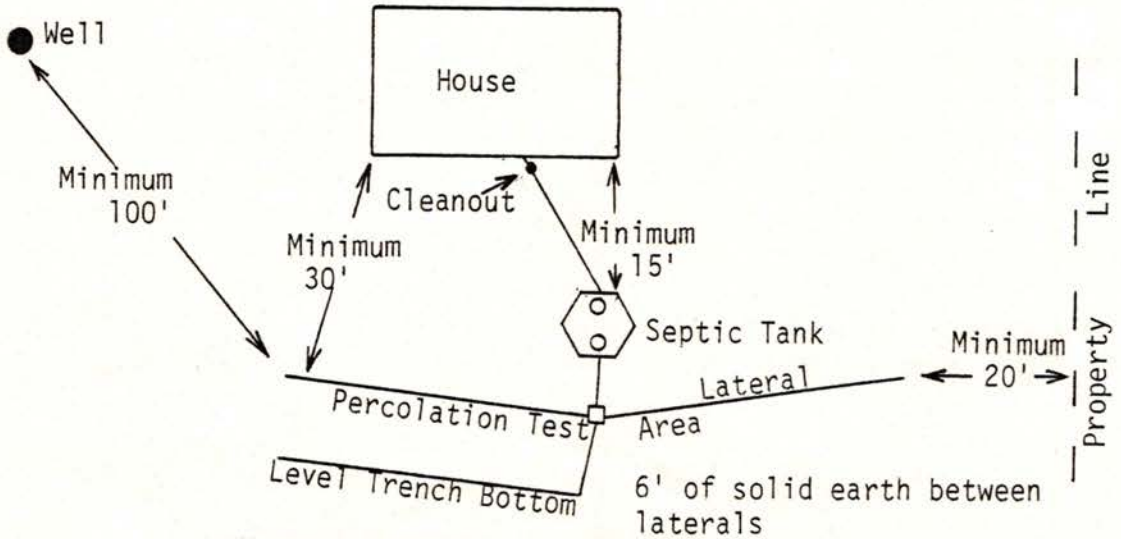

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

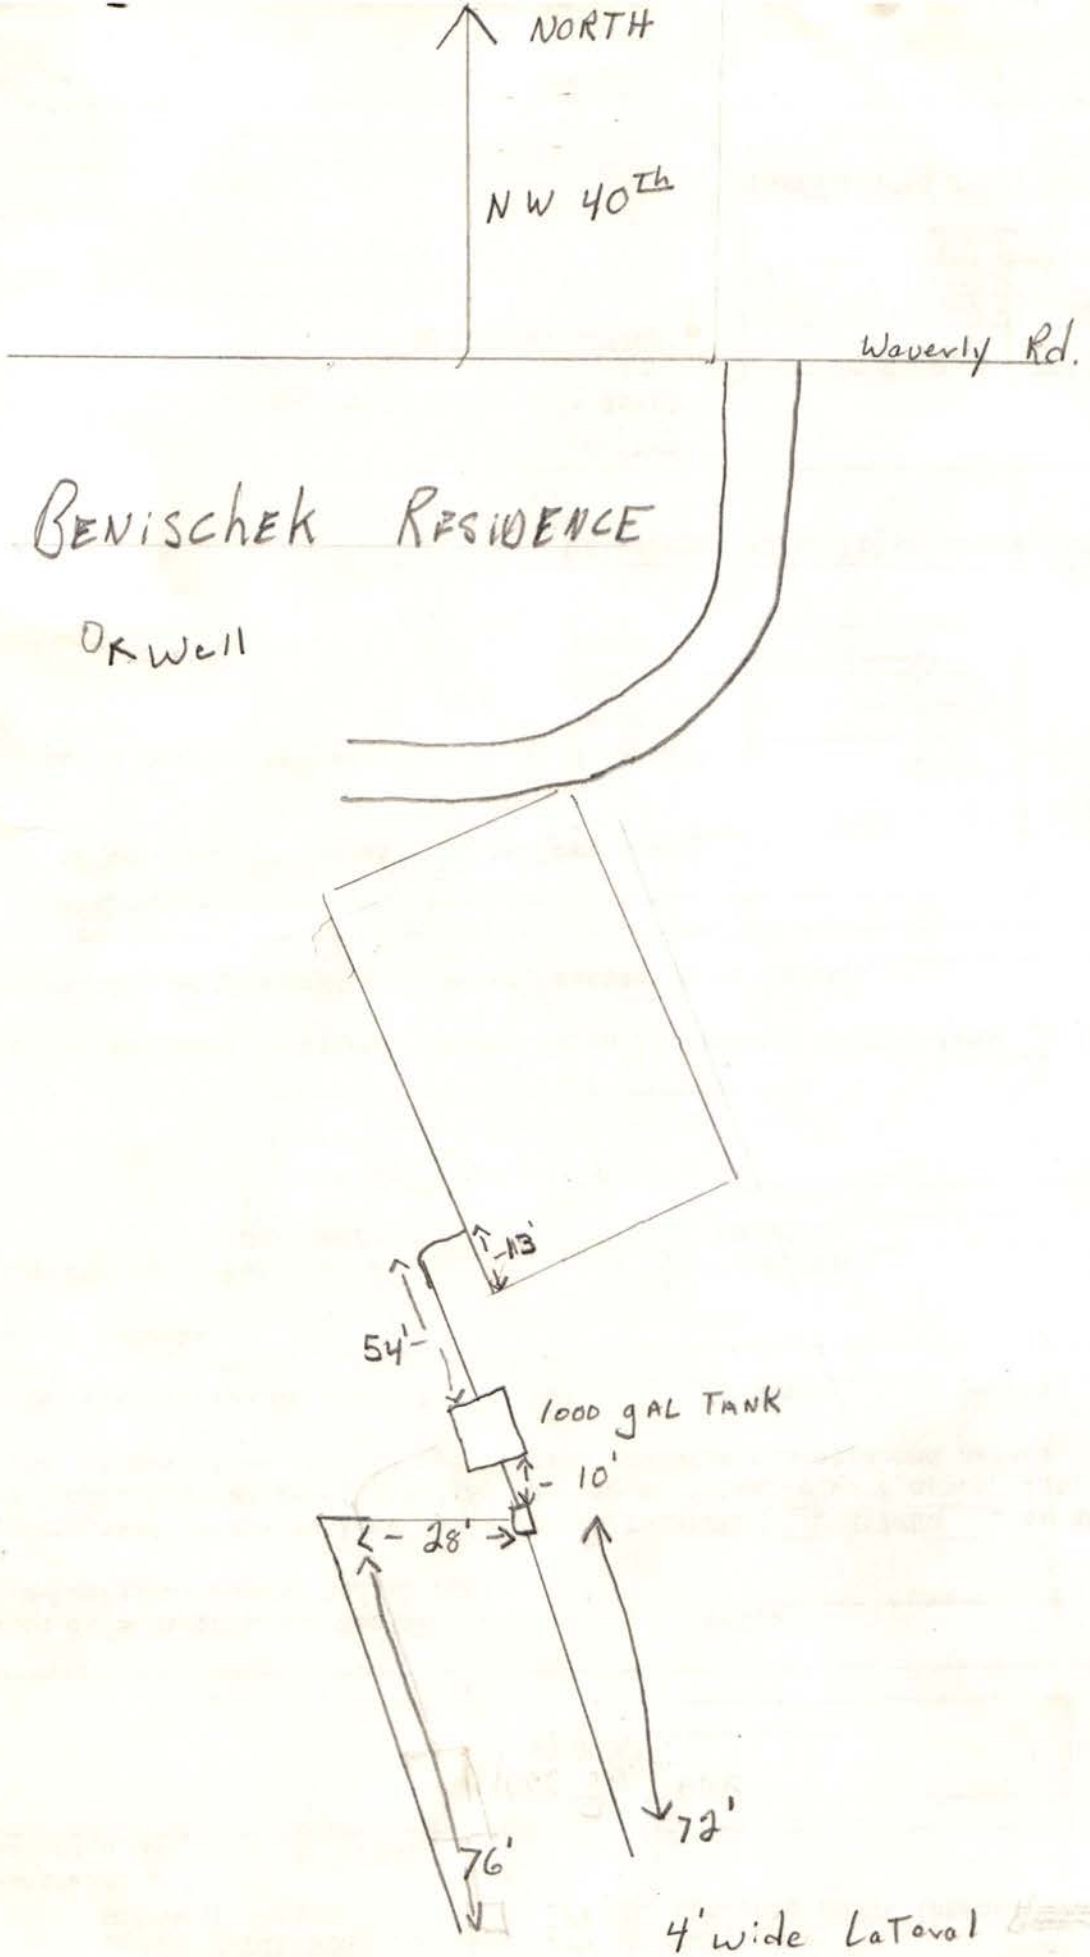
NORTH
NW 40th
Waverly Rd.
BENISCHEK RESIDENCE
ORWELL
13'
54'
1000 gAL TANK
10'
28'
72'
76'
4' wide LaTeval

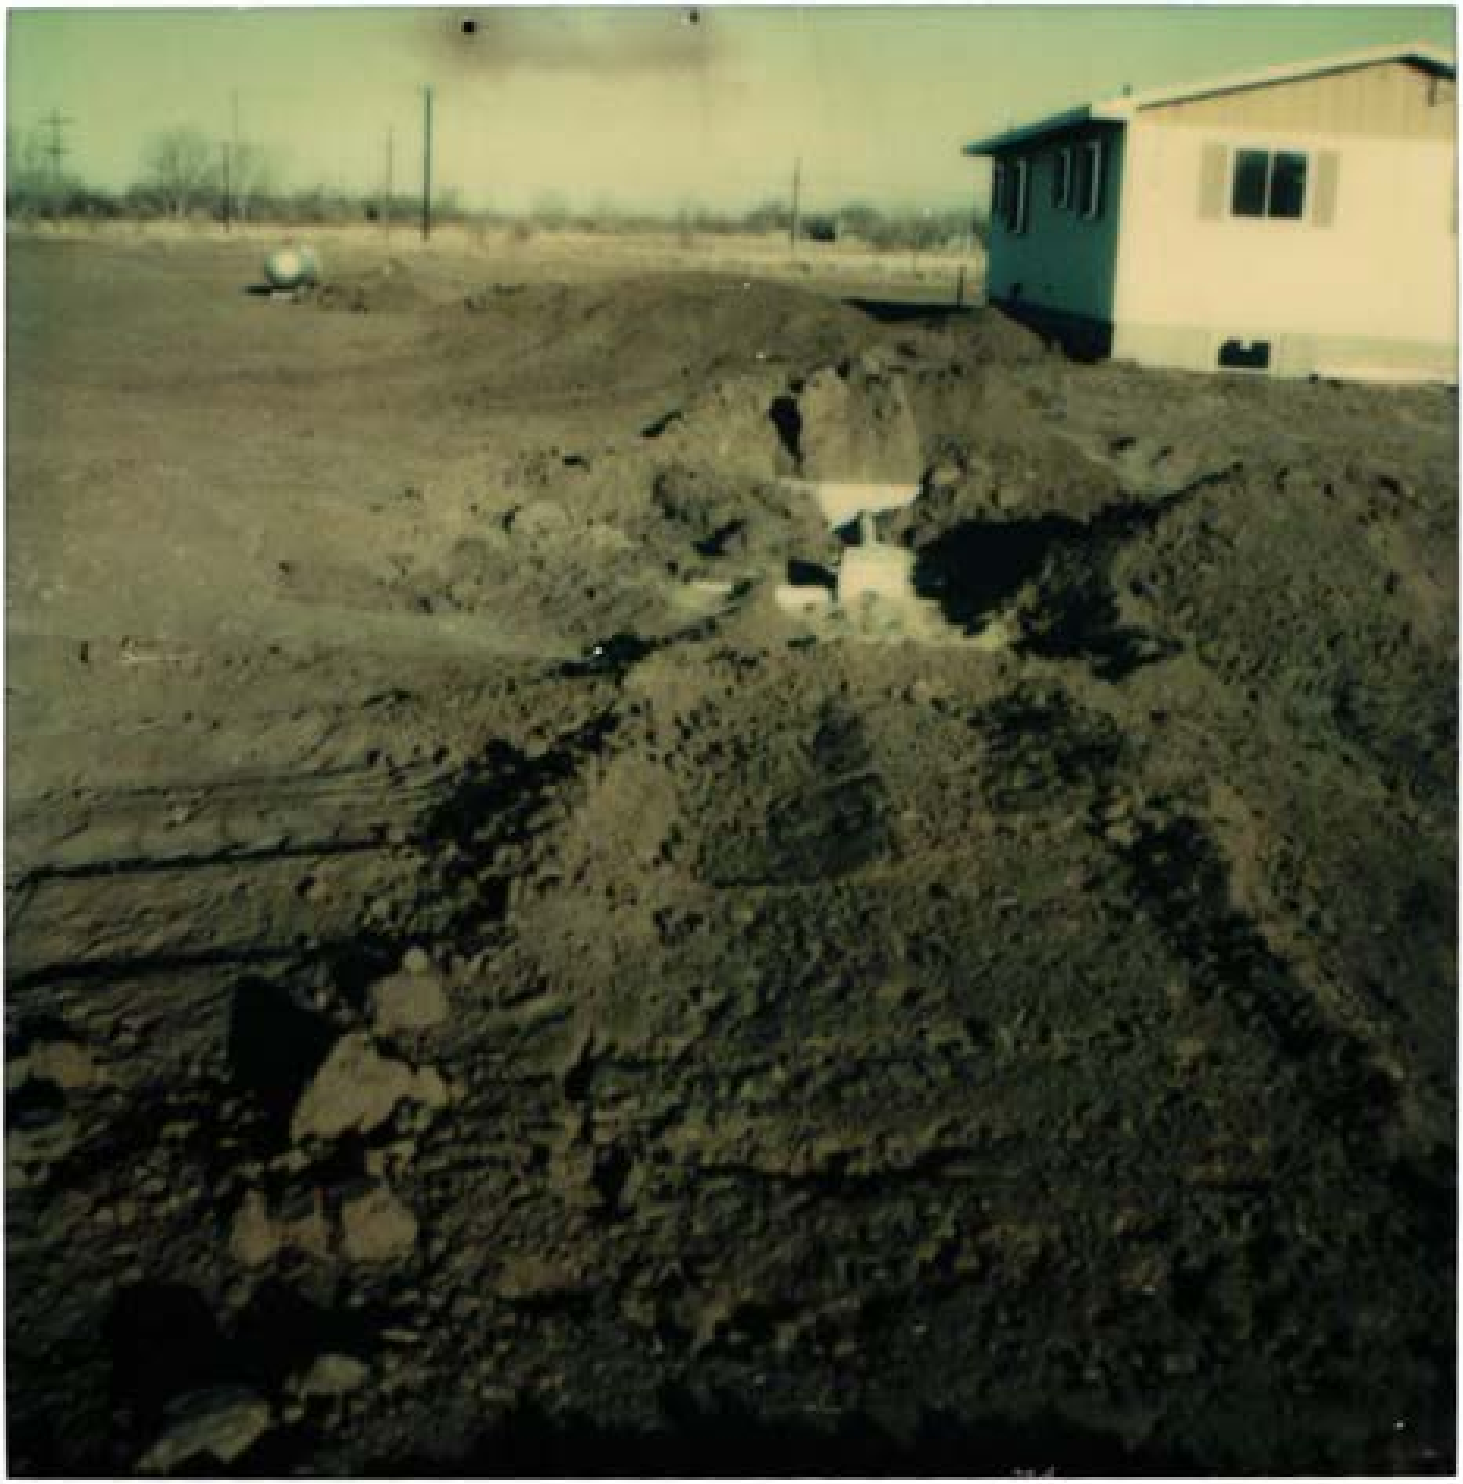


1-26-81 Shallow septic system.
Earth mounded over lakeside
T11N, R6E, Sec. 27. NW¼
William Banischek

William and Kathleen Benischek

LEGAL DESCRIPTION

A tract of land in the NW ¼ of Section 17, T 11 N, R 6 E of 6th P.M., Lancaster County, Nebraska, and more particularly described as follows:

Commencing at the NE corner of Said NW ¼ thence on an assumed bearing of N 90° W along the North line of said NW ¼ a distance of 755.4', Thence 50° E a distance of 33' to the point of beginning, said point being the SW corner of the county road intersection, Thence S16° 49' along the west line of said county road a distance of 415.9', Thence N 86° 57' W a distance of 122.7', Thence S1° 41' E a distance of 46.25', Thence N 90° W a distance of 30.0', Thence S1° 41' E a distance of 40', Thence N 90° W a distance of 503' , Thence N 23° 24' W a distance of 191' Thence N 87° 24' W a distance of 214', Thence N 29° 57' W a distance 337.9' to a point on the south line of said county road, Thence N 90° E a distance of 991' to the point of beginning. Said tract contains 9.06 acres.

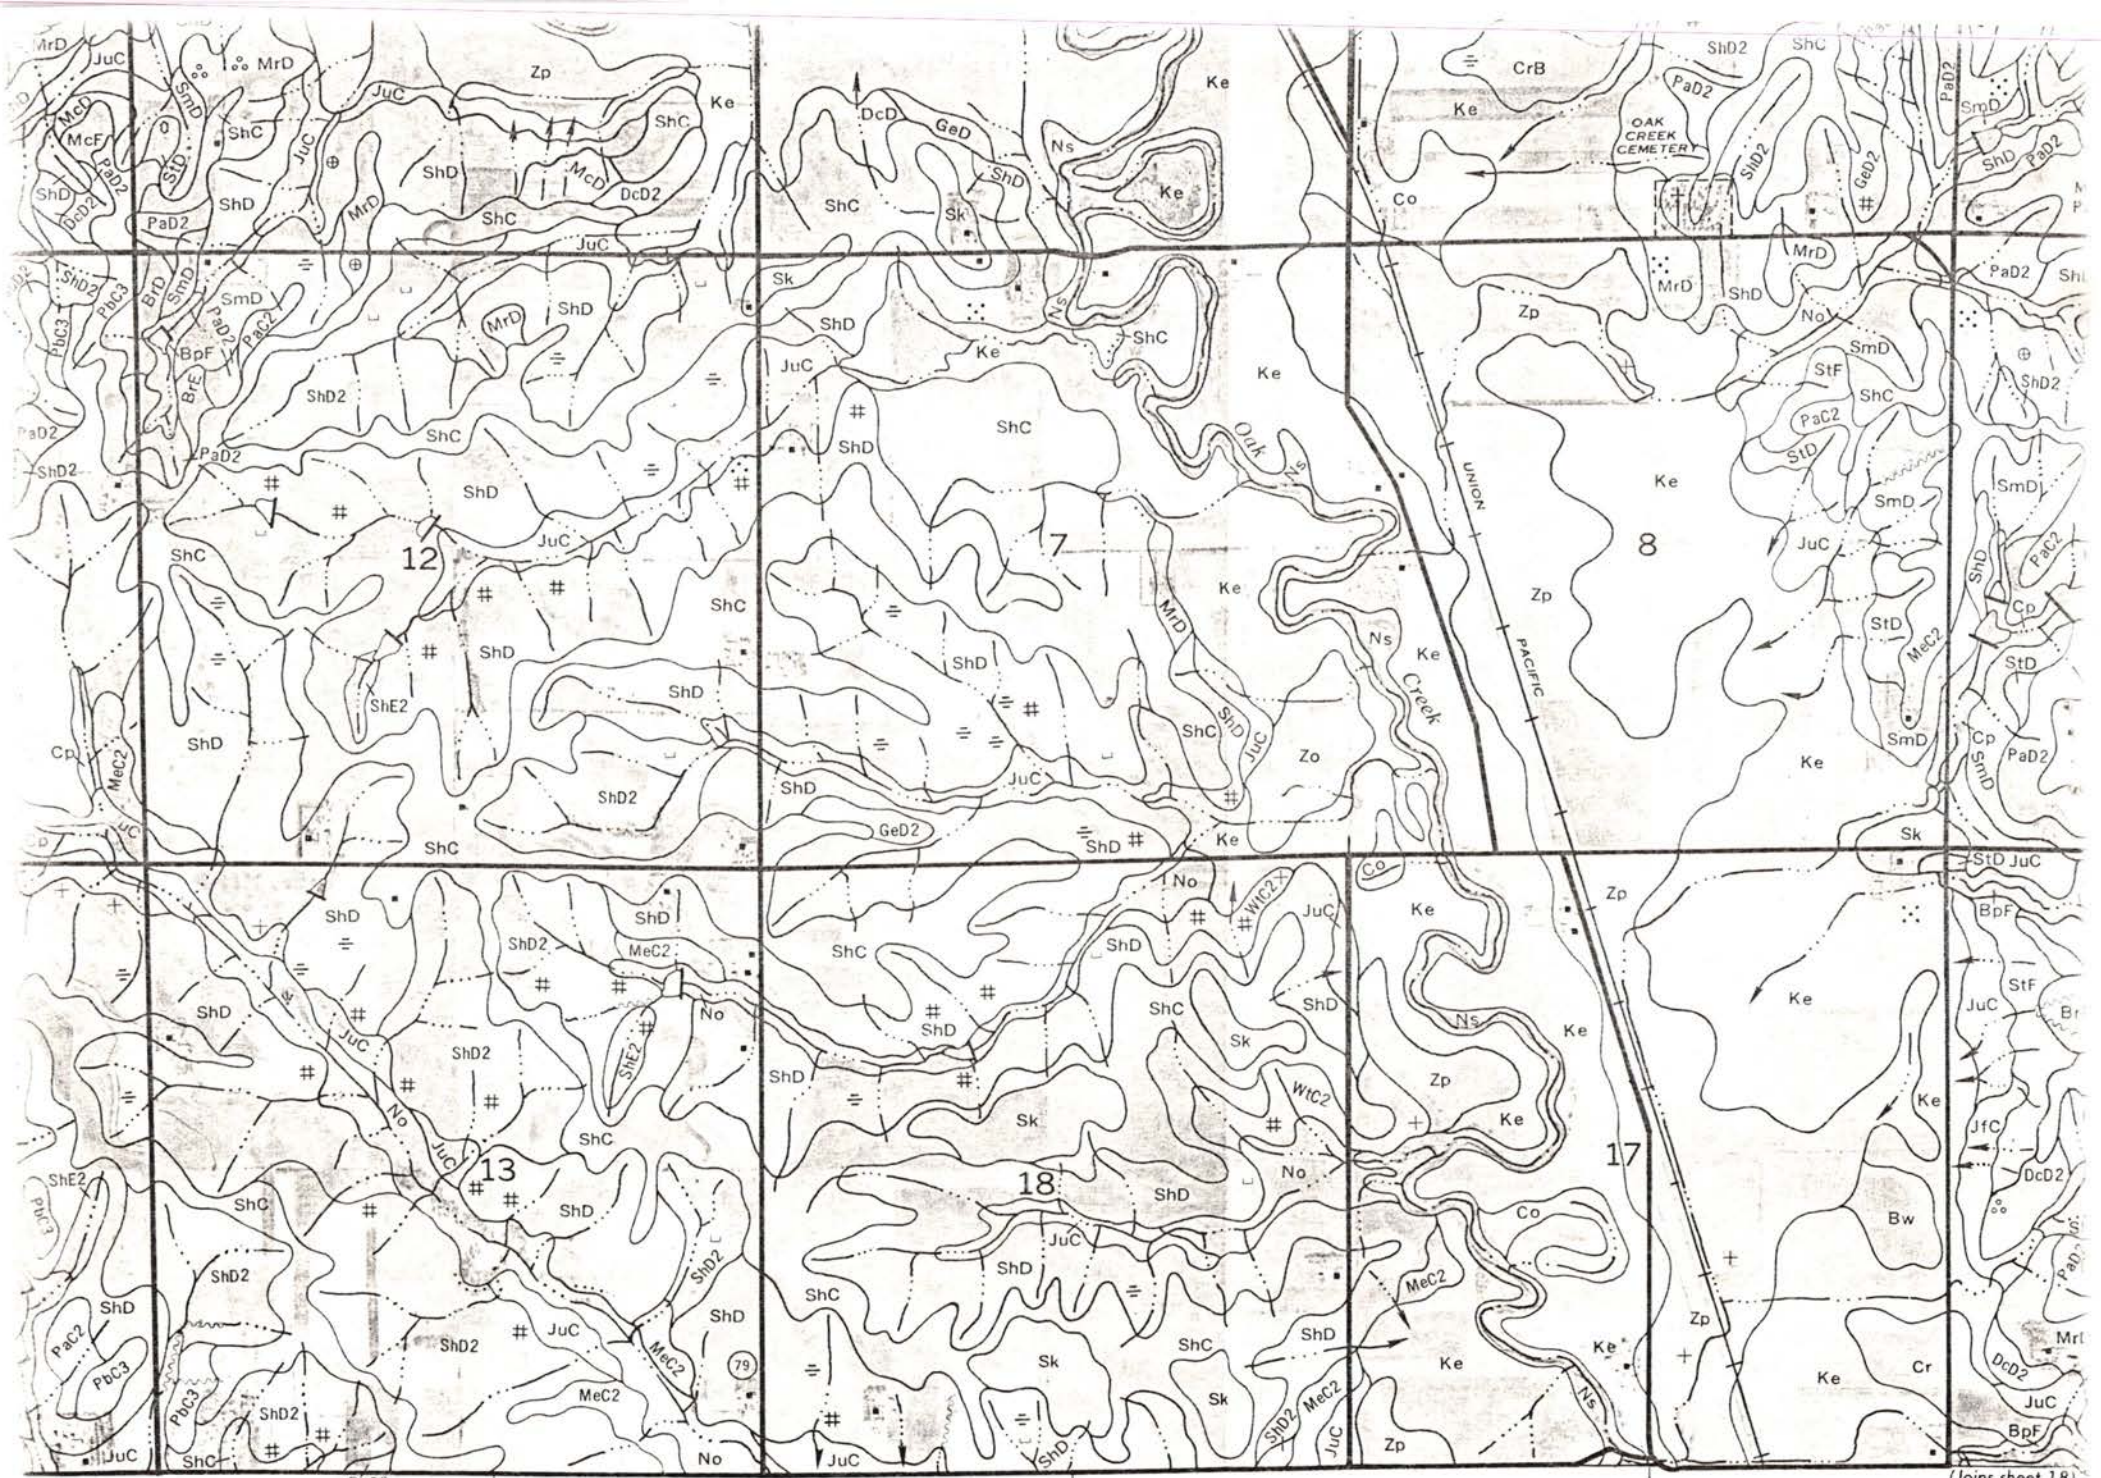
OAK CREEK CEMETERY
UNION PACIFIC
Oak Creek
12
7
8
13
18
17
79
(Joins sheet 18)

007

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 St. Marys Avenue Phone (402) 471-7800 Lincoln, Nebraska 68502

REAL ESTATE TRANSFER / LOAN APPROVAL

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECKS PAYABLE TO: Lincoln-Lancaster County Health Department.

☐ Evaluation of the Individual Water System Date: 6-25-92

☐ Evaluation of the Sewage Disposal System ☐ Enclosed is $150.00

Legal Description of Property: TWP. 11 ; RANGE 6 ; SECTION 17 ; BLOCK ___

LOT 26 ; ADDITION _____ ; Street Address 3601 West Waverly Rd.

Directions to Property 1½ miles east of Hiway 79 on West Waverly Rd.

Location of Well Directly behind shop bld. Tap Location: Inside ☐ Outside ☒

Location of Sewage System approx 40' S-SW from house Year Installed 81?

	NAME	ADDRESS	PHONE
Present Owner:	William Benischek	Rt 5 Lincoln Ne 68508	783-2314
Tenant/Buyer:			
Return to:	Owner's architect	American Charter Sue Badmon 3930 So. St. Lincoln, NE 68506	476-6600

NOTE: Allow two weeks for processing. Incomplete information will delay processing.

Signature of Applicant William Benischek Address 3601 West Waverly Rt 5 Lincoln 68508

==========

HEALTH DEPARTMENT USE ONLY

Date Received 6-25-92 Received $150.00 Check ☒ Cash ☐

PRELIMINARY STATUS--DATE 6-26-92

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM:	SITE VISIT:
Construction	☒	☐	Approved: ☒	Date 6-26-92 by RM
Bacteria	☒	☐	Provisional: ☐	Date ____ by ____
Nitrate	☒ <0.1	☐	Disapproved: ☐	Date ____ by ____

Comments: Recommend checking to see if septic tank needs pumping

See Attached Letter ☐

FINAL STATUS

WATER SYSTEM:	SEWAGE DISPOSAL SYSTEM:	
Approved: ☒	Approved: ☒	Provisional Approval: ☐

APPROVED BY Ron Magenau DATE 7-2-92

Approval or disapproval is based on written standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operation. WELLS - Nebraska Safe Drinking Water Act,
- Standards for A Private Well in Nebraska

FG.4120 INDIVIDUAL SEWAGE SYSTEMS - County Resolution #2832
