LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION
3140 "N" STREET
Lincoln, NE 68510-1514
(402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 96380145001

Issued 07/15/96
Expires 01/15/97
Revenue Code 18754

Establishment
STEVE CHAMPOUX
T11N R6E SEC 9
VALLEY HOME FARMS BLK 2 LOT 1

FEES: $150.00

Permittee
STEVE CHAMPOUX
BOX84891
BOX 84891
LINCOLN NE 68501

TOTAL $150.00

Issued By M. Jane Ford
Health Director

2358

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
3140 N Street
Lincoln NE 68510
(402)-441-8022

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 11N ; Range 6E ; Section 9 ;
   Block 2 : Lot 1 : Addition Valley Home Farms Add
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Steve McClymont
Signature of Applicant (Owner or Lessee)

Box 84891 Line. 68501
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/9/96. Date Frwd. 7/9/96.
   ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hoos

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 7/9/96. Date Frwd. 7/9/96.
   ACTION: Approved ☒ Disapproved ☐ Signature: [illegible]

3. City or County Engineer: Date Rec'd. 07/10/96. Date Frwd. _____.
   ACTION: Approved ☒ Disapproved ☐ Signature: [illegible]

REMARKS OR REASONS FOR DISAPPROVAL Build Septic System Above Top of Dam

Site Visits:
Date: 12-3-96 by: rm (Retaining wall behind outlet butted against concrete)
Date: 12-4-96 by: rm (Corrected)
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: December 5, 1996 By: Ron Mayent

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
3140 N Street
Lincoln NE 68510
(402)-441-8022

B

2300 West James Rd FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township _____; Range _____; Section & ¼ Section _____.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 7-1 to 7-2. Weather: Precip. High Humid Temp. 92°.

OWNER: Prairie Homes

Address: Box

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Water Level (in.)	Time (Hr./Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36	7-1	2:00	7-2	6:00p	7-2	6:10p	6"	6:40p	4¾"	30	1¼	24MIN/IN
2	36	"	2:00p	7-2	6:10p	7-2	6:10p	6"	6:40p	5"	30	1	30MIN/IN
3	36	"	2:00p	"	6:10p	7-2	6:10p	6"	6:40p	5"	30	1	30MIN/IN
4	36	"	2:00p	"	6:15p	7-2	6:15p	6"	6:45p	4½"	30	1½	20MIN/IN
5	36	"	2:00p	"	6:15p	7-2	6:15p	6"	6:45p	4¾"	30	1¼	24MIN/IN
6	36	"	2:05p	"	6:15p	7-2	6:15p	6"	6:45p	5"	30	1"	30MIN/IN
~~7~~	~~36~~	"	~~2:05~~	"	6:20	~~7-2~~	6:20	6"	6:50p				
8	36	"	2:05p	"	6:20p	7-2	6:20p	6"	6:50p	5"	30	1"	30MIN/IN
9	36	"	2:05p	"	6:20p	7-2	6:20p	6"	6:50p	4½	30	1½	20MIN/IN

Phillip D Nelk
Signature of Person Conducting Test

Address Rt 6 Box 52 Phone 438-3349

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Morrill Clay Loam
Date: July 9, 1996

Approved Percolation Rate (a)
A. 26 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
3140 N Street
Lincoln NE 68510
(402)-441-8022

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO._____

Indicate on sketch if residence and well are exisiting or proposed.

REVIEWING ACTION

Remarks :_____

Date: JULY 9, 1996

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed 701 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

2300 W. James

D

Permit Number:

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

Wellmann Plumbing

Sewage Disposal System

As Built Plans & Specifications

Date 12-4-96

System Location (Indicate correct number and street)

Address 2300 W. James (no rural route) City Lincoln NE, Zip

A. Building Sewer

1. Material: Sdd 40 4"
   Diameter: 4 in.
2. Distance above basement floor: — in.
   or distance below basement floor: 12 in.
3. Distance between dwelling and septic tank: 110 ft.
4. Number of clean-outs: 2
5. Distances to: well or suction line 20 ft.
   stream — ft.
   pressure line 2 ft.
   property line 130 ft.

B. Septic Tank

1. Material: Concrete
   Number of compartments: 3
2. Capacity: 1250 gal.
3. Factory built: ☑ Yes ☐ No
4. Manholes: Over inlet, diameter — in.
   Over outlet, diameter — in.
   Riser: ☑ above ☐ below grade 0 in.
5. Inlet: ☑ baffle ☐ tee
6. Outlet: ☑ baffle ☐ tee
7. Depth to top of tank, below unfinished grade: 12 in.
8. Distances to: Well or suction line 120 ft.
   Stream — ft.
   Pressure line 120 ft.
   Property line 130 ft.

C. Distribution Box

1. Material: Concrete
   Number available outlets: 3
2. Factory built: ☑ Yes ☐ No
3. Distance from septic tank: 18 ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☑ Half rounds ☐ Perforated pipe
   Diameter of half round: 12" Infil Trator
   or perforated pipe:
   Material: ☐ fiberglass ☑ plastic ☐ concrete
   ☑ other Infiltrator from precast
2. Lateral lines: Number 2
   Length of each line: 88 ft. 88 ft.
   ft. ft., ft.
3. Trench dimensions: Width 4 ft.
   Slope 2 in/100 ft.
   Average depth 24 in
4. Filter material: Gravel
   Depth of material 14 in.
5. Distances to: Well or suction line 120 ft.
   Stream — ft.
   Pressure line 120 ft.
   Property line 42 ft.

Indicate North with Arrow


Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

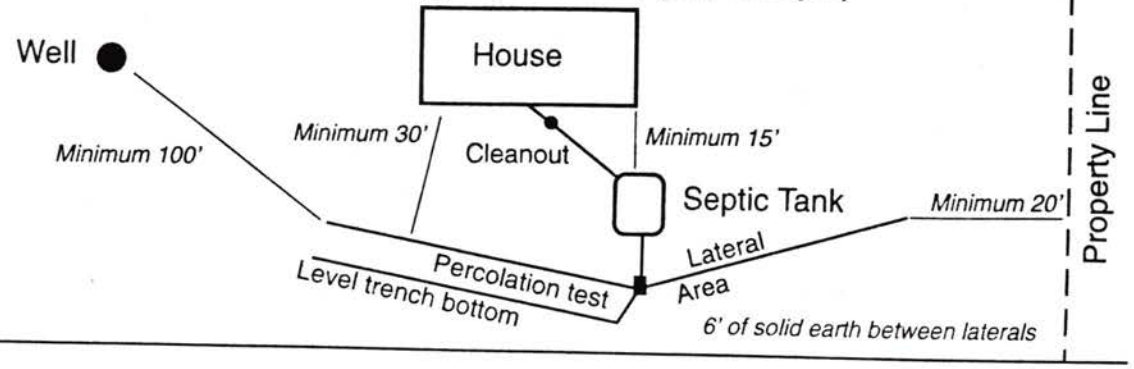

FORM 23-103 10-96

As Built Drawing

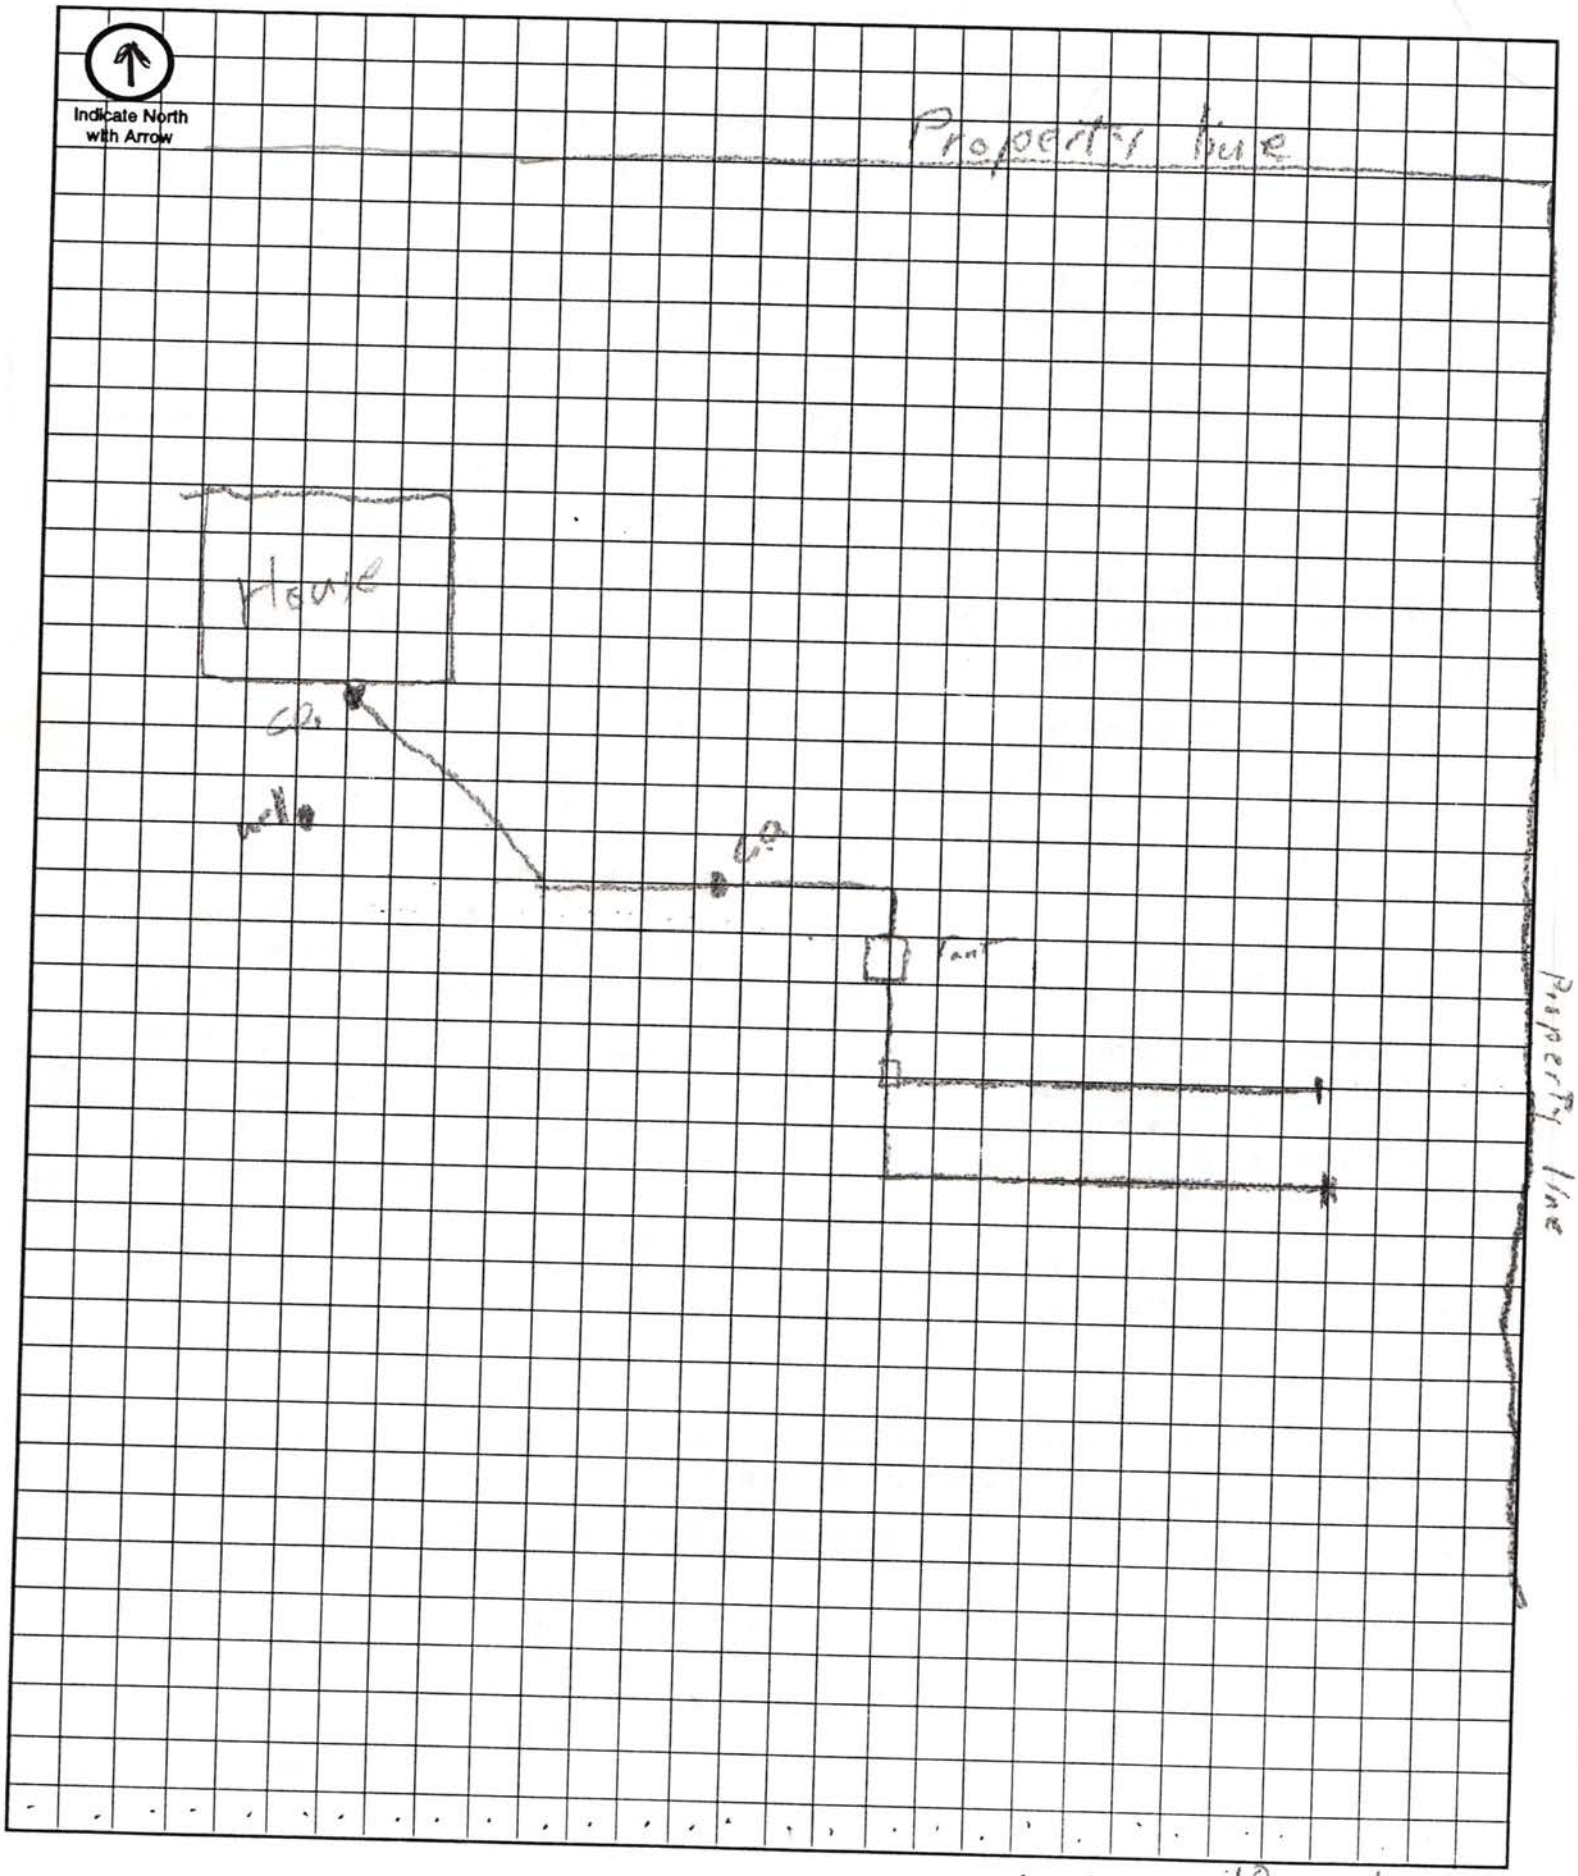

Approximate Scale: 10 ft. = 1 grid line/s

NW 27th


(Joins sheet 8)
(Joins sheet 14)
(Joins sheet 18)
OAK CREEK CEMETERY
Oak Creek
UNION PACIFIC
5
4
8
17
16
1 Mile
470 000 FEET
2 760 000 FEET
