LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 871-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

January 5, 1977 — THIS PERMIT EXPIRES

Donald L. Biskup — ISSUED TO

6843 Colfax, Lincoln, NE 68507 — ADDRESS

T11N; R5E; Sec. 33-W½ of S¼ of SE¼; — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 871-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: July 5, 1976

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 11-N; Range 5-E; Section 33
   W½ OF SW¼ OF SE¼
   Block ____; Lot ____; Addition ____
   Street Address ~~10,000~~ West Fletcher Ave

2. Property Use: Residential SFR ☒; Commercial ____ ☐
   No. of Bedrooms 2.
   Describe: ____
   Other Use ____ ☐
   Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Distance to public sewer: ____ ft.

Donald F. Bishop
Signature of Applicant (Owner or Lessee)

6843 Co/Fax, Lincoln, Nebr 68507
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 7/6/76. Date Frwd. 7/7/76. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: Date Rec'd. 7-7-76. Date Frwd. 7-7-76. ACTION: Approved ☒ Disapproved ☐ Signature: W W
3. City or County Engineer: Date Rec'd. 7/7/76. Date Frwd. 7/7/76. ACTION: Approved ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL ____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 871-C

DATE: July 5, 1976

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto. W½ OF SE¼ OF SE¼

1. Legal description of property: Twp. 11-N ; Range 5-E ; Section 33 ; Block ; Lot ; Addition .
Street Address 19000 WEST FLETCHER AVE

2. Property Use: Residential SFR ☒ Commercial ☐
No. of Bedrooms 2 Describe:
Other Use
Describe:

3. Type of Individual Sewage Disposal System: Septic Tank ☒ Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Donald L Becker
Signature of Applicant (owner or lessee)

6843 COLFAX AVE
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd;
Filing Fee: $ 30.00

2. Site Visits:
Date: 8-25-76 by: pw
Date: by:
Date: by:

3. Date: Approved ☒ ; Disapproved ☐ 7/6/76
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 8-26-76 by: James Weeks

FORM HD- 43(73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 475-6221)

FILE NO. 871-C

PROPERTY WHERE SOIL TESTED:
Location: Township 11-N ; Range 5 E
Section & ¼ Sect. ____
Property Dimensions: 658 ft. x 1333 ft.
Area: 20.12 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ☐; Silty Clay Loam ☐; Sandy Loam ☐
Silty Loam ☐; Clay Loam ☑; Sandy Clay ☐

Owner: Donald L Biskup
Address 6843 COLFAX AVE

L-60
H-85

Dates of Tests: July 2-76 to July 2-76. Weather: Precip. .35 Temp. ____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	29"	7/1	8:00	7/2	5:50	7/2	5:55	6"	6:25	5 3/4	30	1/4	30 - 1/4
2	36	7/1	8:00	7/2	5:50	7/2	5:55	6"	6:25	5 1/4	30	3/4	30 - 3/4
3	36	7/1	8:00	7/2	5:50	7/2	5:55	6"	6:25	5 3/4	30	1/4	30 - 1/4
4	24	7/1	8:05	7/2	5:50	7/2	5:55	6"	6:25	5 1/2	30	1/2	30 - 1/2
5	24	7/1	8:05	7/2	5:50	7/2	5:55	6"	6:25	5 1/4	30	3/4	30 - 3/4
6	36	7/1	8:05	7/2	5:00	7/2	5:55	6"	6:25	5 1/2	30	1/2	30 - 1/2

Sum of Percolation Rates 180 - 3"
Average of Rates: 30 - 3/4"
Mean of Rates:

DONALD L BISKUP
Signature of Person Conducting Test

Address 6843 COLFAX, LINCOLN NEBR
Phone: 467-1669

(Do not write below this line)

REVIEWING ACTION

REMARKS: ____

Approved Percolation Rate(s)
A. 40 min./inch
B. ____ min./inch
C. ____ min./inch

DATE: July 6, 1976

Jerrold C. Hook
Signature of Reviewing Official

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 971-C

SPECIFICATIONS

DATE: July 5, 1976


A. BUILDING SEWER:
1. Material PVC; Diameter 4 in.
2. Distance above basement floor ~~24~~ in.; or below basement floor 24 in.
3. Distance between dwelling and septic tank 30 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 100 ft.;
Stream 0 ft.; Pressure Line 0 ft.;
Property Line 300 ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material FIBERGLASS; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth 48 in.
3. Factory Built: Yes ☒ (Company CORR-A-GLASS CO.)
No ☐
4. Manholes: Over Inlet; diam. 16" in.
Over Outlet; diam. 16" in.
Below Grade 12" in.
5. Inlet: Baffle ☐; or Tee ☒
6. Outlet: Baffle ☒ or Tee ☐
Depth of outlet below inlet 4 in.
7. Depth of top of tank below finished grade 12 in.
8. Distances To:
Well or Suction Line 100 ft.;
Stream 0 ft.; Pressure Line 0 ft.;
Property Line 300 ft.

C. DISTRIBUTION BOX
1. Material ____; No. available outlets ____.
2. Factory Built: Yes ☐, (Company ____) No ☐
3. Dimension: Length ____ in.; Width ____ in. Depth ____ in.
4. Distance from Septic Tank ____ ft.
5. Serial Distribution: Yes ☐, No ☐ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: CORR-U-LATERAL
2. Lateral Lines: Depth below grade 24 in.
Number 1; Length of each line ~~150~~ 191 ft.
Total length of Laterals ~~150~~ 191 ft.;
Slope 2" in/100 ft. Diameter of pipe 16" in.; Shape U
Material: concrete ☐; fiber asbestos ☒; clay ☐; other ____
Distance between lateral lines ____ ft.
3. Trench Dimensions: Depth 36 in.; Width 48 in.
4. Filter Material: COURSE GRAVEL
Depth of material from trench bottom 16 in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream 0 ft.; Pressure Line 0 ft.
Property Line 300 ft.
6. Percolation Rate: 30/34 minutes/inch

TYPICAL SKETCHES

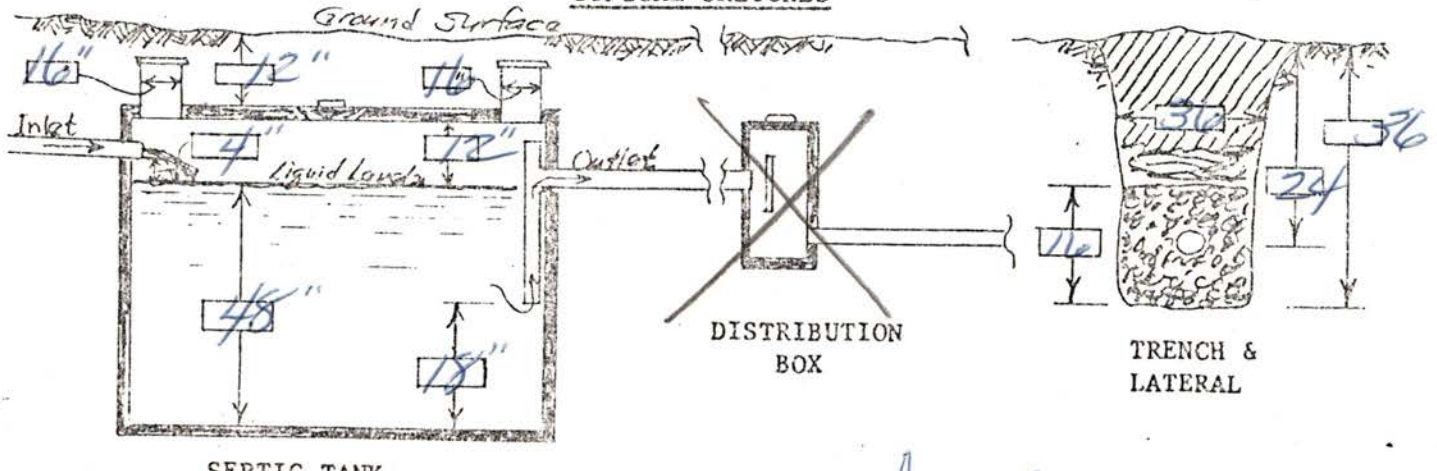

SEPTIC TANK

DISTRIBUTION BOX

TRENCH & LATERAL

Donald J. Bishop
Signature of Applicant

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 871-C

SPECIFICATIONS

DATE: July 5, 1976


A. BUILDING SEWER:
1. Material DWV; Diameter 4" in.
2. Distance above basement floor ___ in.; or below basement floor 24 in.
3. Distance between dwelling and septic tank 30 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 100 ft.;
Stream 0 ft.; Pressure Line 0 ft.;
Property Line 300 ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Fiber Glass; No. of compartments 1.
2. Capacity 1,000 gals.; Liquid depth 48 in.
3. Factory Built: Yes ☒ (Company Corr-A-Glas Co.)
No ☐
4. Manholes: Over Inlet; diam. 16" in.
Over Outlet; diam. 16" in.
Below Grade 12" in.
5. Inlet: Baffle ☐; or Tee ☒
6. Outlet: Baffle ☒; or Tee ☐
Depth of outlet below inlet 4 in.
7. Depth of top of tank below finished grade 12 in.
8. Distances To:
Well or Suction Line 100 ft.;
Stream 0 ft.; Pressure Line 0 ft.;
Property Line 300 ft.


C. DISTRIBUTION BOX
1. Material ___; No. available outlets ___
2. Factory Built: Yes ☐, (Company ___)
No ☐
3. Dimension: Length ___ in.; Width ___ in.
Depth ___ in.
4. Distance from Septic Tank ___ ft.
5. Serial Distribution: Yes ☐, No ☐
(If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: Corr-A-Lateral
2. Lateral Lines: Depth below grade 24 in.
Number 1; Length of each line 150 ft
Total length of Laterals 150 ft.;
Slope 2" in/100 ft. Diameter of pipe 16" in.; Shape U
Material: concrete ☐; fiber asbestos ☒; clay ☐; other ___
Distance between lateral lines — ft.
3. Trench Dimensions: Depth 36" in.;
Width 36" in.
4. Filter Material: Course gravel.
Depth of material from trench bottom 16" in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream 0 ft.; Pressure Line 0 ft.
Property Line 300 ft.
6. Percolation Rate: 30/3¼" minutes/inch

TYPICAL SKETCHES

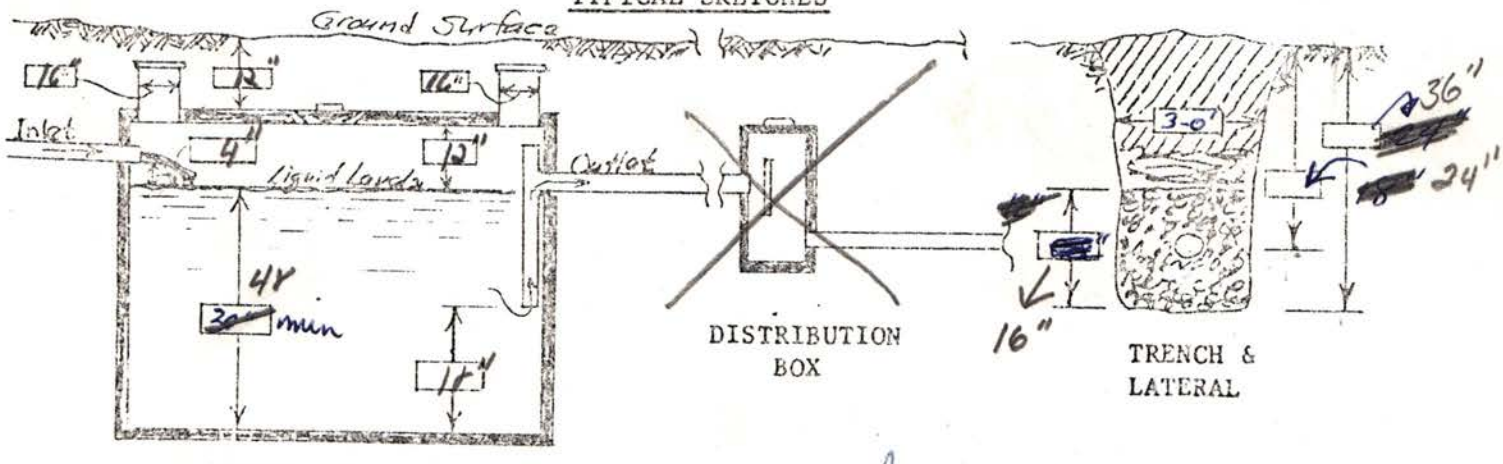

Donald L Bishop
Signature of Applicant

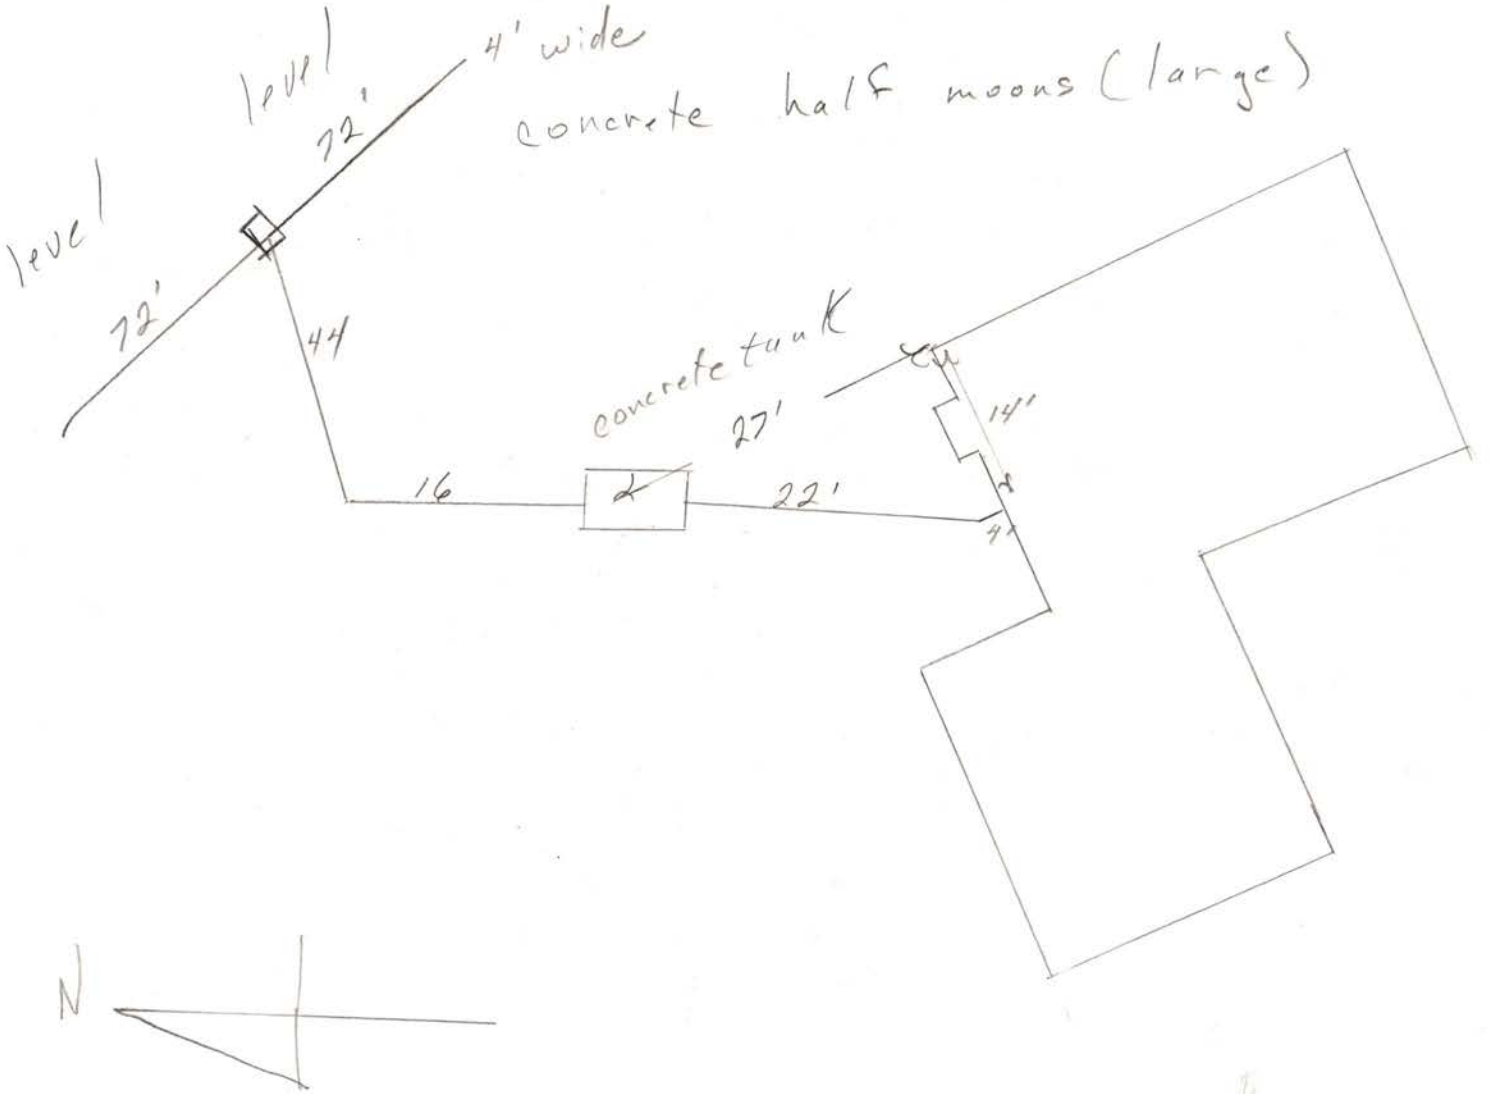
level
72'
4' wide
concrete half moons (large)
level
72'
44
concrete tank
27'
14'
16
22'
N

JW
8-25-76
