LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2699-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

JANUARY 21, 1989 — THIS PERMIT EXPIRES

SHELLY J. JANSSEN — ISSUED TO

1841 RIDGEWOOD CT., #1 LINCOLN, NE 68505 — ADDRESS

T10N; R8E; Sec 13; Lot 1; Glenwood Acres, Outlot A — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE NEW CONSTRUCTION

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY	DATE	AMOUNT
MG	7-21-88	

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $60.00

FILE NO. 2699-C

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 10N; Range 8E; Section 13; Block _____: Lot 1: Addition Glenwood Acres
   Street Address Outlot A
2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3. Describe _____
3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒
4. Distance to public sewer: _____ ft.

Shelly J Janssen
Signature of Applicant (Owner or Lessee)

1841 Ridgebaren Ct. #1
Address
Lincoln, NE 68505

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/20/88. Date Frwd. 7/21/88. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 7/21/88. Date Frwd. 7/21/88. ACTION: Approved ☒ Disapproved ☐ Signature: _____
3. City or County Engineer: Date Rec'd. 7/21/88. Date Frwd. 7/21/88. ACTION: Approved ☒ Disapproved ☐ Signature: Larry V. Worrell

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 10-18-88 by: no sewer line yet ok
Date: 10-26-88 by: ok overflow of pond at top of lagoon dike
Date: 11-2-88 by: ok dike to be

INSTALLATION FINAL WRITTEN APPROVAL
Date: 12-28-88 By: Ron Maynard

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. 2699-C

PROPERTY WHERE SOIL TESTED:

Location: Township_____; Range_____; Section & ¼ Section_____.
Property Dimensions: _____ft. x _____ft. Area:_____acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ■ .
Dates of Tests: 4-7-87 to 4-8-87. Weather: Precip. 0 Temp. 70°.

Hole's 1-2-3-4-6 Had water in From Pre-Test

OWNER: Gary S. Janssen - 464-8249
Address: 1841 Ridgehaven Ct. No. 1 Lincoln, NE. 68505

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36"	4-7	6:00 pm	4-8	4:00 pm	4-8	4:00 pm	6"	4:30 pm	5 3/4"	30m	1/4"	
2	36"	4-7	6:00 pm	4-8	4:00 pm	4-8	4:00 pm	6"	4:30 pm	5 7/8"	30m	1/8"	
3	36"	4-7	6:00 pm	4-8	4:00 pm	4-8	4:00 pm	6"	4:30 pm	6"	30m	0"	
4	36"	4-7	6:00 pm	4-8	4:00 pm	4-8	4:00 pm	6"	4:30 pm	5 7/8"	30m	1/8"	
5	36"	4-7	6:00 pm	4-8	4:00 pm	4-8	4:00 pm	6"	4:30 pm	5 1/2"	30m	1/2"	
6	36"	4-7	6:00 pm	4-8	4:00 pm	4-8	4:00 pm	6"	4:30 pm	5 7/8"	30m	1/8"	

Mike Hoagland
Signature of Person Conducting Test
Address 2525 Cleveland Ave. Phone 464-0638

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: Too slow for
Soil Type (SCS): _____
Date: _____

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

Signature of Reviewing Official

RECEIVED OCT 3 1 1988

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material #160; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 16 in.
3. Distance between dwelling and ~~septic~~ lagoon tank 191 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material _____; No. of compartments _____.
2. Capacity _____ gals.;
3. Factory Built: Yes ☐ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number ___ ; Length of each line _____, _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width _____ ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: _____
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

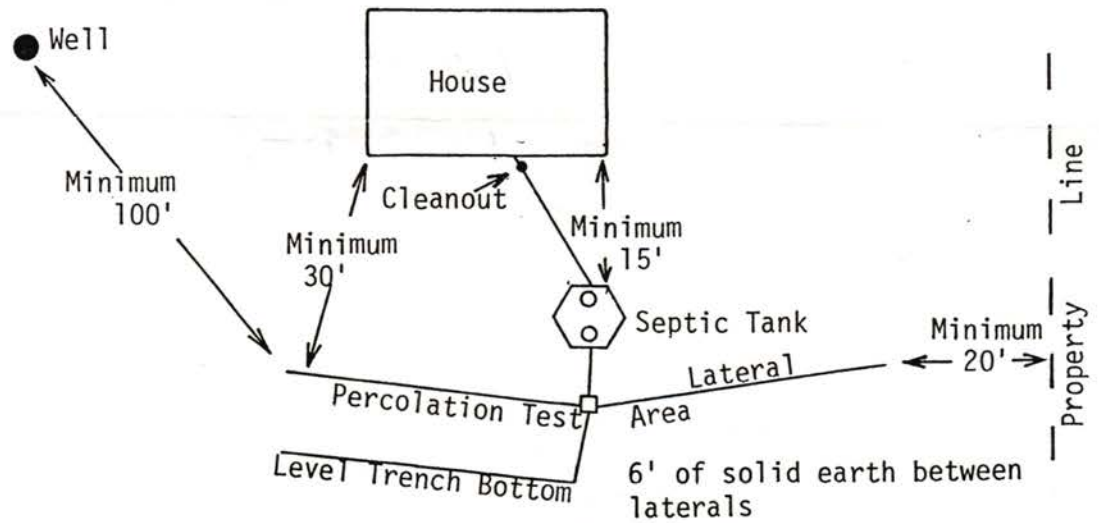

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

10-25-88

Larry Schwarek
For Mann Homes

