LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2365-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

FEBRUARY 5, 1986 — THIS PERMIT EXPIRES

R. C. WOBIG — ISSUED TO

1143 SUMNER LINCOLN, NE 68502 — ADDRESS

T11N; R5E; Sec 18, SE¼ I.T. — LEGAL DESCRIPTION

REMARKS: NON-TRANSRERABLE NEW CONSTRUCTION

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY: EB — DATE: 8/6/86 — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2365-C

DATE: 8-4-86

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 11 N ; Range 5 E ; Section SE¼ 18;
   Block ____ : Lot 47 irregular tract ; Addition ____
   Street Address ____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe ____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: ____ ft. EXPERIMENTAL

B. C. Wohlig
Signature of Applicant (Owner or Lessee)

1143 Sumner
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 8/5/86. Date Frwd. 8/6/86. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold E. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 8/6/86. Date Frwd. 8/6/86. ACTION: Approved ☒ Disapproved ☐ Signature: [illegible]

3. City or County Engineer: Date Rec'd. 8/6/86. Date Frwd. 8/6/86. ACTION: Approved ☒ Disapproved ☐ Signature: Larry V. Worrell

REMARKS OR REASONS FOR ~~DISAPPROVAL~~ Part of this lot is in flood plain

Site Visits:
Date: 10/30/86 by: L.C.H.
Date: 10/30/86 by: L.C.H.
Date: ____ by: ____

need 2nd hole in septic tank

INSTALLATION FINAL WRITTEN APPROVAL
Date: ____ By: ____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 2365-C

Indicate on sketch if residence and well are exisiting or proposed.

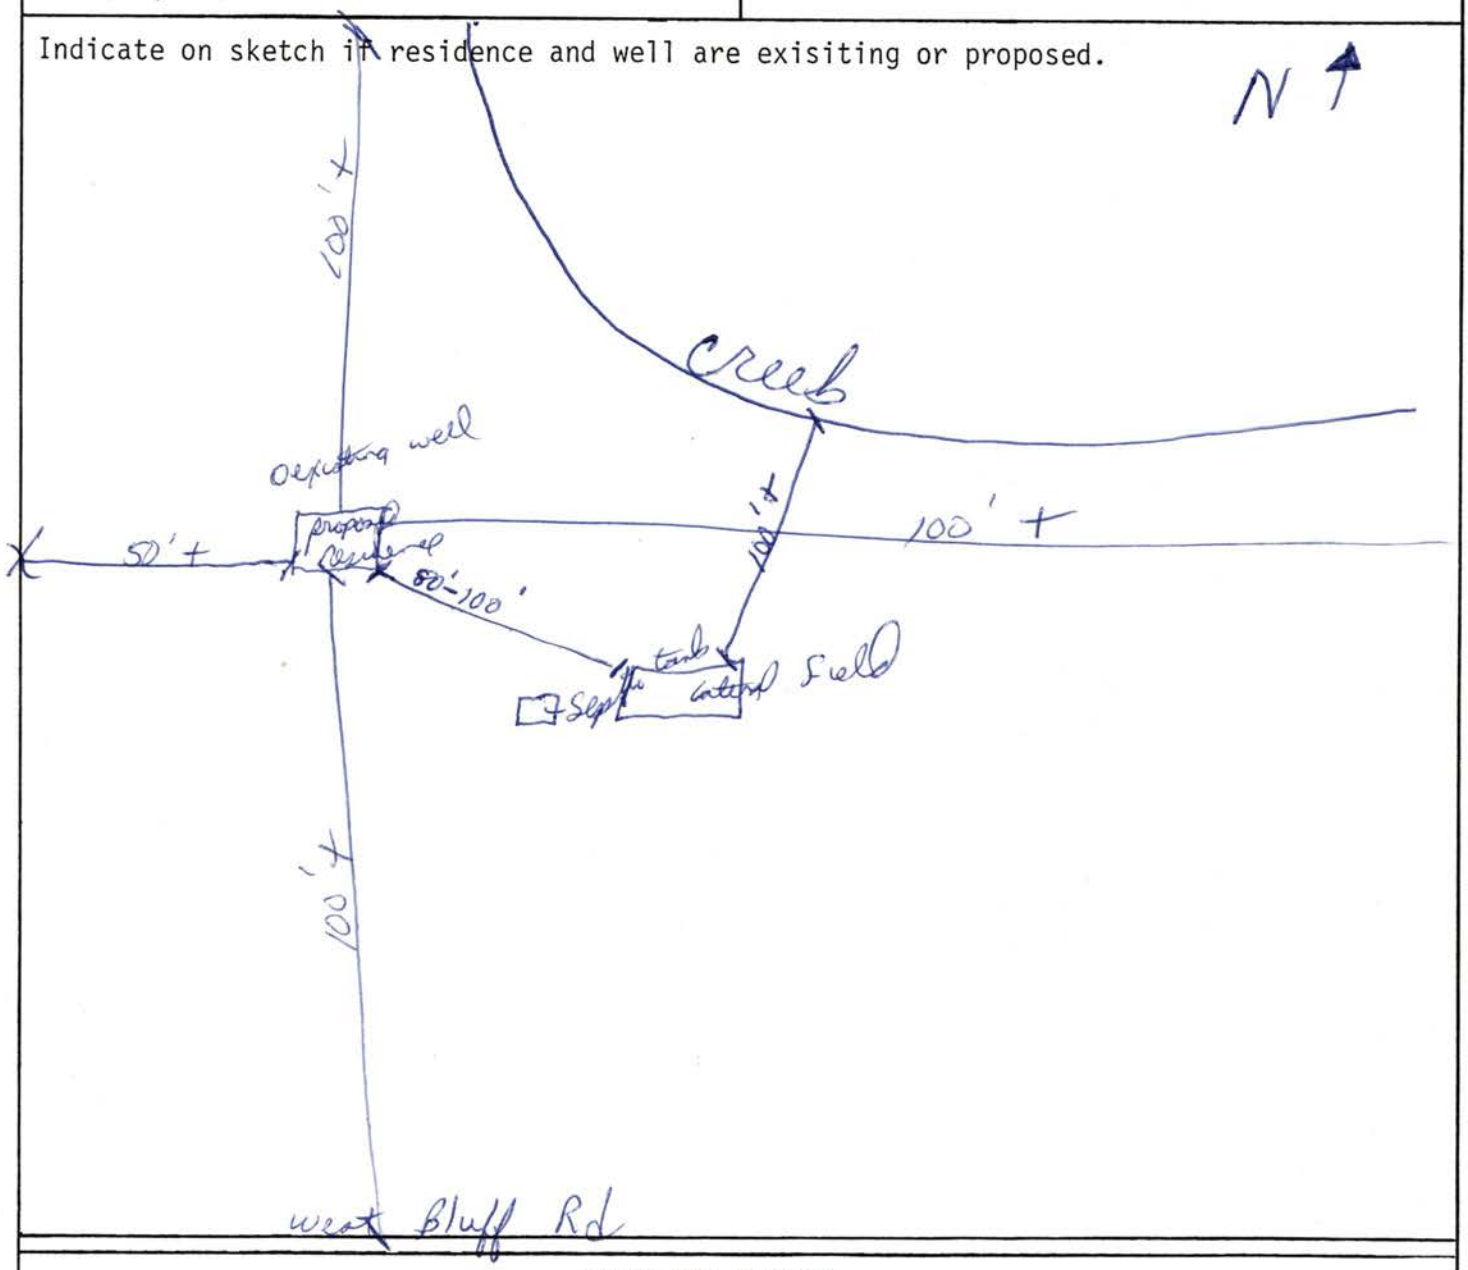

REVIEWING ACTION

Remarks: _____

_____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank _____ gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed _____ sq.ft.

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 10-30-86

FILE NO. _____

T11N R5E SEC 18 Dobie Const.
NW 126 & Bluff Rd


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Fiberglas; No. of compartments 1.
2. Capacity 1,000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Corra Glas Co.)
4. Manholes: Over Inlet; diam. 12 in.
Over Outlet; diam. 6 in.
Riser Above ☐ Below ☐ Grade N/A in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☒
7. Depth of top of tank below finished grade 13 in.
8. Distances to:
Well or Suction Line >100 ft.; Stream >20 ft.; Pressure Line >100 ft.; Property Line >100 ft.

C. DISTRIBUTION BOX:
1. Material Plastic; Number - available outlets 7.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank 11 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4.
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 2 ; Length of each line 100, 100, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 15 ft.
3. Trench dimensions: Width 8 ft.;
Slope 2 in/100 ft.; Average Depth 36 in.
4. Filter Material: Road Gravel
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

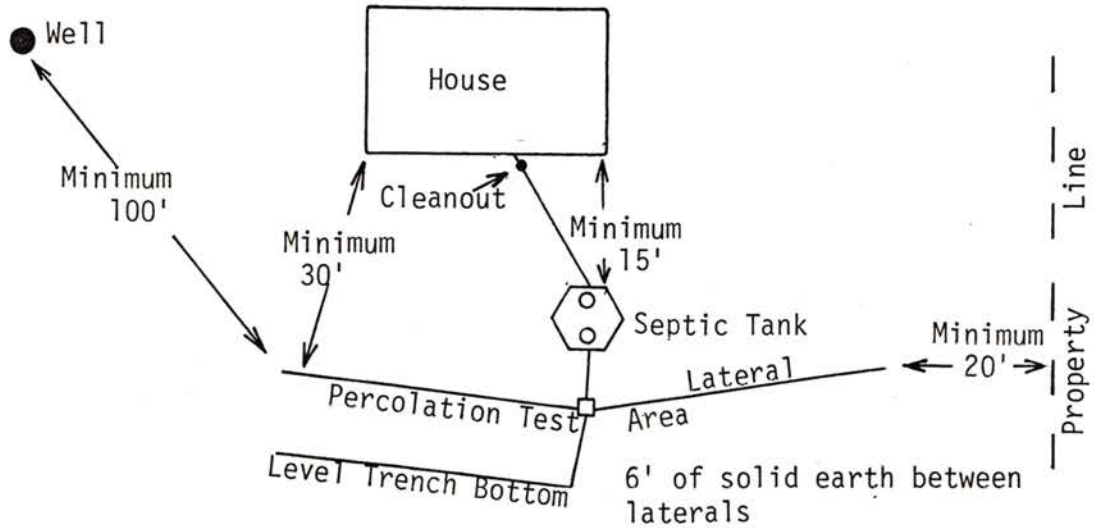

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 10-29+30 86 INSTALLER Southwick Sewer + Drain

