LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET
NON TRANSFERABLE

ENVIRONMENTAL HEALTH DIVISION
Lincoln, NE 68510-1514

(402) 441-8000

PERMIT

Permit

SEWAGE INSTALLATION
LAGOON

No. 97380156301

Issued 04/09/97
Expires 10/09/97
Revenue Code 18754

Establishment

JAMES GOSEY
7601 CHERRYWOOD DR
APT 12
LINCOLN NE 68510

FEES: $150.00

TOTAL $150.00

Permittee

JAMES GOSEY
7601 CHERRYWOOD DR
APT 12
LINCOLN NE 68510

4379

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

A

Permit Number:

Sewage Disposal System

Request for Site Clearance and Permit

Include Form B, Form C and Applicable Fees with this Application.

☐ Septic System ☑ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

PLEASE PRINT OR TYPE

A. System Location (Indicate correct number and street)

Address 6101 West Waverly Rd (no rural route) City Raymond NE, Zip 68428

Legal Description NE (1/4) 13 (1/4) Section 11N Township 5E Range Subdivision Addition Block 2 Lot

Geographical Location (if known): Longitude _____ Latitude _____

☑ Check if system mail address is not the same as the owner's address

B. Owner

Name JAMES A. GOSEY Signature James A. Gosey

Address 7601 CHERRYWOOD #12 City/State/Zip LINCOLN, NEB. 68510

☑ Check if owner designed system Home Phone 489-3022 Work Phone 472-6417

C. Contractor

Name HAROLD HEISER Company Name CONRAD ENTERPRISES

Address 3305 North 63rd City/State/Zip LINCOLN, NEB. 68507

☐ Check if contractor designed system Work Phone 580-0664

D. Engineer/Installer ☑ Check and complete if engineer designed system

Designer Name BEN EARNEST Firm EARNEST Well Drilling Co. Work Phone 475-3276

E. This System Will Serve a

☑ Residential Dwelling Number of Bedrooms 4 Is there a Whirlpool Bathtub (YES) NO

☐ Commercial Establishment/Other Facility Specify _____

Design flow in gallons per day _____ Type of Wastewater: ☑ Domestic ☐ Non-Domestic.

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☒ County Resolution No. 2832

1. **Health Department** Date rec'd 4/8/97 Date frwd 4/8/97 ACTION ☒ Approved ☐ Disapproved Signature Jerrold C. Hood
2. **Supt. Bldg. Insp. or Village Clerk** Date rec'd 4/9/97 Date frwd _____ ACTION ☐ Approved ☐ Disapproved Signature _____
3. **City or County Engineer** Date rec'd 4-9-97 Date frwd 4-9-97 ACTION ☒ Approved ☐ Disapproved Signature Larry V. Worrell

4-23-97 - trees within 100 ft need Ground need fence or drawing
9-15-97 run fence up.

Installation Final Written Approval

By Ron Morgan

Date 9-15-97

Business Office Use Only 3195

Date Rec'd 04/08/97

Amt Paid 150 cc

Rec'd By LS Cash/Check No. 1242

FORM 23-100 10-96 White - Health Dept. Yellow - Engineer Pink - Bldg. Inspector

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Sewage Disposal System

Soil Absorption Test Data Report

Annex to Application

PLEASE PRINT OR TYPE

System Location (Indicate correct number and street)

Address 6101 West Waverly Road (no rural route) City Raymond NE, Zip 68428

Owner JAMES A. GOSEY Addresss 7601 Cherrywood Drive #12, Lincoln, Neb. 68510

Soil Type (SCS): _____ Percolation Rate: _____ min./inch

Date of Tests _____ to _____ Weather: Precipitation _____ Temperature _____

Percolation Test Data Table

A.	B.	C. D. E. F. Pre-Saturation Period				G. H. I. J. K. Percolation Readings					L. M. N. Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time (Min)	Water Level Drop (in)	Percolation Rates (Min/in)

Will do LAGOON SYSTEM

Sum of Percolation Rates: _____

Average of Rates: _____

Rate Used for Calculation: _____

Person Conducting Percolation Tests

Name: _____

Phone: _____

Address _____

_____

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Remarks _____

_____

_____

Signature of Reviewing Official _____ Date _____

FORM 23-101 10-96


Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

C

Permit Number:

Sewage Disposal System
Preliminary Plan Specifications

Draw a plot plan showing system location, lines, distribution box, tank and laterals, percolation test hole locations, well, residence, compass direction and property lines. Indicate on drawing if residence and well are existing or proposed.

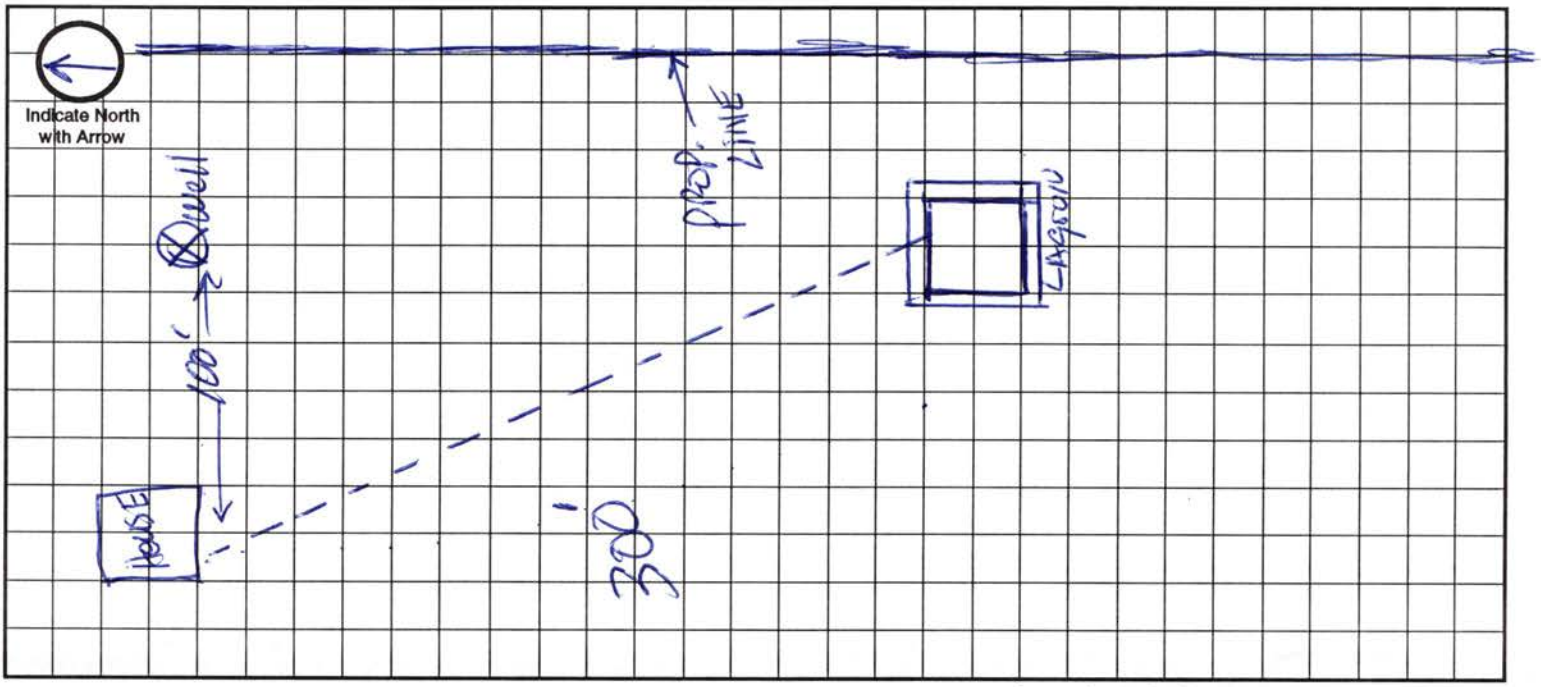

Approximate Scale: _____ ft. = _____ grid line/s

A. System Location (Indicate correct number and street)

Address (no rural route) 6101 WEST WAVERLY City RAYMOND NE, Zip 68428

B. Proposed Septic Tank/s

Tank Material: ☐ Concrete ☐ Plastic ☐ Other _____

C. Proposed Absorption System (See Form B for Percolation Information)

Percolation Rate _____ (min. per inch) Soil Type: _____ Land Slope: _____ %

Type of Absorption System: ☐ Trench ☐ Bed ☐ Other _____

Total Square Feet of Field Required: _____ sq. ft.

Type of Lateral: ☐ Half-Moon ☐ Perforated Pipe ☐ Other Lateral Material: _____

Capacity of Septic Tank _____ gals Number of Absorption Beds: _____ Number of Distribution Laterals per Bed _____

Total Length of Laterals _____ ft. Number of Trenches _____ Trench Width _____

D. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	25 ☐	20 ☐	15 ☐	25 ☐	☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	30 ☐	20 ☐	30 ☐	40 ☐	☐
Lagoon (ft)	100+ ☑	500+ ☑	50+ ☑	N/A ☐	30+ ☑	50+ ☑	100+ ☑	200+ ☑	☐

E. Required Signatures

Home Building Contractor Harold Heiser Date 4-7-97

Installer Ben Barnes Jr Date 4-7-97

FORM 23-102 10-96

APR 2 8 1997

D

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

Permit Number:

Jim Gosey

Sewage Disposal System

As Built Plans & Specifications

LAGOON SYSTEM

Date 4/23/97

System Location (Indicate correct number and street)

Address _____ City _____ NE, Zip _____
(no rural route)

A. Building Sewer

1. Material: 4" sch 40 PVC
   Diameter: _____ in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: _____ ft.
4. Number of clean-outs: _____
5. Distances to: well or suction line _____ ft.
   stream _____ ft.
   pressure line _____ ft.
   property line _____ ft.

B. Septic Tank

1. Material: _____
   Number of compartments: _____
2. Capacity: _____ gal.
3. Factory built: ❑ Yes ❑ No
4. Manholes: Over inlet, diameter _____ in.
   Over outlet, diameter _____ in.
   Riser: ❑ above ❑ below grade _____ in.
5. Inlet: ❑ baffle ❑ tee
6. Outlet: ❑ baffle ❑ tee
7. Depth to top of tank, below unfinished grade: _____ in.
8. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.

C. Distribution Box

1. Material: _____
   Number available outlets: _____
2. Factory built: ❑ Yes ❑ No
3. Distance from septic tank: _____ ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ❑ Half rounds ❑ Perforated pipe
   Diameter of half round: _____
   or perforated pipe: _____
   Material: ❑ fiberglass ❑ plastic ❑ concrete
   ❑ other _____
2. Lateral lines: Number _____
   Length of each line: _____ ft. _____ ft.
   _____ ft. _____ ft., _____ ft.
3. Trench dimensions: Width _____ ft.
   Slope _____ in/100 ft.
   Average depth _____ in
4. Filter material: _____
   Depth of material _____ in.
5. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.

Complete "As Built" drawing on back of this form.

Indicate North with Arrow


Individual Sewage System Design (Example)

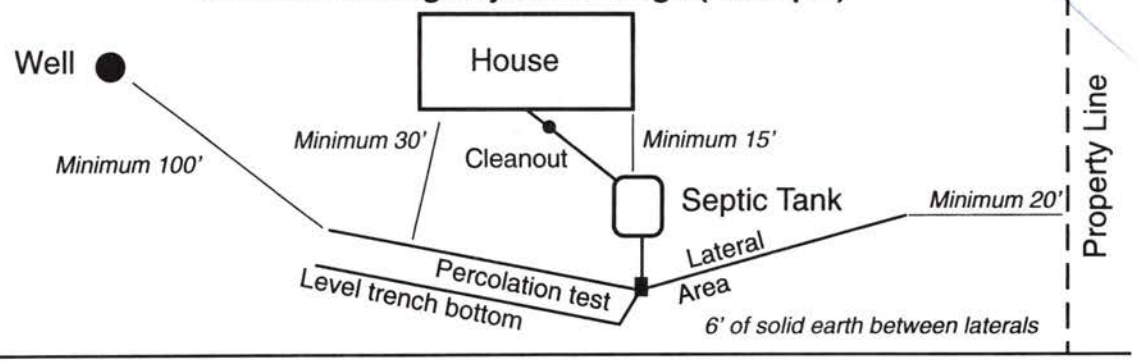

FORM 23-103 10-96

As Built Drawing

Jim Gosey

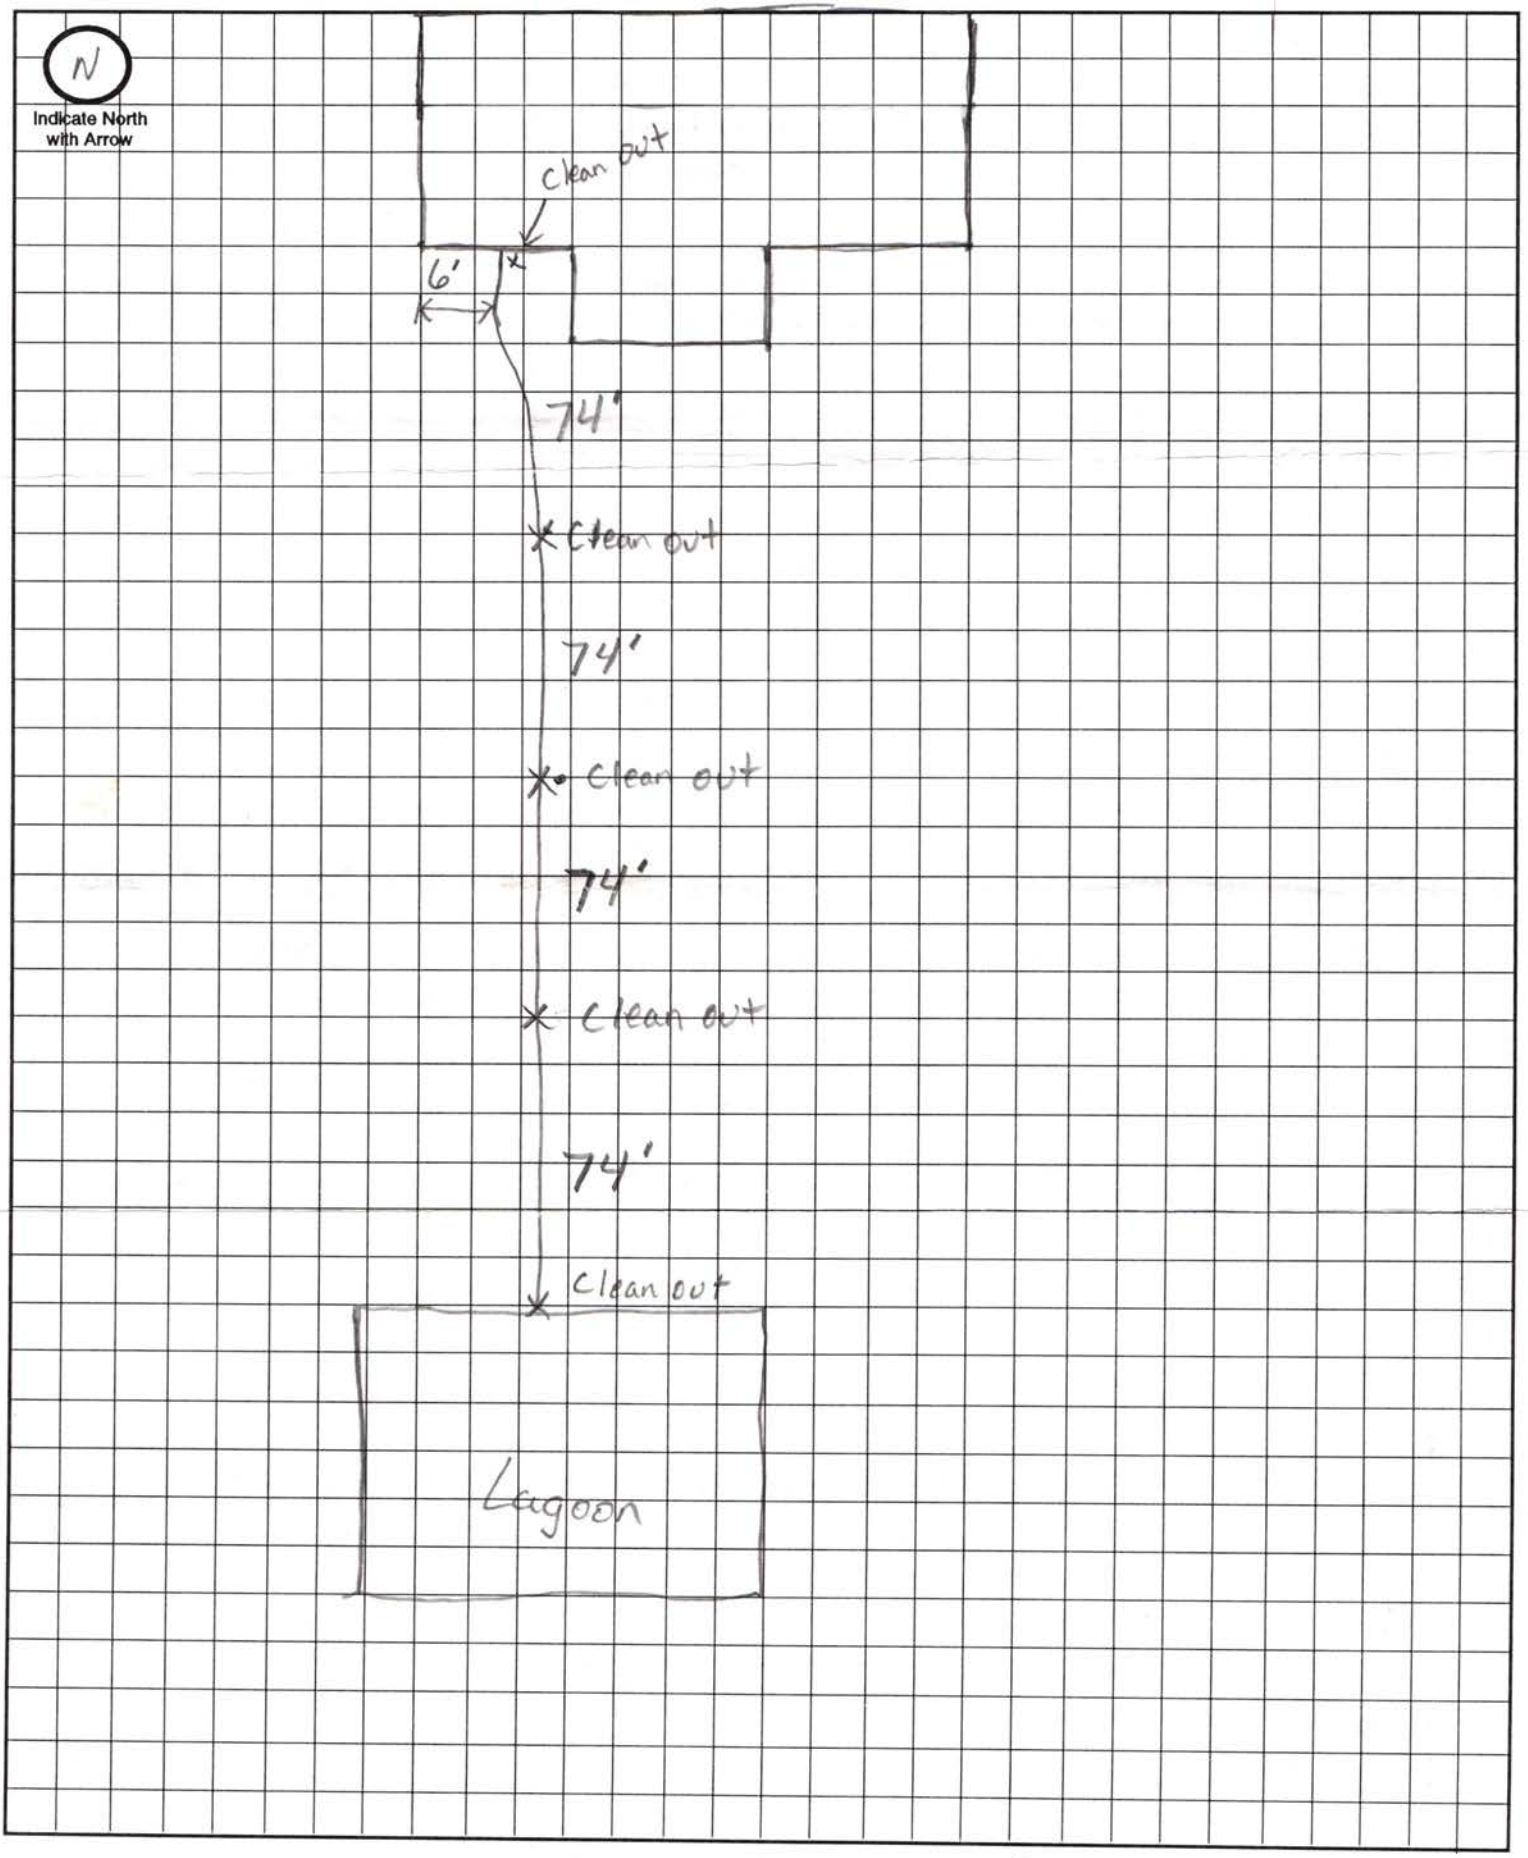

Approximate Scale: _____ ft. = _____ grid line/s
