Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
HS001214

New Construction

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☒ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 13700 W Bluff Rd (no rural route) City Malcolm, NE Zip 68402

Legal Description: SW (1/4) 1/4 | 18 Section | 11N Township | 5E Range | Elk Creek Estates Subdivison | Addition | 3 Block | Lot

PID 05-18-301-003-000

B. Owner

Name Synergy Homes Inc Signature Maria Sorensen

Address 5410 NW Fairway Dr. City/State/Zip Lincoln NE 68521

Home Phone _____ Work Phone 402-499-3496

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature Lloyd L. Jakoubek

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number: _____

Designer Name _____ Firm _____ Work Phone _____

E. This system will serve a

☒ Residential Dwelling Number of Bedrooms 5 Whirlpool Bathtub? ☐ Yes ☒ No Total Acres 3.65

Garbage Grinder? ☒ Yes ☐ No

☐ Commercial Establishment/Other Facility Specify _____ Design flow in gallons per day _____

Type of Wastewater ☐ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits _____ Date rec'd _____ ACTION ☐ Approved ☐ Disapproved
Date frwd _____ Signature _____
Comments _____

2. Supt. Bldg. Insp. or Village Clerk
Comments _____ Date rec'd _____ ACTION ☐ Approved ☐ Disapproved
Date frwd _____ Signature _____

3. City or County Engineer
Comments _____ Date rec'd _____ ACTION ☐ Approved ☐ Disapproved
Date frwd _____ Signature _____

Installation Final Written Approval
By _____
Date _____

Business Office Use Only
Date Received 3-23-16 Amount Paid $385.00
Received By SB Cash/Check No. 8854

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 1/13

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number: HS001214

Onsite Wastewater Treatment System

Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 13700 W Bluff Rd (no rural route) City Malcolm NE, Zip 68402

Owner Synergy Homes, Maria Semerad Address 5410 NW Fairway Dr, Lincoln, NE 68521

Date of Tests 3/10/16 to 3/11/16 Weather: Precipitation 0 Temperature 66°

Percolation Test Data Table

A.	B.	C. D. E. F. Saturation/Swelling Time				G. H. I. J. K. Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					L. M. N. Results		
		Start		End		Start		Initial Water Lev (in.)	End		Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)		Date (Mo/Da)	Time (Hr/Min)			
1	20	3/10	12:15p	3/10	4:15p	3/11	2:45p	6	3/11	3:15p	30	0	---
2	24	"	"	"	"	"	"	6	"	"	"	0	---
3	30	"	"	"	"	"	"	6	"	"	"	1	30
4	24	"	"	"	"	"	"	6	"	"	"	1/8	240
								6					
								6					
								6					
								6					

Person Conducting Percolation Test

Name: Terri L Jakoubek, Raymond Contracting, Inc.

Phone: 402-783-2663 or 402-890-6009

Address 13800 NW 70th St

Raymond, NE 68428 Cert #1198

Sum of Percolation Rates: 270

Average of Rates: 135

Rate Used for Calculation: Failed

Soil type (NRCS Maps/Other) Pawnee Clay Loam

Groundwater Depth >8

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.) _____

Signature of Reviewing Official _____ Date _____

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number: HS001214

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

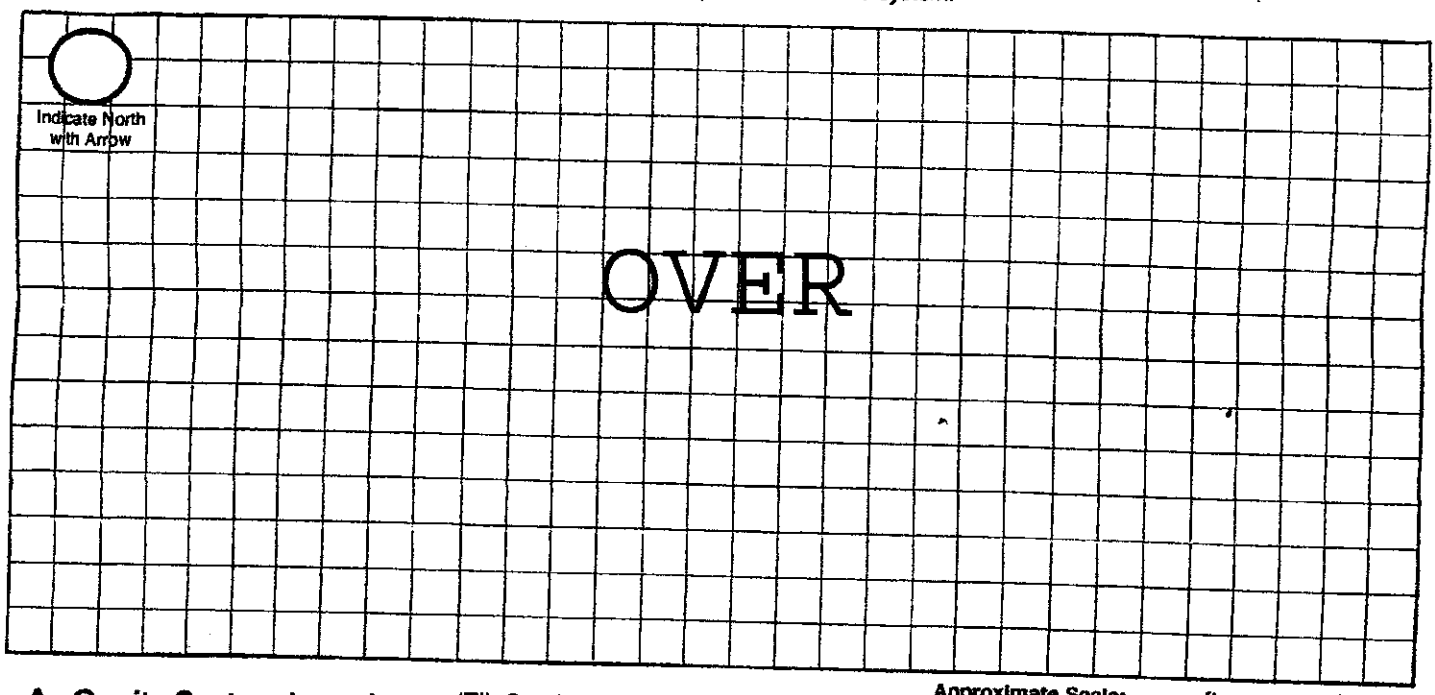

Approximate Scale: _____ ft. = _____ grid line/s

A. Onsite System Location (Elk Creek Estates, Lot 2)

Address (no rural route) 13700 W Bluff Rd City Malcolm NE, Zip 68402

B. Proposed Septic Tank/s

Septic Tank Cap. 2,000 gals Tank Material: ☒ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percoloation test required) ☒ Lagoon

D. Drainfield Absorption System

Percolation Rate 60 (min/inch = mpi) No. of Bedrooms 5 Soil Type Clay Loam/Silty Clay Loam Land Slope_____%

☒ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield 1,760 sq.ft.

Total length of laterals 485' Type of distribution: ☐ Perforated pipe ☐ Half-Round ☒ Chamber ☐ Other

No. of absorption trenches_____ Width 40" No. of drop boxes 2 Distrubtion Box_____

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____


E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	25 ☒	20 ☒	15 ☒	25 ☒	☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	30 ☒	20 ☒	30 ☒	40 ☒	☒
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures

Home Building Contractor Mark A Sorensen Date 3-16-15

Installer Dennis L. Dahlquist Date 3/23/16

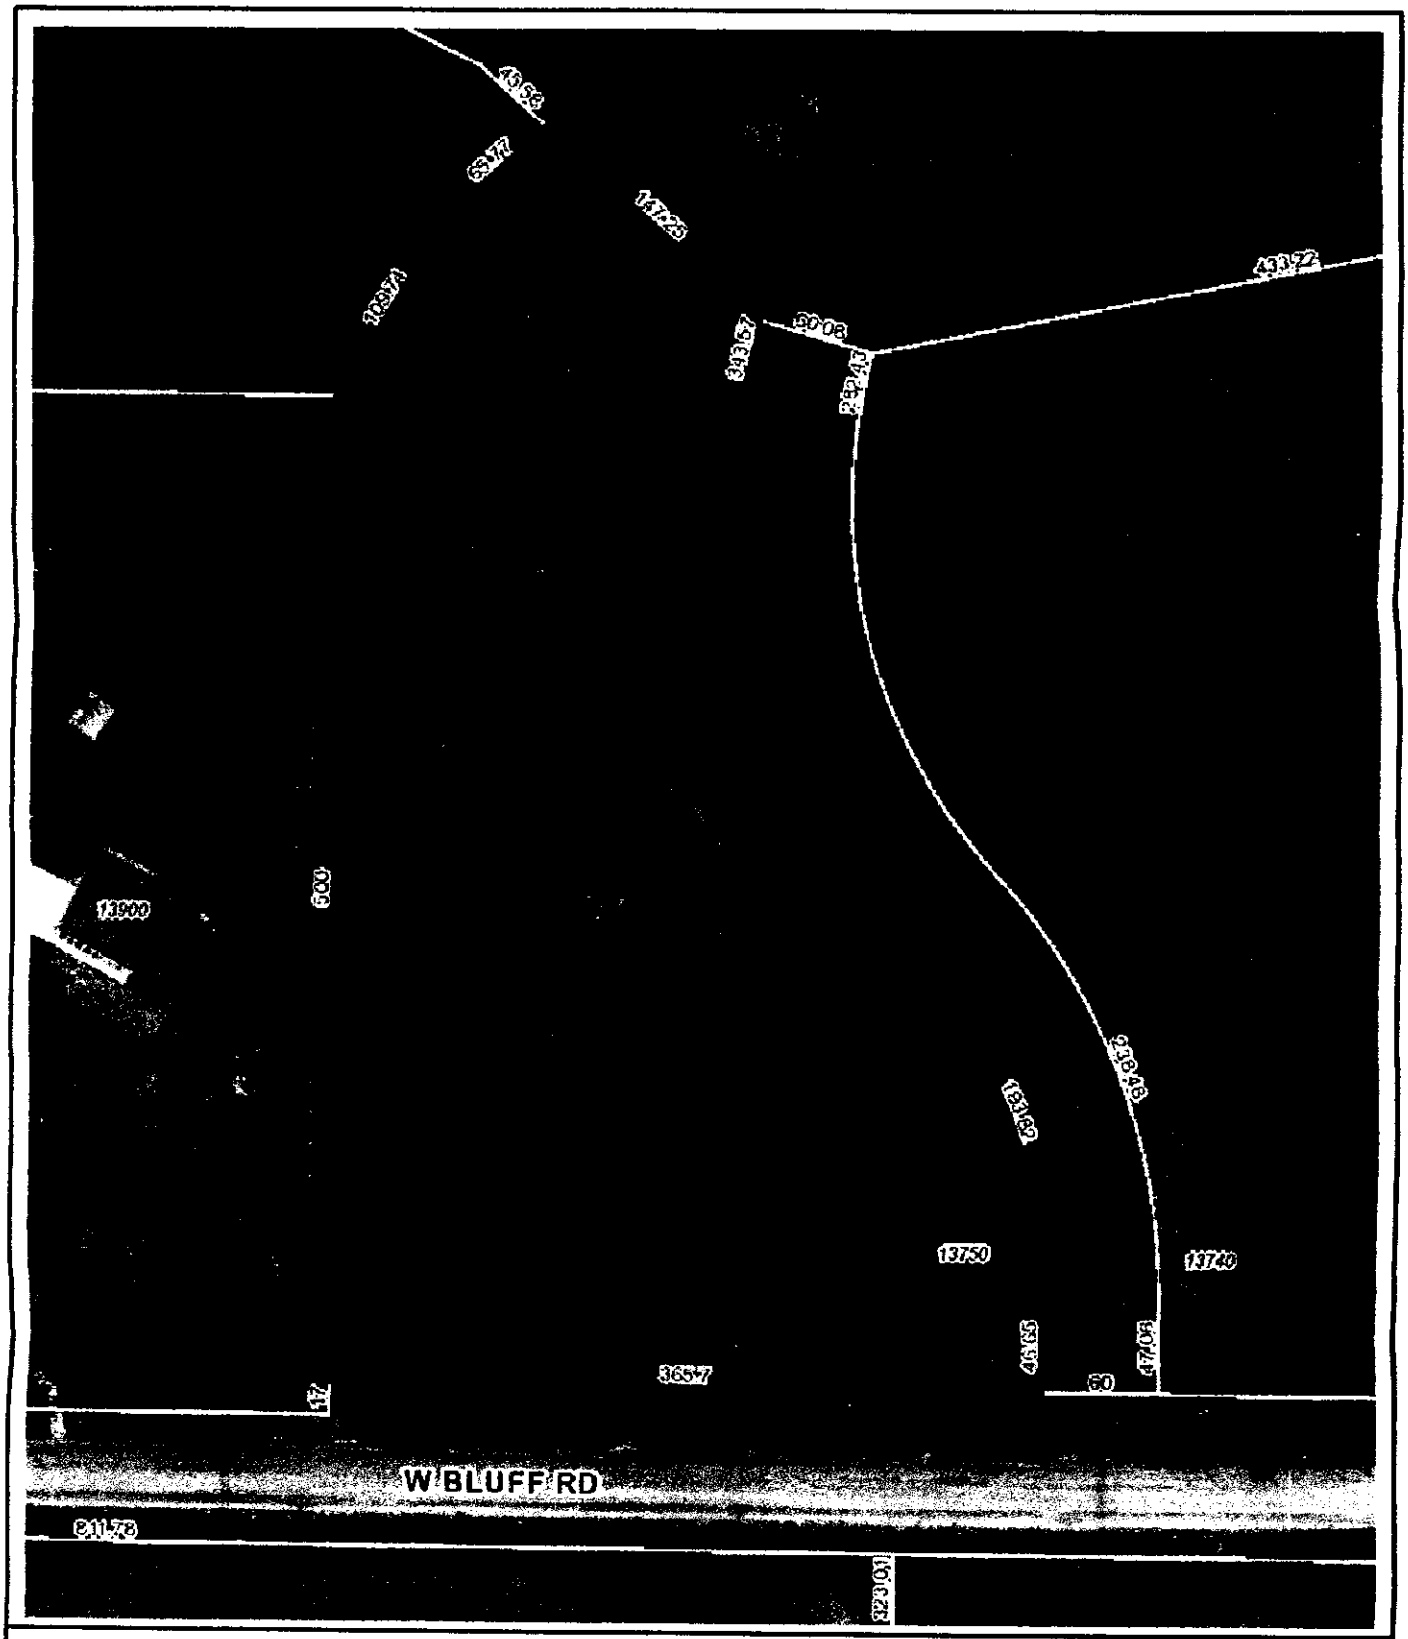

Lancaster County/City of Lincoln GIS Map

13700 W Bluff Rd - Synery

N
W E
S

Printed: Mar 17, 2016

DISCLAIMER: The information is presented on a best-efforts basis, and should not be relied upon for making financial, survey, legal or other commitments. If you have questions or comments regard data displayed on this map, please email ags@lincoln.ne.gov and you will be directed to the appropriate department.

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
HS001214

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C.
Submit correct fee
with this Application

3 acres or more required for: ☐ Septic System ☒ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 13700 W Bluff Rd (no rural route) City Malcolm, NE Zip 68402

Legal Description SW (1/4) 18 (Section) 11N (Township) 5E (Range) Elk Creek Estates (Subdivison) 2 (Block)

PID 05-18-301-002-000

B. Owner

Name Synergy Homes Inc Signature Melissa Semerad

Address 5416 NW Fairway Dr. City/State/Zip Lincoln NE 68521

Home Phone Work Phone 402-499-3496

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature Lloyd Jakoubek

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☒ Residential Dwelling Number of Bedrooms 5 Whirlpool Bathtub? ☐ Yes ☒ No Total Acres 3.65

Garbage Grinder? ☒ Yes ☐ No

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day

Type of Wastewater ☐ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date

Business Office Use Only
Date Received Amount Paid
Received By Cash/Check No.

White - Health Department Yellow - Engineer Pink - Building & Safety

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number: HS001214

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

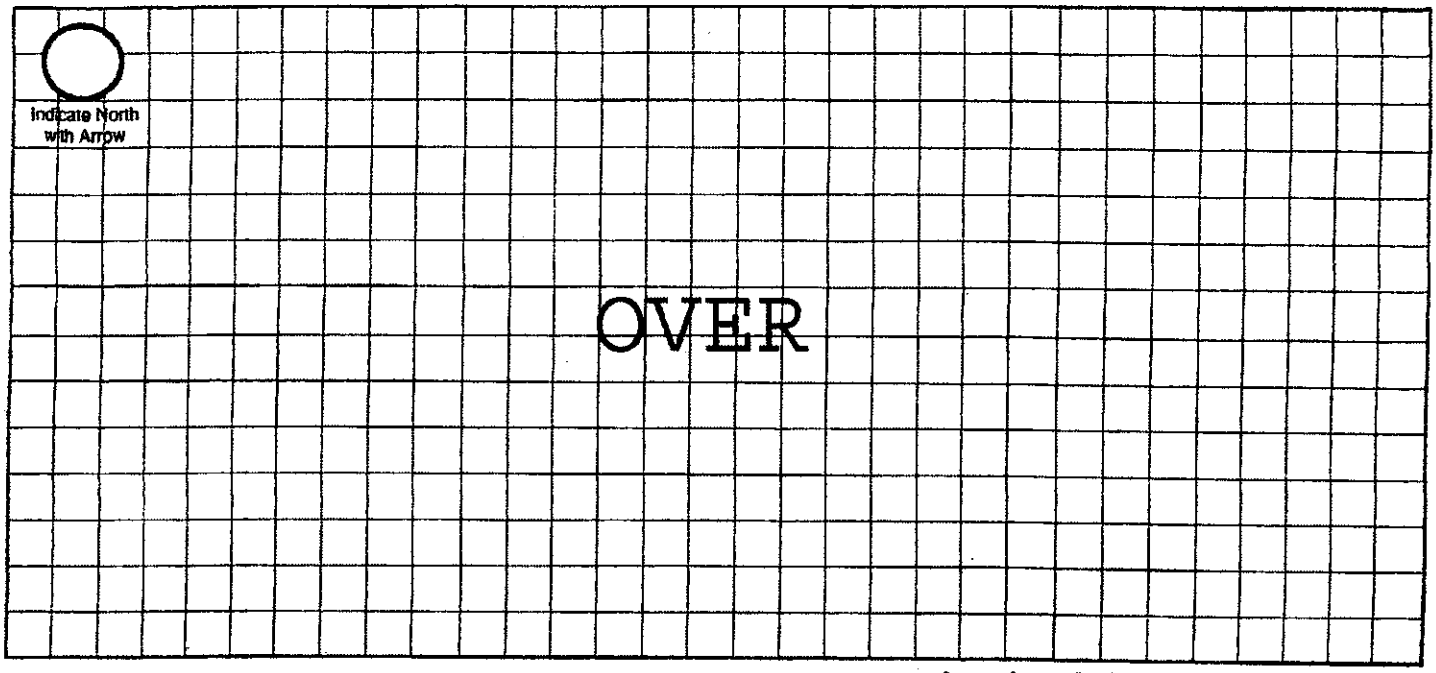

Approximate Scale: _____ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 13700 W Bluff Rd City Malcolm NE, Zip 68402

B. Proposed Septic Tank/s

Septic Tank Cap._____ gals Tank Material: ☐ Concrete ☐ Plastic ☐ Other_____ ☒ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percolation test required) ☒ Lagoon

D. Drainfield Absorption System

Percolation Rate_____ (min/inch = mpi) No. of Bedrooms_____ Soil Type_____ Land Slope_____%

☐ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield_____sq.ft.

Total length of laterals_____ Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☐ Other

No. of absorption trenches_____ Width_____ No. of drop boxes_____ Distrubtion Box_____

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____

E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	25 ☐	20 ☐	15 ☐	25 ☐	☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	30 ☐	20 ☐	30 ☐	40 ☐	☐
Lagoon (ft)	100 ☒	500 ☒	50 ☒	N/A ☒	30 ☒	50 ☒	100 ☒	200 ☒	☒

F. Required Signatures

Home Building Contractor Marvin A Sorensen Date 3-16-15

Installer [signature] Date 3/23/16

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001214

System Type: Lagoon

Situs: 0518301003000

Issued: 3/31/2016

Expires: 3/31/2017

Description: ELK CREEK ESTATES ADDITION, Lot 3

Owner: SEMERAD, ANDREW J & MARIA A
13600 W BLUFF RD
MALCOLM, NE 68402

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead
Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH ST
RAYMOND, NE 68428

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

6/4
7/19/16 qf

Exhibit 6

Permit Number: HS00 1214

Onsite Wastewater Treatment System-Lagoon

Inspection Sheet

Lot 2

Date 7/19/16 Legal Description ____ ¼ ____ ¼ 18 / 4 / 5 Section/Township/Range

Onsite System Location

Address (no rural route) 13750 W. Bluff City ____

Owner ____ Address ____

Mark One: ☒ Dwelling ☐ Non-dwelling

☒ New System ☐ Repair

☐ Temporary modification (Describe problem causing discharge and reason for temporary modification): ____

Lagoon constructed so not to receive surface water	Yes X No ___
Lagoon floor is level	Yes X No ___
Lagoon is equipped with a depth gage/concrete slab	Yes X No ___
Influent line is at least 4 inches and slopes no less than 1/8 inch	
Clean outs located every 75 feet and one located 1 foot about highest water level	Yes X No ___
Inside slope not steeper than three horizontal to one vertical	Yes X No ___
Minimum width of the top of the dike shall be 4 feet	Yes X No ___
Fence installed	Yes X No ___

Top of the Dike 70' Bottom of Lagoon 34' Design Flow 450

Setbacks (Check the Boxes Below if the Required Setback has been Satisfied):

Surface Water distance from Water Mark	Private Drinking Water Wells	Public Drinking Water Supply Wells		All Other Water Wells	Property Lines	Trees and Brush	Neighbor's Foundation		All Other Setbacks
50 ft ☑	100 ft ☑	Non-Community	100ft ☑	100ft ☑	50ft ☑	50ft ☑	Class 1	200ft ☑	☑
		Community	* ☑				Class 2	200ft ☐	
							Class 3	100ft ☐	

*Evaluated by a professional engineer for potential impact on the well and submitted to Dept. for approval if less than 1000ft.

Geographical Coordinates to 6 Decimals: N/A

Dike North side

Comments:

Inspections prior to Final Approval
Initial DF Date 7/13/16

Follow-Up ____ Date ____

Follow-Up ____ Date ____

Installation Final Written Approval
By [signature]
Date 7/19/16

Updated 4/15
