Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
HSOD1534

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C.
Submit correct fee
with this Application

3 acres or more required for: ☒ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 5100 W Mulberry Cir (no rural route) City Lincoln, NE Zip 68522

Legal Description NW (1/4) 31 (1/4) Section 10N Township 6E Range High Ridge West Acres Subdivison 4 Addition 3 Block Lot

PID 10-31-101-009-000

B. Owner

Name Pamela J Livingston Signature Pamela J Livingston

Address 5100 W Mulberry Cir City/State/Zip Lincoln, NE 68522

Home Phone 402-730-0401 Work Phone

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☒ Residential Dwelling Number of Bedrooms 3 Whirlpool Bathtub? ☒ Yes ☐ No Total Acres 3.06
Garbage Grinder? ☐ Yes ☒ No

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day

Type of Wastewater ☐ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date

Business Office Use Only
Date Received 9-12-17 Amount Paid 405.00
Received By LC Cash/Check No. CC

7152

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 1/13

3 bedroom

Lot 3 - Block 4

High Ridge West acres

5100 W Mulberry Cir.

22 - 23 1/2 = 1 1/2

22 1/2 - 23 3/4 = 1 1/4

24 - 26 = 2

24 - 25 1/2 = 1 1/2

16 - 16 1/2 = 1/2

20 1/2 - 21 3/4 = 1 1/4

1.3333

23 MIN
222' lateral 3' wide

On File @ LLCHD

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

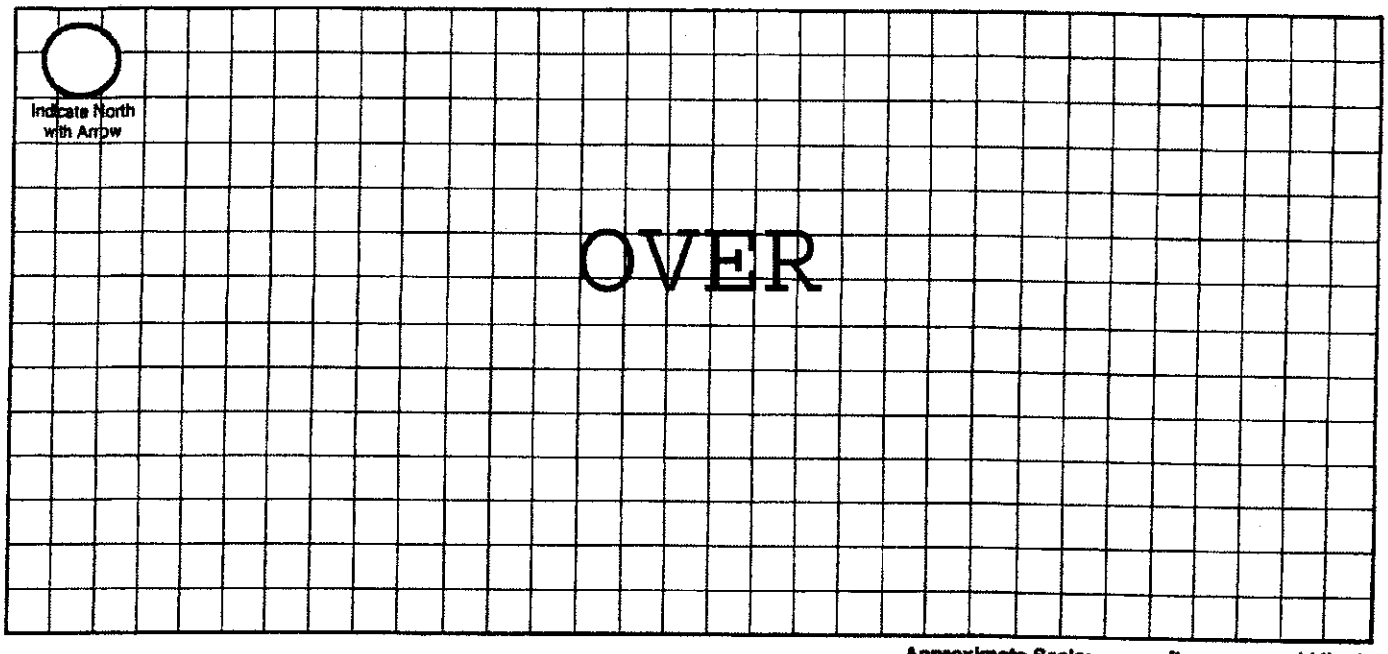

Approximate Scale: _____ ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 5100 W Mulberry Cir City Lincoln NE, Zip 68522

B. Proposed Septic Tank/s

Septic Tank Cap. 1,500 gals Tank Material: ☒ Concrete ☐ Plastic ☐ Other _____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percolation test required) ☒ Lagoon

D. Drainfield Absorption System

Percolation Rate 60 (min/inch = mpi) No. of Bedrooms 3 Soil Type CL/SCL Land Slope _____ %

☒ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield 1,080 sq.ft.

Total length of laterals 240 Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☒ Other EZFlow 1203H

No. of absorption trenches 2 Width 40" No. of drop boxes 1 Distrubtion Box _____

No. of absorption beds _____ Width _____ No of Distribution lines per bed _____

E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	25 ☒	20 ☒	15 ☒	25 ☒	☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	30 ☒	20 ☒	30 ☒	40 ☒	☒
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures

Home Building Contractor Existing Home Date _____

Installer Kevin L Fakenbel Date 9/11/17



N
W E
S

Lancaster County/City of Lincoln GIS Map

5100 W Mulberry Cir, Lincoln, NE 68522

Printed: Sep 11, 2017

DISCLAIMER: The information is presented on a best-efforts basis, and should not be relied upon for making financial, survey, legal or other commitments. If you have questions or comments regarding the data displayed on this map, please email age@lincolnne.gov and you will be directed to the appropriate department.

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001534

System Type: Standard

Situs: 5100 W MULBERRY CIR, RURAL, NE

Issued: 9/15/2017

Expires: 9/15/2018

Description: HIGH RIDGE WEST ACRES, BLOCK 4, Lot 3

Owner: LIVINGSTON, DAVID E & PAMELA J
5100 W MULBERRY CIR
LINCOLN, NE 68522

Shavonna M. Lausterer, MPH, CPH, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Shavonna M. Lausterer, MPH, CPH
Health Director

RAYMOND CONTRACTING INC
13800 NW 70 ST
RAYMOND, NE 68428
