LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

3140 "N" STREET
Lincoln, NE 68510-1514
(402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 95380128401

Issued 03/14/95
Expires 09/14/95
Revenue Code 18754

Establishment
ED BENES
T8N R7E SEC 30
3501 MARTELL ROAD

FEES: $150.00

TOTAL $150.00

Permittee
ED BENES
3501 MARTELL RD
ROCA NE 68430

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

Lincoln-Lancaster County
HEALTH DEPARTMENT
3140 "N" STREET LINCOLN, NE 68510-1514

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 7E ; Section 30 ; SEE ATTACHED N½N½
   Block _____ : Lot 28 I.T. : Addition _____
   Street Address 3501 MARTELL ROAD

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms _____. Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒

4. Distance to public sewer: _____ ft.

792-2086

ED BENES
Signature of Applicant (Owner or Lessee)

3501 MARTELL ROAD, ROCA, NE. 68430
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 3/14/95. Date Frwd. 3/14/95. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 3/14/95. Date Frwd. 3/14/95. ACTION: Approved ☒ Disapproved ☐ Signature: [signature]
3. City or County Engineer: Date Rec'd. 3/14/95. Date Frwd. 3/14/95. ACTION: Approved ☒ Disapproved ☐ Signature: [signature]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 8-3-95 by: P.D
Date: 8/16/95 by: J.C.H.
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 8/15/95 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23 43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material C plastic; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 16 in.
3. Distance between dwelling and ~~septic~~ Lagoon tank 300 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line 400 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material _____; No. of compartments _____.
2. Capacity _____ gals.;
3. Factory Built: Yes ☐ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number ___ ; Length of each line _____, _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width _____ ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: _____
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

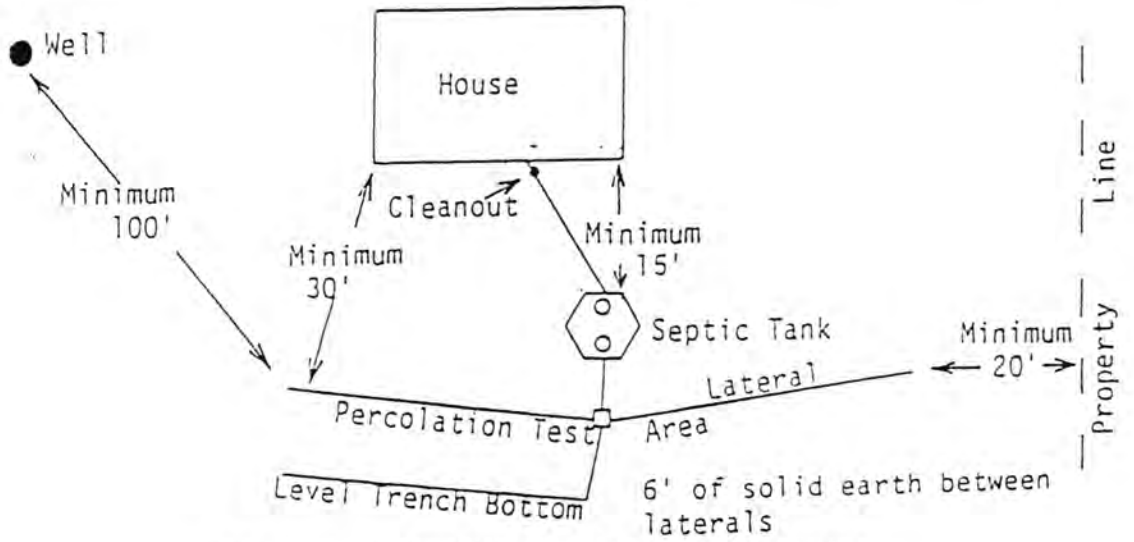

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

SURVEY RECORD

LANCASTER COUNTY, NEBRASKA

Survey of N½ N½


Section 30 T. 8 N., R. 7 E. of 6th P.M.

County Survey No. _____

Date OCT. 17 1992 Weather _____

● = CORNERS FOUND

○ = SET 5/8" REBARS

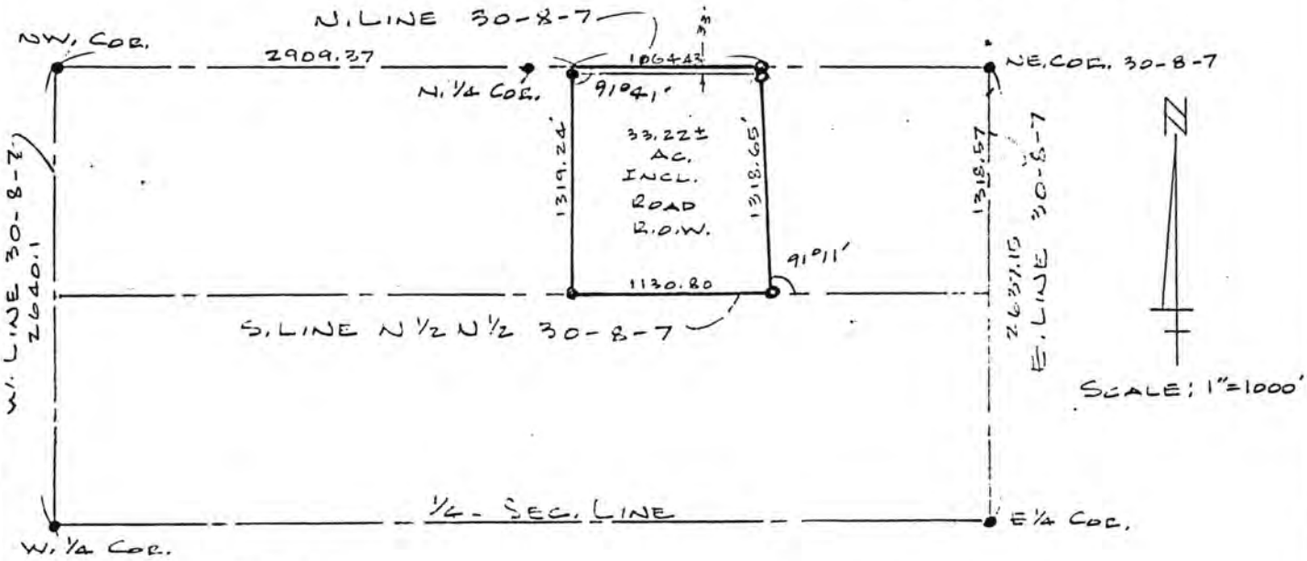

CORNER TIES:

E. ¼ COR. - CONC. CYL.
E. 32.33' – 1" I.P. W/CAP
W. 33.00' – ½" REBAR
SE. 50.0' – ½" REBAR W/CAP
E. 33' – POW. LINE SO.
W. 33' – POW. LINE NO.

NE. COR. – 1" I.PIPE W/CAP
E. 44.00' – 1" I.PIPE W/CAP
NW. 50.00' – ½" REBAR W/CAP
SW. 40.00' – ½" REBAR W/CAP
W. 26' – N-S POW. LINE

N ¼ COR. – 1" I.PIPE W/CAP
N. 33.00' – 1" I.PIPE W/CAP
S. 33.00' – 1" I.PIPE W/CAP
SW. 50.00' – ½" REBAR W/CAP
E. 6' – FIELD DR. SO.
W. 6' – FIELD DR. NO.

NW. COR. – 1" I.PIPE
W. 33.0' – 1" I.PIPE
SE. 47.7' – "X" – NAILS C.F.P.
NE. 46.25' – NAIL POW. POLE
NW. 21.22' – NEAR TOP COR. CULV. POST

W. ¼ COR. – 1" I.PIPE W/CAP
W. 33.00' – 1" I.PIPE
E. 33.08' – 1" I.PIPE
SE. 53.92' – 5/8" REBAR
NW. 49.00' – 5/8" REBAR

N ¼ NE ¼ – ½" REBAR
S. 33.0' – 5/8" REBAR
N. 32.1' – FACE C.F.P.
NNW. 33.09' – NAIL TOP BRACE POST
W. 1' – N-S FC LINE

SURVEYOR'S CERTIFICATE

I hereby certify that, to the best of my ability, I have accurately surveyed the property in the above plat. All dimensions are in feet and decimals of a foot and are chord measurements unless otherwise noted.

NEBRASKA REGISTERED LS-246 LAND SURVEYOR PAUL E. KASL


PAUL E. KASL
SURVEYOR L.S. – 246
3101 LOVELAND DRIVE
LINCOLN, NEBRASKA 68502

Signed this 19TH day of OCT. 1992

Name Paul E. Kasl

LAND SURVEYOR'S SEAL

N ↑

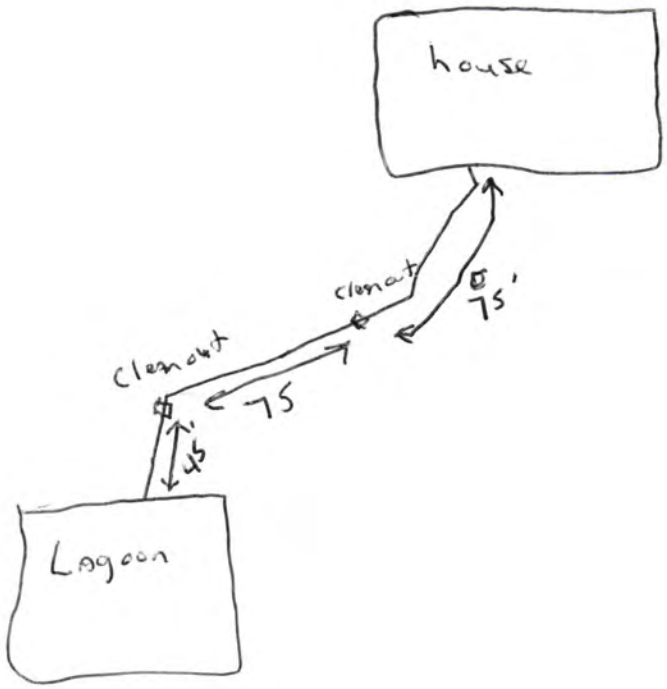

LEGAL DESCRIPTION

A part of the North Half of the Northeast Quarter of Section 30, Township 8 North, Range 7 East of the 6th P.M., Lancaster County, Nebraska, described as follows: Commencing at the Northwest corner of said Section 30; thence easterly along the north line of said Section 30, a distance of 2,909.37 feet to the Point of Beginning; thence southerly deflecting 91°41'00" right, a distance of 1,319.24 feet to the south line of the North Half of the Northeast Quarter of said Section 30; thence easterly along said south line, a distance of 1,130.80 feet; thence northerly deflecting 91°11'00" left, a distance of 1,318.65 feet to the northeast corner of the Northwest Quarter of said Northeast Quarter; thence westerly along the north line of said Northeast Quarter, a distance of 1,064.43 feet to the Point of Beginning, containing 33.22 acres more or less and including road right of way.
