LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

3140 "N" STREET Lincoln, NE 68510-1514 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 95380128901

Issued 04/06/95
Expires 10/06/95
Revenue Code 18754

Establishment
REMBOLT DEVELOPMENT
T9N R5E SEC 8
LOT 10
4601 SW 12 STREET

FEES: $150.00

TOTAL $150.00

Permittee
REMBOLT DEVELOPMENT
3743 S 48 ST
LINCOLN NE 68506

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

Lincoln-Lancaster County HEALTH DEPARTMENT
3140 "N" STREET LINCOLN, NE 68510-1514

FILING FEE: $ 150.00

FILE NO. _____

DATE: 4/5/95

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 5E ; Section 8 ;
   Block _____ : Lot 10 I.T. : Addition _____
   Street Address 4601 S.W. 112TH

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒

4. Distance to public sewer: 400,000 ft.

Signature of Applicant (Owner or Lessee)

3743 S. 48TH ST. SUITE 100
Address
LINCOLN, NE 68506
488-9222

(Do not write below this double line)

1. Health Department: Date Rec'd. 4/6/95 . Date Frwd. 4/6/95 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Nood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 4/6-95 . Date Frwd. 4/6/95 . ACTION: Approved ☒ Disapproved ☐ Signature: Amy Lyon
3. City or County Engineer : Date Rec'd. _____ . Date Frwd. _____ . ACTION: Approved ☒ Disapproved ☐ Signature: Jim Pluvgh

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 7/19/95 by: L. C. H. Need fence, etc.
Date: 11/22/95 by: L.C.H. Need signs only. Spoke with lady of house.
Date: 11/27/95 by: L.C.H.
Date: 12/4/95 by: L.C.H.

INSTALLATION FINAL WRITTEN APPROVAL
Date: 12/4/95 By: Jerrold C. Nood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23 43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 7-19-95

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 16 in.
3. Distance between dwelling and ~~septic~~ Lagoon tank 100' ft.
4. Number of clean-outs 3.
5. Distances to:
Well or Suction Line 130 ft.; Stream no ft.; Pressure Line _____ ft.; Property Line 110 ft.


B. ~~SEPTIC TANK~~: Lagoon
1. Material _____; No. of compartments _____.
2. Capacity _____ gals.;
3. Factory Built: Yes ☐ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line 200' ft.; Stream no ft.; Pressure Line _____ ft.; Property Line 60 ft.

C. DISTRIBUTION BOX:
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number ___ ; Length of each line _____, _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width _____ ft.; Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: _____.
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

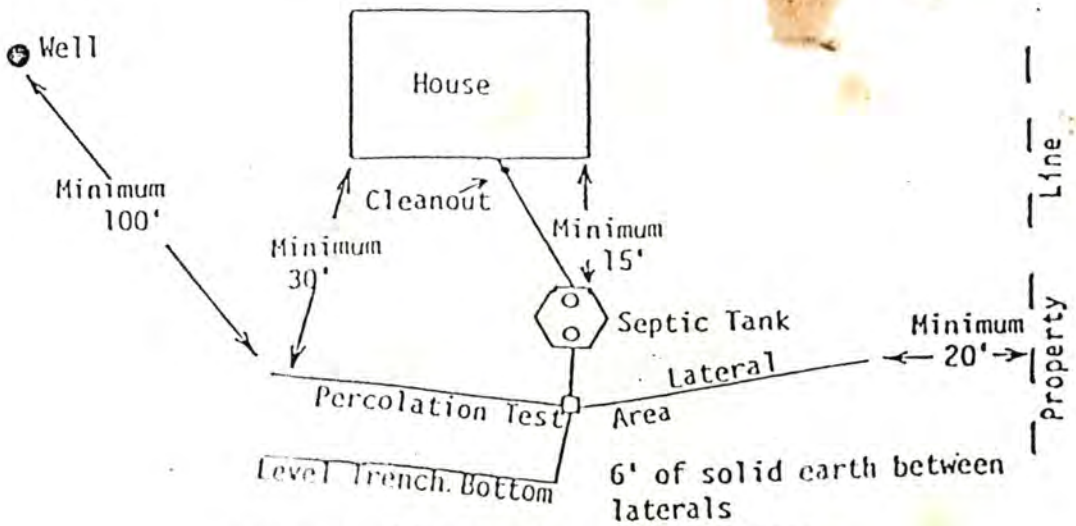

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

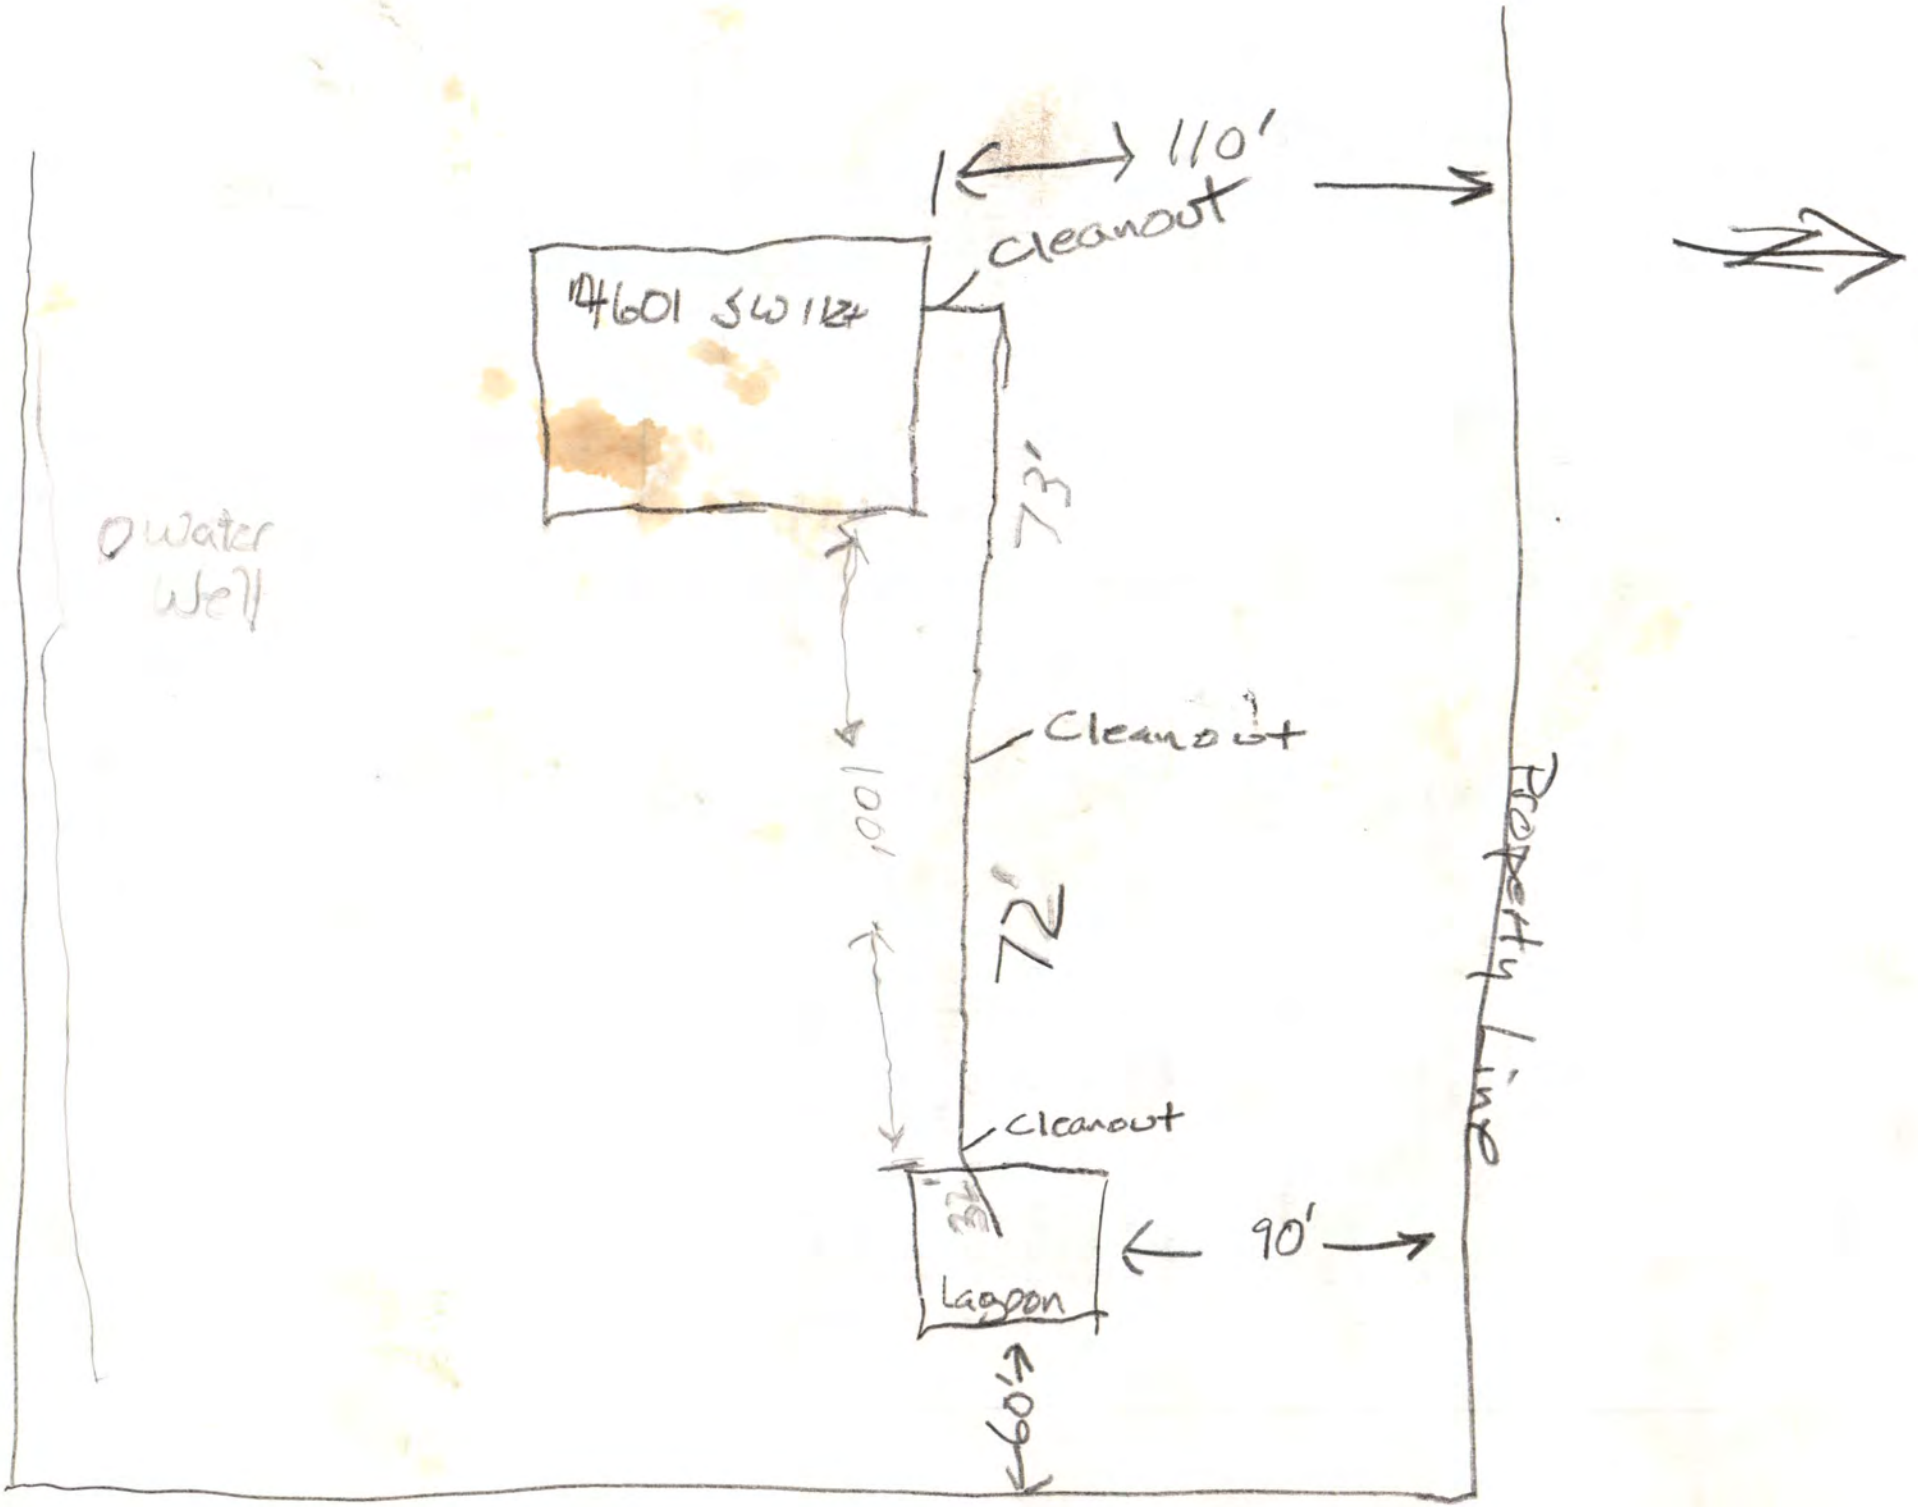
110'
cleanout
4601 SW 12th
73'
Water Well
Cleanout
100'
72'
Property Line
cleanout
90'
Lagoon
60'
