FILE No. 1612

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

April 18, 1980 — THIS LICENSE OR PERMIT EXPIRES

Sintek Service — LICENSEE OR PERMITTEE

6710 North 7th, Lincoln, NE 68508 — ADDRESS

T9N; R7E; Section 22; Block 4; Lot 3, Clarenden Hills Addition — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: NONTRANSFERABLE (Extend and Repair)

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT
53023		30.00

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION
HEALTH

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☒

County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1612

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 10-16-79

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 7E ; Section 22 ;
Block 4 ; Lot 3 ; Addition Clondara Hills
Street Address _____

2. Property Use: Residential _____ ☒; Commercial _____ ☐
No. Bedrooms 3
Describe _____
Other Use ☐
Describe _____

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: add sewer.
Bdrm & 20x lot

5. Work to be done by: Owner ☐ ; or Contractor ☐ , _____
Contractor's Name

6. Estimated cost of project:

a. Materials	$	
b. Labor	$	
c. Other	$	
TOTAL	$	

Signature of Applicant (owner or lessee)

6710 NO 7
Address

475-1484

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd: 10-16-79
Filing Fee: $ 30.00

2. Site Visits:
Date: 10-16-79 by: SM
Date: _____ by: _____
Date: _____ by: _____

3. Date: Approved ☒ ; Disapproved ☐
by: Jerold E Wood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 10-16-79 by: Ron Mayer

FORM HD-32a(67) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

T9N R7E Sec 22
Blk 4 Lot 3

FILE NO. 1612

Clorendon Hills SPECIFICATIONS

DATE: 10/18/79


A. BUILDING SEWER:
1. Material _____; Diameter 4 in.
2. Distance above basement floor 1 in.; or below basement floor 16 in.
3. Distance between dwelling and septic tank 30 ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Fiber; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth 50 in.
3. Factory Built: Yes ☒ (Company CORRIGATED FIBERGLASS) No ☐
4. Manholes: Over Inlet; diam. 12 in.
Over Outlet; diam. ___in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade 24 in.
8. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.


C. DISTRIBUTION BOX
1. Material Concrete No. available outlets 6.
2. Factory Built: Yes ☒ (Company PRE-CAST STEP) No ☐
3. Dimension: Length ___in.; Width ___in. Depth ___in.
4. Distance from Septic Tank ____ft.
5. Serial Distribution: Yes ☐, No ☒ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: Half Round
2. Lateral Lines: Depth below grade ___in. Number 2; Length of each line 100 ft Total length of Laterals 199 ft.; Slope 4 in/100 ft. Diameter of pipe 16 in.; Shape O
Material: concrete ☐; fiber asbestos ☐; clay ☐; other FIBERGLASS
Distance between lateral lines ____ft.
3. Trench Dimensions: Depth 36 in.; Width 48 in.
4. Filter Material: GRAVEL.
Depth of material from trench bottom _____in.
5. Distances To:
Well or Suction Line ____ft.;
Stream _____ft.; Pressure Line ____ft.
Property Line ____ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

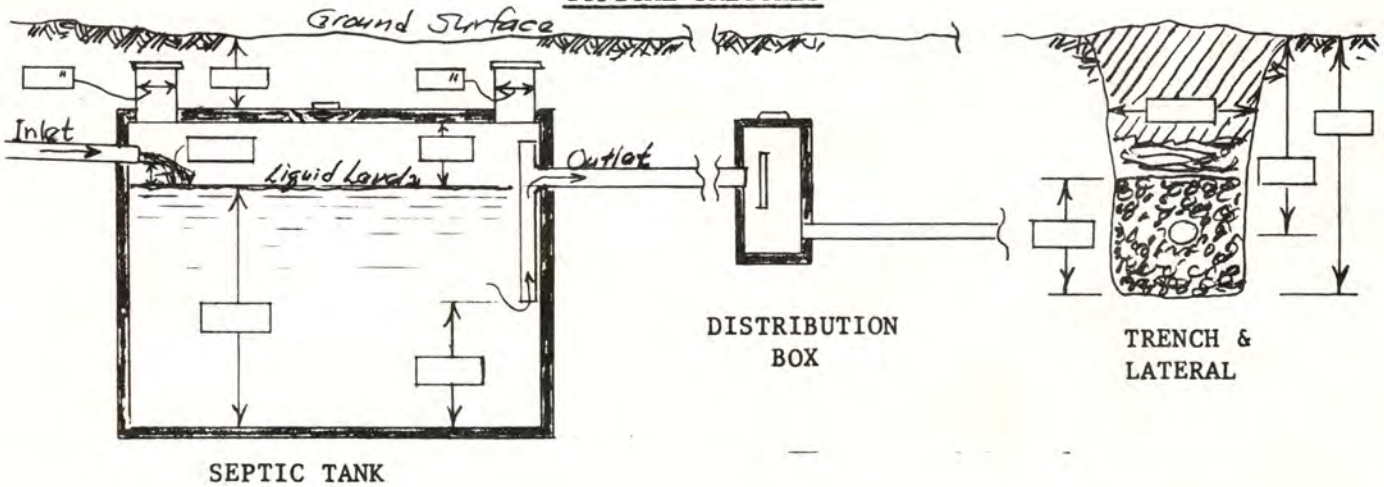

Signature of Applicant

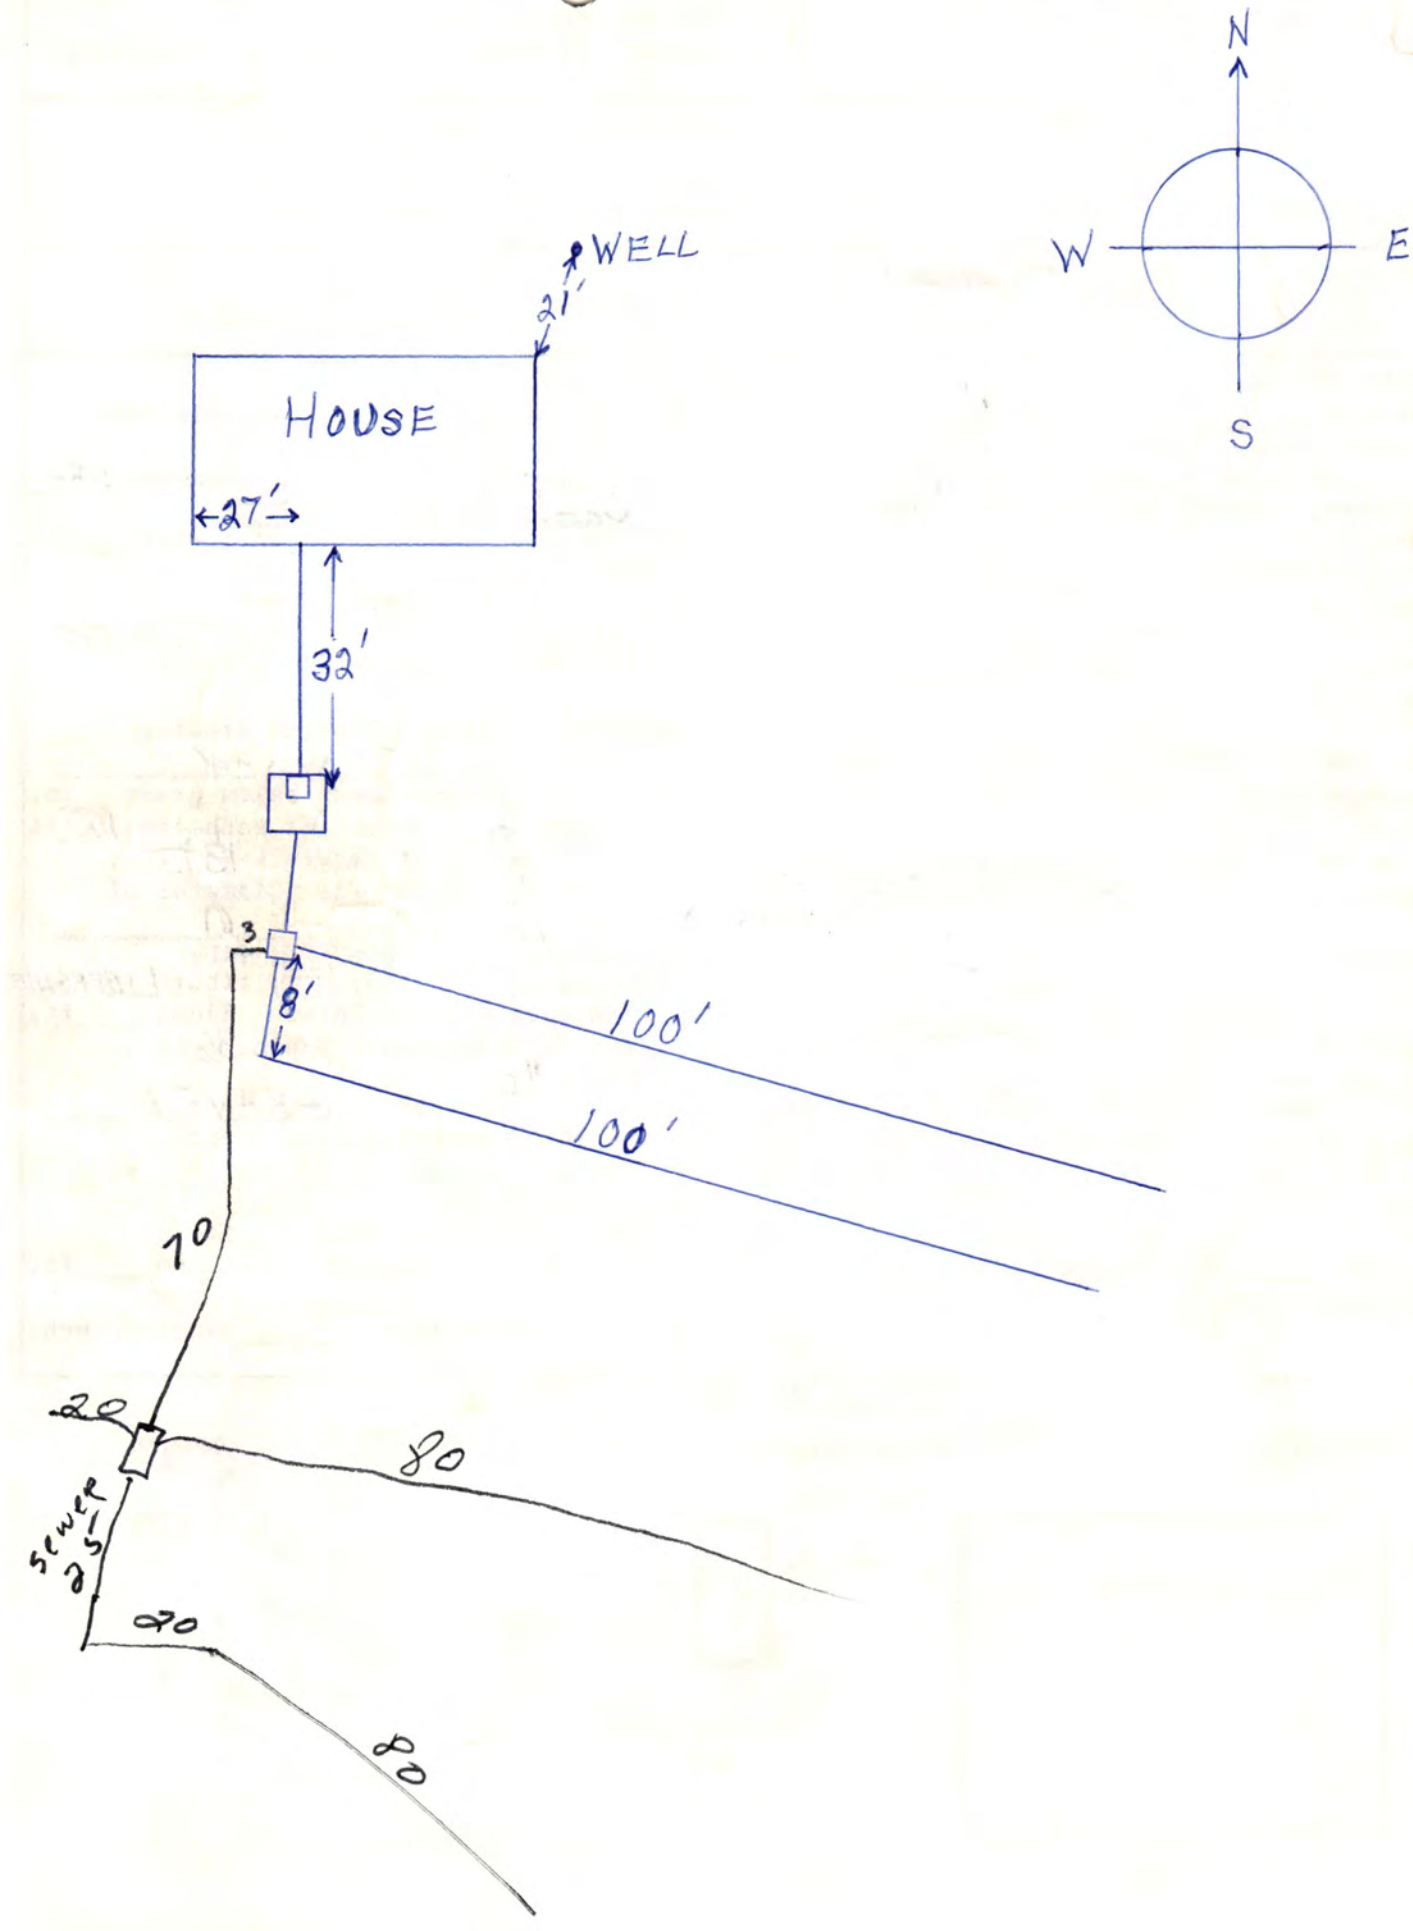
N
W
E
S
WELL
21'
HOUSE
27'
32'
3
8'
100'
100'
10
20
80
SEWER
25'
90
80
