CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

FILE NO. 1315

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — November 12, 1978

TYPE OF LICENSE OR PERMIT — THIS LICENSE OR PERMIT EXPIRES

Paul Van DeWater %Griffiths Builder , 3426 O Street, Lincoln, NE

LICENSEE OR PERMITTEE — ADDRESS

T9N, R7E, Section 22, Bl 4, Lot 2, Clarendon Hills First Addition

NAME OF ESTABLISHMENT, IF ANY — ADDRESS

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
110.15	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT
624-1535		

APPLICATION
HEALTH

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 30.00

FILE NO. 1315

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 22 ;
   Block 4 : Lot 2 : Addition ~~[illegible]~~ CLARENDON HILLS FIRST ADDITION
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒

4. Distance to public sewer: _____ ft.

Paul VandeWater
Signature of Applicant (Owner or Lessee)

3426 Ost
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 5/12/78. Date Frwd. 5/12/78. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 5/12/78. Date Frwd. 5/12/78. ACTION: Approved ☐ Disapproved ☐ Signature: [illegible]

3. City or County Engineer: Date Rec'd. 5/12/78. Date Frwd. 5/12/78. ACTION: Approved ☒ Disapproved ☐ Signature: Dennis D Bartels

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 7-14-78 by: [illegible]
Date: 7-18-78 by: [illegible]
Date: 7/25/78 by: J.C.H.

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 7/25/78 By: Jerrold C. Hood *

* Provisional approval only
System installed is considered experimental only.

Dave Griffith Bldrs

FORM HD-43 (73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 474-1541)

FILE NO. 1315

PROPERTY WHERE SOIL TESTED:
Location: Township 9 : Range 7
Section & ¼ Sect. 22 NE
Property Dimensions: ____ ft. x ____ ft.
Area: ____ acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ; Silty Clay Loam ; Sandy Loam
Silty Loam ; Clay Loam ; Sandy Clay

Owner: Paul Vandewater
Address: 3426 Ost

Dates of Tests: april 26-78 to april 27-78 Weather: Precip. T Temp. 50°

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	32"	4/26	5 39 PM	4/27	5 39 PM	4/27	5 39 PM						
2													
3								Water in all holes from Pre Soak					
4													
5													
6													

Robert D Johnson
Signature of Person Conducting Test

Address 2618 no 33rd
Phone 432-3595

Sum of Percolation Rates: ____
Average of Rates: ____
Mean of Rates: ____

(Do not write below this line)

REVIEWING ACTION

REMARKS: Pawnee Clay Loam or Wymore Silty Clay Loam


DATE: May 12, 1978

Approved Percolation Rate (a)
A. ____ min./inch
B. ____ min./inch
C. ____ min./inch

Gerald C. Hood
Signature of Reviewing Official

AS BUILT DRAWING OF SYSTEM

DATE 7-24-78 INSTALLER Smith Service

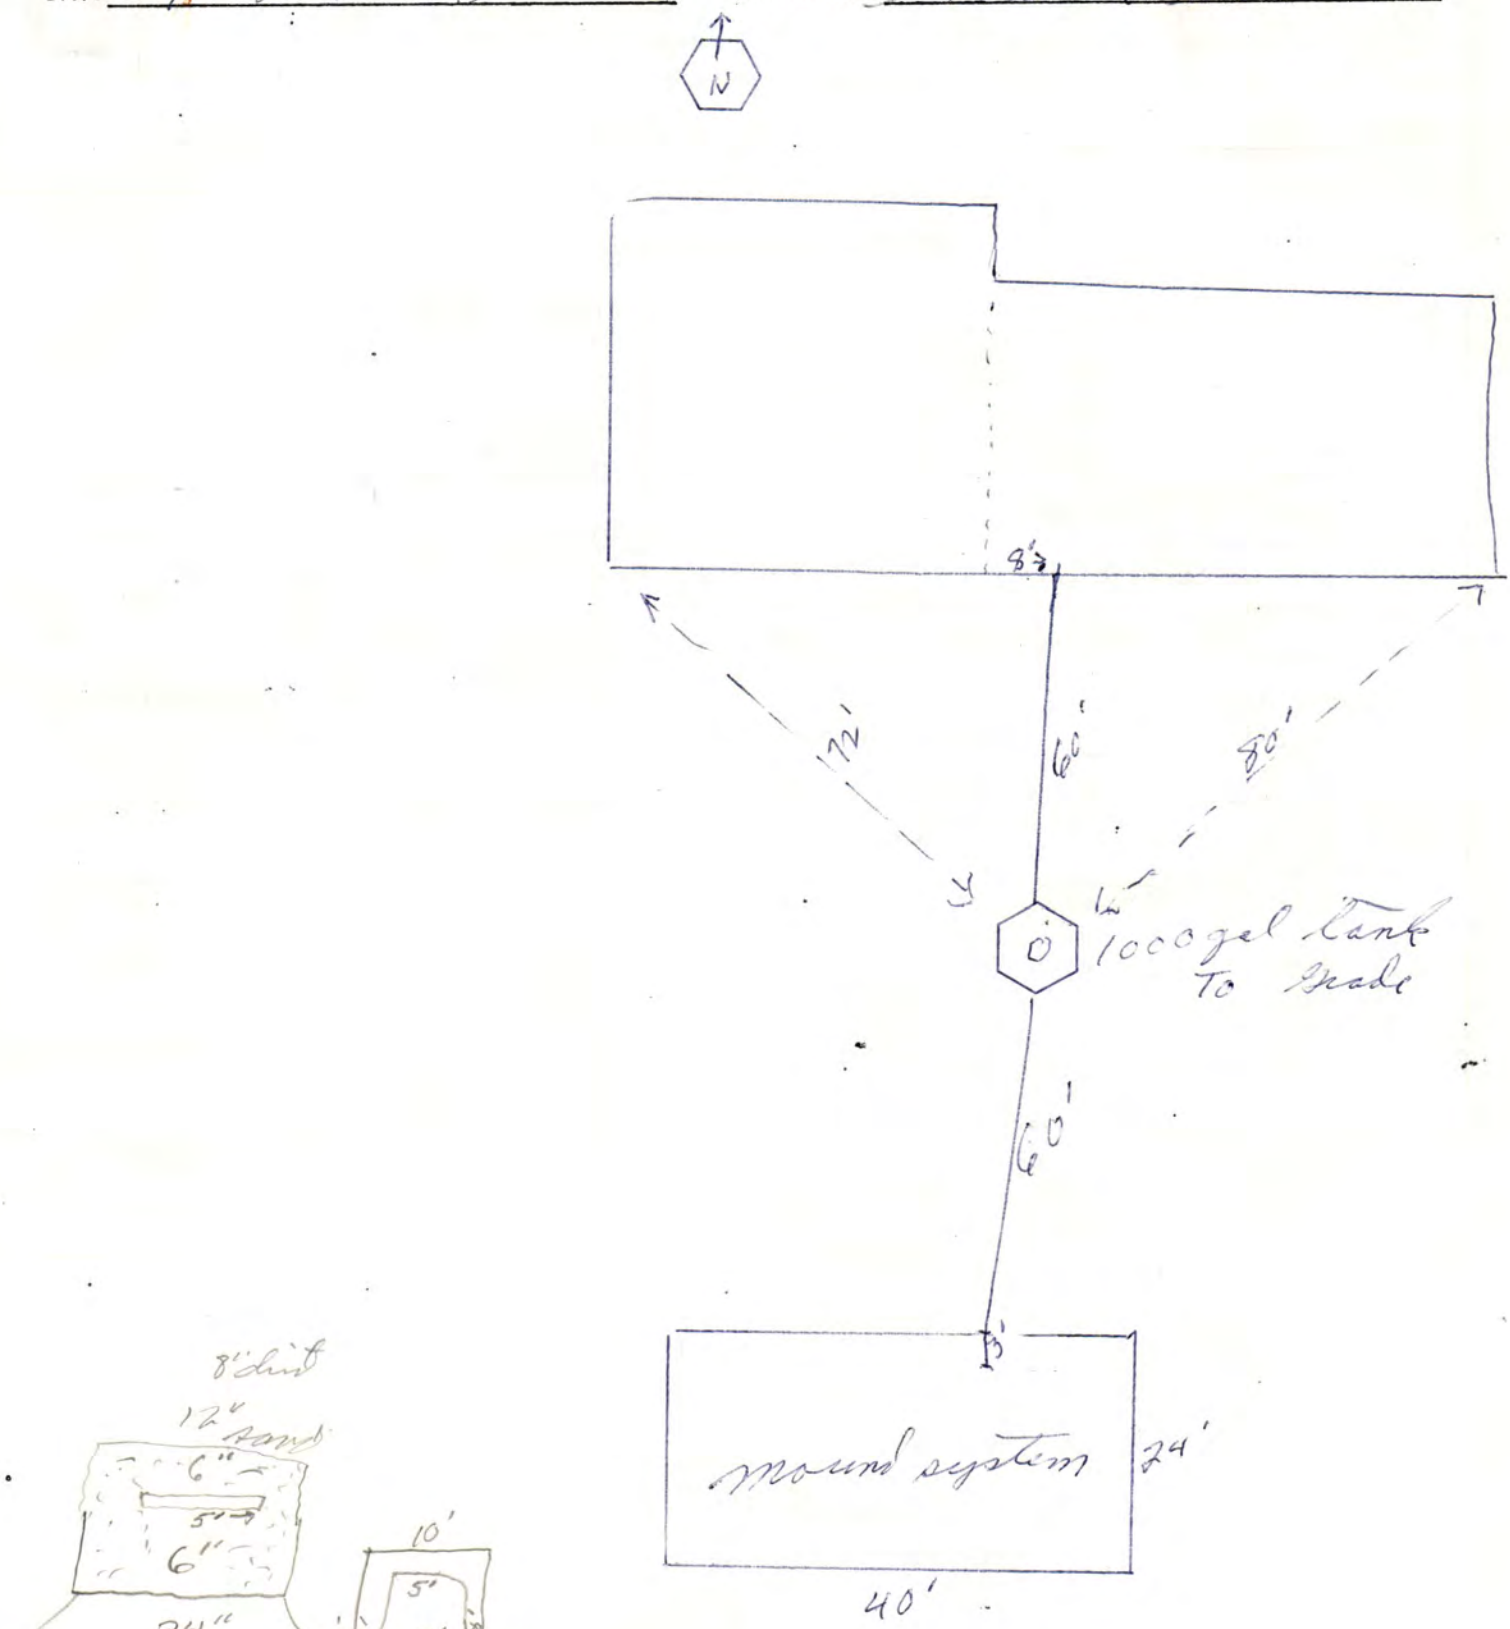

plans att-

006

Lincoln-Lancaster County Health Department

2200 St. Mary's Avenue, Lincoln, Nebraska 68502 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☑ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☑ Evaluation of the Individual Water System ☑ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address 7521 Boone Trail

Twp 9N Range 7E Section 22 1/4 ___ 1/4 ___ Block 4 Lot 2 Addition CLARENDON HILLS 1ST ADD

Directions to Property ½ mile south of Pine Lake Road & 75th Street

Location of Well NW corner of house Tap Location: Inside ☑ Outside ☑

Location of Sewage System back of house (south side) Year Installed 1978

	NAME	ADDRESS	PHONE
Present Owner:	Paul/Kathy VanDe Water	7521 Boone Trail Lincoln, NE 68516	423-3547
Tenant/Buyer:			474-6055
Return to:	SAME	SAME	SAME

Signature of Applicant Paul VanDe Water Address 7521 Boone Trail Lincoln, NE 68516 Date 11/15/93

474-6055

HEALTH DEPARTMENT USE ONLY

Date Received 11/16/93 Received $150.00 Check ☑ Cash ☐

PRELIMINARY STATUS--By PAUL DROTZMANN **DATE:** 11/16/93

WATER SYSTEM:	Approved	Disapproved
Construction	☐	☒
Bacteria	☒ 0 /ml	☐ ____ /ml
Nitrate	☒ <0.1 ppm	☐ ____ ppm

SEWAGE SYSTEM

Approved ☐

Provisional ☐

Disapproved ☒

Additional Site Visits

Date 12/1/94 by [redacted]

Date 6/28/94 by J.C.H.

Date ___/___/___ by ___

Comments: Sanitary seal is broken. Sewage running out onto ground surface 12-1-93 Repair made. Sample collected. 6/28/94 SEWAGE SYSTEM IS STILL CREATING NO PROBLEM. PROVISIONAL APPROVAL BECAUSE SEWAGE SYSTEM IS OF AN EXPERIMENTAL VARIETY. See Attached Letter ☐

FINAL STATUS


WATER SYSTEM: Approved: ☒ Jerold C. Hood R.E.H.S.

SEWAGE DISPOSAL SYSTEM Approved: ☐

Provisional Approval: ☒ J.C.H.

Approved by Paul Drotzmann Date 12/1/93

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

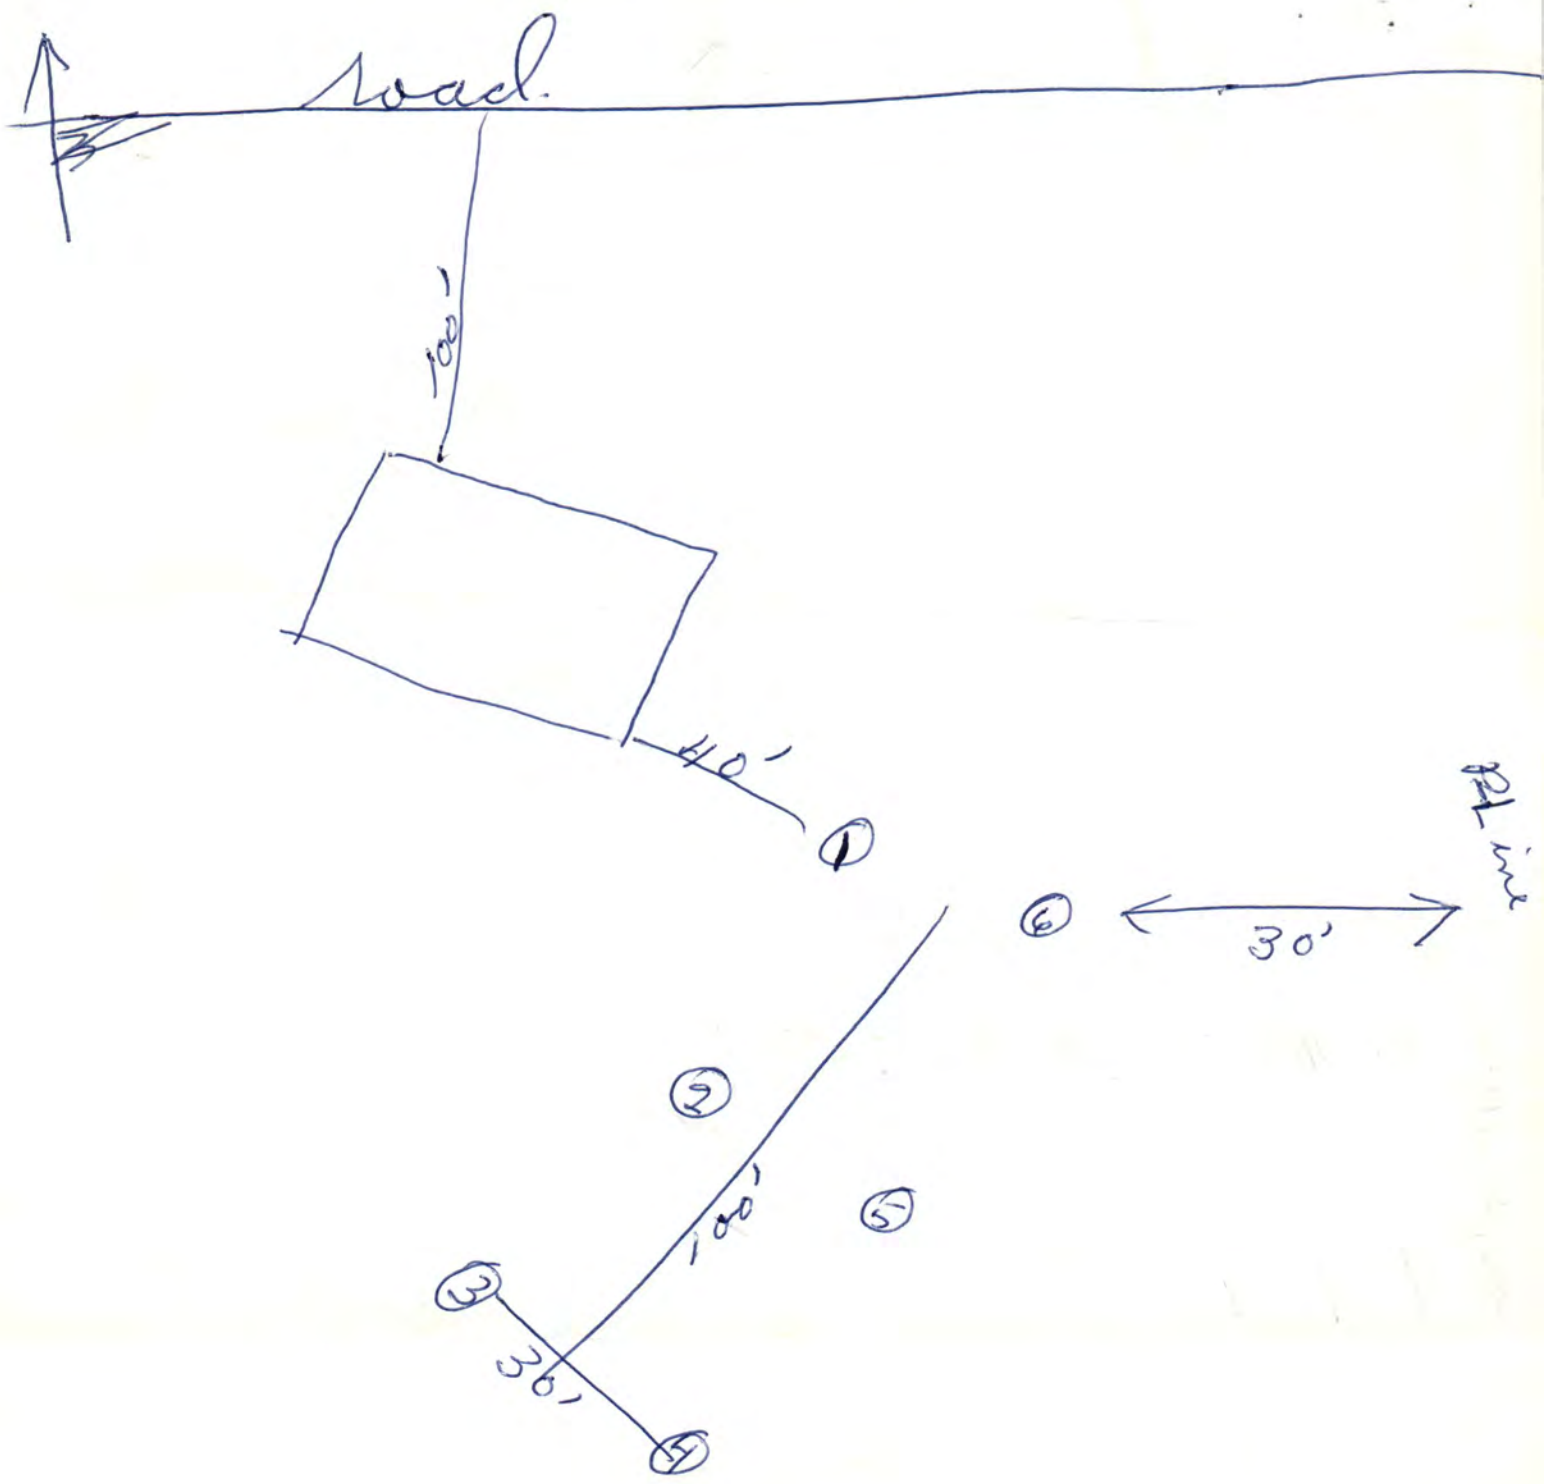
Road.
100'
40'
1
6
30'
R/W line
2
100'
5
3
30'
4
