Lincoln-Lancaster County Health Department

ENVIRONMENTAL PUBLIC HEALTH DIVISION

3140 N STREET · LINCOLN, NE 68510-1514

002749

(402) 441-8000

Permit: SEWAGE SYSTEM REPAIR
SEWAGE REPAIR

Permit # 03390075201

Issued 06/12/03
Expires 12/12/03
Revenue Code 3157

Establishment: MELVIN LINDNER
T11N R5E SEC 33
4IT LOT 57&4
7000 NW 112 ST

FEES: $100.00

TOTAL: $100.00

Permittee: MELVIN LINDNER
7000 NW 112 ST
LINCOLN NE 68524

Bruce D. Dart

Bruce D. Dart, Health Director

EPH COPY

LINCOLN LANCASTER COUNTY HEALTH DEPARTMENT

4033900752

Application to Alter, Extend or Repair an Individual Sewage Disposal System

☐ Municipal Code 24.38 ☒ County Resolution Number 2832

The undersigned hereby applies for a permit to: ☐ **ALTER** ☐ **EXTEND** ☒ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 11N Range 5E Section 33 1/4 Section ____
   Block ____ Lot 57 or 4 I.T. Addition ____
   Parcel ID 05 - 33 - 100 - 012 - 000 (i.e. 99-99-999-999-999)
   Street Address 7000 NW 112th St. Lincoln, NE 68524

2. **Property use:** ☑ residential ☐ commercial ☐ other use
   Number of bedrooms 3 Describe ____

3. **Type of Present Individual Disposal System** ☑ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** Add 100' of Lateral, New distribution box, Add risers on old tank

5. **Work to be done by:** ☐ owner ☒ contractor's name Raymond Contracting Inc. Lloyd Finkenbiner

6. **Estimated project:**
   a. Repair, replace or minor extension with a cost less than $400 (no fee required).
   (b.) Total cost is greater than $400 (Return fee with this application)
   c. A "construction permit" is required if the use, operation, location, or type of the system is being change.

Print Name Melvin Lindner Address 7000 NW 112th St. Phone 796-2135
Applicant Signature (owner or lessee) See Sewage Disposal Permit Application Lincoln, NE 68524

Please include the permit fee ($100) with this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 6/12/03 REVIEW: ☒ Approved ☐ Disapproved By: Jerrold C. Hood

Site visits
Date 11/18/03 By ____
Date ____/____/____ By ____
Date ____/____/____ By ____

Installation final written approval
Date NOV/24/03 By ____

Return application to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8022

Business Office Use Only
Received: Date: 06/12/03 Amount 100.00 Check No. 4943 & 4945 Initials ____

White - Division Copy Pink - Business Office Revised 9/00


Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

C

Permit Number: 03390075 2

Sewage Disposal System
Preliminary Plan Specifications

Draw a plot plan showing system location, lines, distribution box, tank and laterals, percolation test hole locations, well, residence, compass direction and property lines. Indicate on drawing if residence and well are existing or proposed.

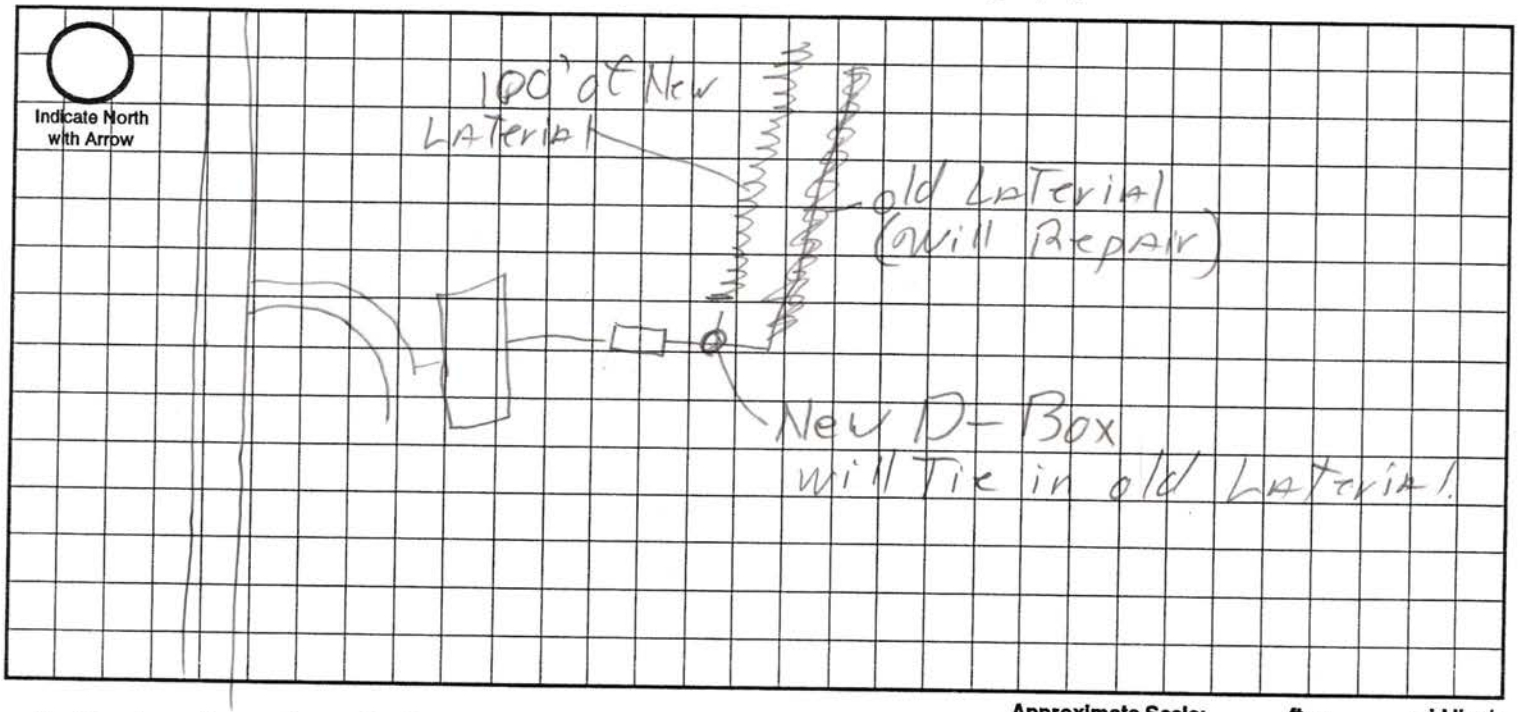

Approximate Scale: _____ ft. = _____ grid line/s

A. System Location (Indicate correct number and street)

Address (no rural route) 7000 NW 112. City Lincoln NE, Zip 68524

B. Proposed Septic Tank/s

Tank Material: ☒ Concrete ☐ Plastic ☐ Other _____

C. Proposed Absorption System (See Form B for Percolation Information)

Percolation Rate _____ (min. per inch) Soil Type: _____ Land Slope: _____ %

Type of Absorption System: ☒ Trench ☐ Bed ☐ Other _____

Total Square Feet of Field Required: 4' wide 100' Long sq. ft. 400'

Type of Lateral: ☐ Half-Moon ☐ Perforated Pipe ☐ Other Lateral Material: Gravel

Capacity of Septic Tank 1000 gals Number of Absorption Beds: 2 Number of Distribution Laterals per Bed _____

Total Length of Laterals 200' ft. Number of Trenches _____ Trench Width _____

D. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	25 ☒	20 ☒	15 ☒	25 ☒	☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	30 ☒	20 ☒	30 ☒	40 ☒	☒
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

E. Required Signatures

Home Building Contractor _____ Date _____

Installer Lloyd J. Jobst Date 06/12/03

FORM 23-102 10-96

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System

As Built Plans & Specifications

Date 11-19-03

System Location (Indicate correct number and street)

Address 7000 NW 112 (no rural route) City Lincoln NE, Zip 68524

A. Building Sewer

1. Material: _____
   Diameter: _____ in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: _____ ft.
4. Number of clean-outs: _____
5. Distances to: well or suction line _____ ft.
   stream _____ ft.
   pressure line _____ ft.
   property line _____ ft.

B. Septic Tank old

1. Material: concrete.
   Number of compartments: _____
2. Capacity: 1000 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter 12 in.
   Over outlet, diameter 24 in.
   Riser: ☐ above ☐ below grade _____ in.
5. Inlet: ☒ baffle ☐ tee
6. Outlet: ☒ baffle ☐ tee
7. Depth to top of tank, below unfinished grade: 14 in.
8. Distances to: Well or suction line 100+ ft.
   Stream 100+ ft.
   Pressure line 100+ ft.
   Property line 100+ ft.

C. Distribution Box New

1. Material: Plastic.
   Number available outlets: 10
2. Factory built: ☐ Yes ☒ No
3. Distance from septic tank: 4 ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round: 12" w/ thgrnvr
   or perforated pipe: _____
   Material: ☒ fiberglass ☐ plastic ☐ concrete
   ☐ other _____
2. Lateral lines: Number 2
   Length of each line: 100 old ft. 100 New ft.
   _____ ft. _____ ft., _____ ft.
3. Trench dimensions: Width 4' ft.
   Slope Flat in/100 ft.
   Average depth 24" in
4. Filter material: Gravel
   Depth of material 16" in.
5. Distances to: Well or suction line 100 ft.
   Stream 100' ft.
   Pressure line 100 ft.
   Property line 100 ft.

Indicate North with Arrow


Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

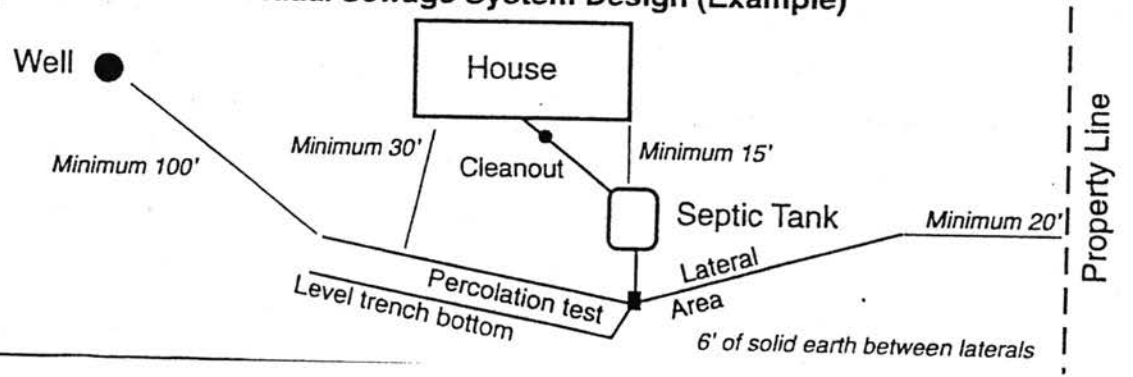

FORM 23-103 10-96

As Built Drawing

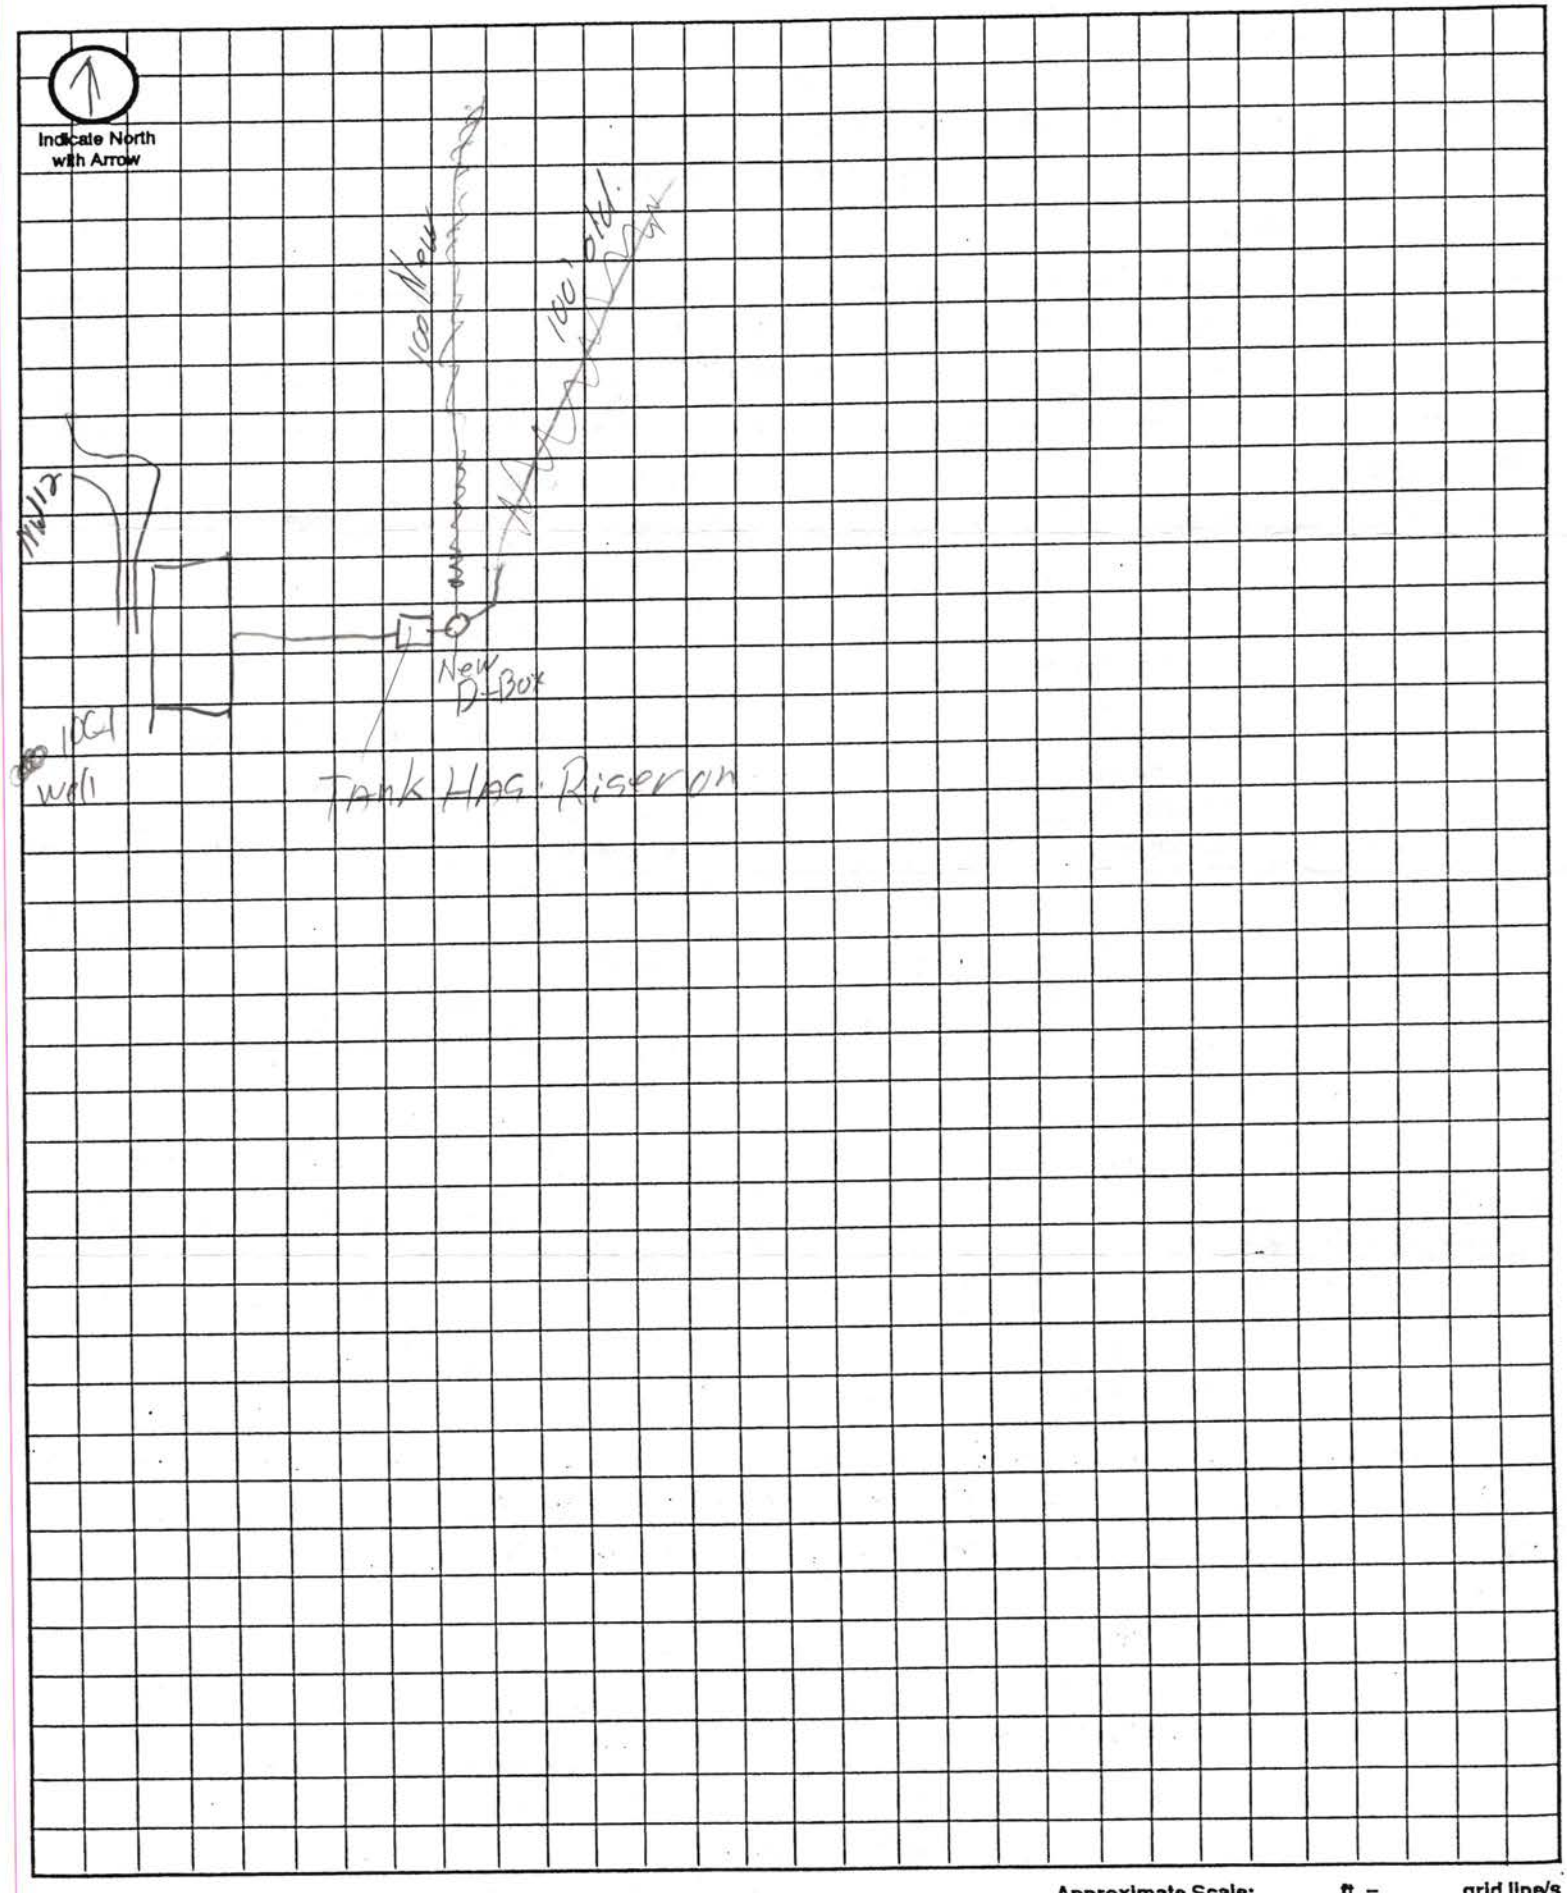

Approximate Scale: _____ ft. = _____ grid line/s

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1571-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

January 23, 1980 — THIS PERMIT EXPIRES

Melvin Lindner — ISSUED TO

Rural Route 1, Box 48, Malcolm, NE 68402 — ADDRESS

T11N, R5E, Section 33 — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 60.00

FILE NO. 1571-C

DATE: 7-25-79

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 11N ; Range 5E ; Section 33 ;
   Block _____ : Lot _____ : Addition SEE ATTACHED
   Street Address Route 4 Lincoln NE
2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe _____
3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐
4. Distance to public sewer: None ft.

Melvin Lindner
Signature of Applicant (Owner or Lessee)

Malcolm Ne. 68402
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/25/79. Date Frwd. 7/25/79. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hoot
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☐ Disapproved ☐ Signature: Wm. S. Reese
3. City or County Engineer: Date Rec'd. 7-25-79. Date Frwd. 7-25-79. ACTION: Approved ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 8/3/79 by: L.C.H.
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ By: Jerrold C. Hoot

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1571-C

PROPERTY WHERE SOIL TESTED:

Location: Township 11 ; Range 5 ; Section & ¼ Section NW¼ 33
Property Dimensions: 661.5 ft. x 395.28 ft. Area: 6.0 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: July 23 to July 24. Weather: Precip. .50 Temp. 80°.

OWNER:

Address:

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36	July 23	9.55	July 23	2.00	July 24	5.30	6	24 6.00	3¾	30	2¼	
2	36	July 23	9.57	July 23	2.02	July 24	5.32	6	24 6.02	3¾	30	2¼	
3	36	July 23	9.58	July 23	2.04	July 24	5.34	6	24 6.04	4	30	2	
4	36	July 23	10.01	July 23	2.06	July 24	5.36	6	24 6.06	3⅞	30	2⅛	
5	36	July 23	10.03	July 23	2.08	July 24	5.38	6	24 6.08	4	30	2	
6	36	July 23	10.05	July 23	2:10	July 24	5.40	6	24 6.10	4	30	2	

Melvin Lindner
Signature of Person Conducting Test

Address Malcolm Ne. 68402 Phone 796-2135

Sum of Percolation Rates:
Average of Rates:
Mean of Rates:

(Do not write below this line)

REVIEWING ACTION

Remarks:

Soil Type (SCS): Sharpsburg Silty Clay Loam

Date: July 25, 1979
Confirmed 12/3/79

Approved Percolation Rate (a)
A. 14 min./inch
B. min./inch
C. min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 1571-C

Indicate on sketch if residence and well are exisiting or proposed.

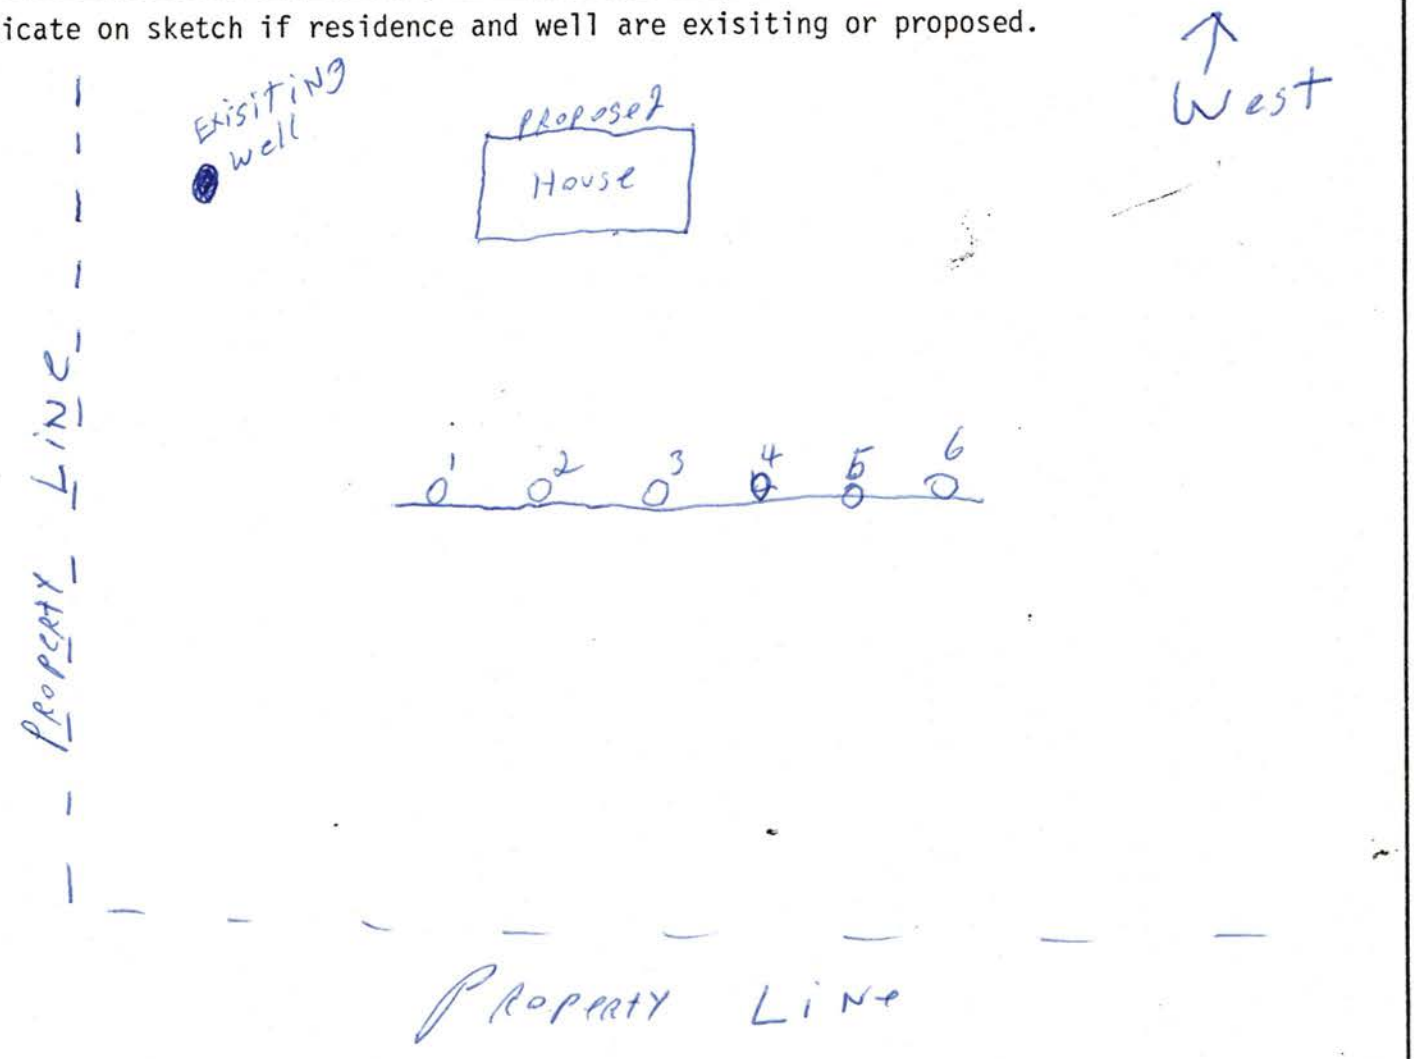

REVIEWING ACTION

Remarks: _____

Date: July 25, 1979

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed 371 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material P.V.C.; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 12 in.
3. Distance between dwelling and septic tank 60 ft.
4. Number of clean-outs ONE.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material CONCRETE; No. of compartments _____.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company PRE CAST)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX: N/A
1. Material ~~CONCRETE~~; Number - available outlets FIVE.
2. Factory Built: Yes ☒ No ☐
(Company PRE CAST)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 16" or
Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____.
2. Lateral Lines:
Number 1 ; Length of each line 100, _____, _____, _____, _____ ft.;
Total length of laterals 100 ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 4 ft.;
Slope _____ in/100 ft.; Average Depth 24 in.
4. Filter Material: GRAVEL
Depth of Material 18 in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

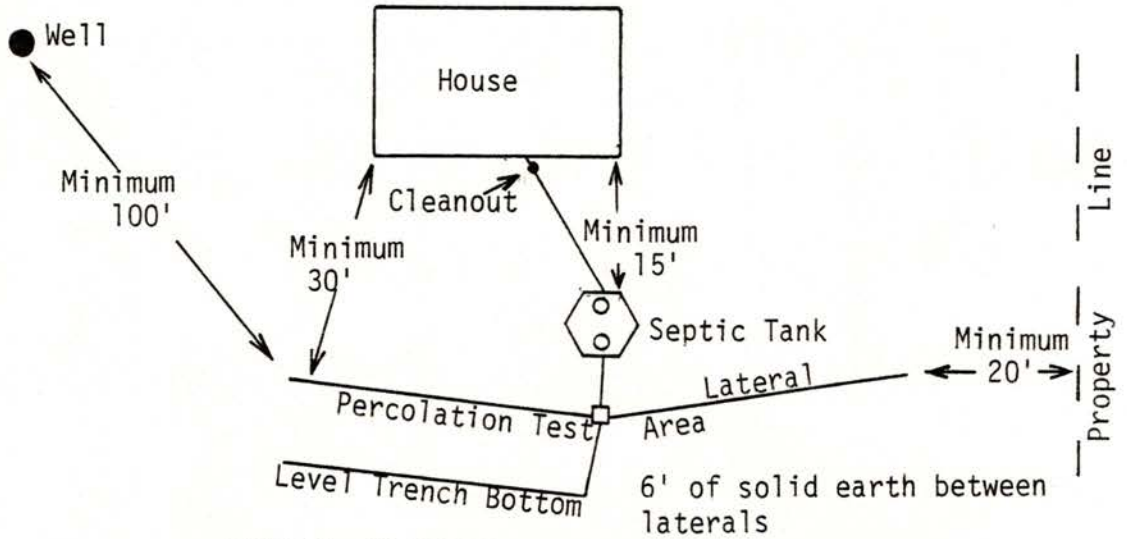


TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE _____ INSTALLER FRIESEN EXCAVATING

Drawing made late so installer forgot some features

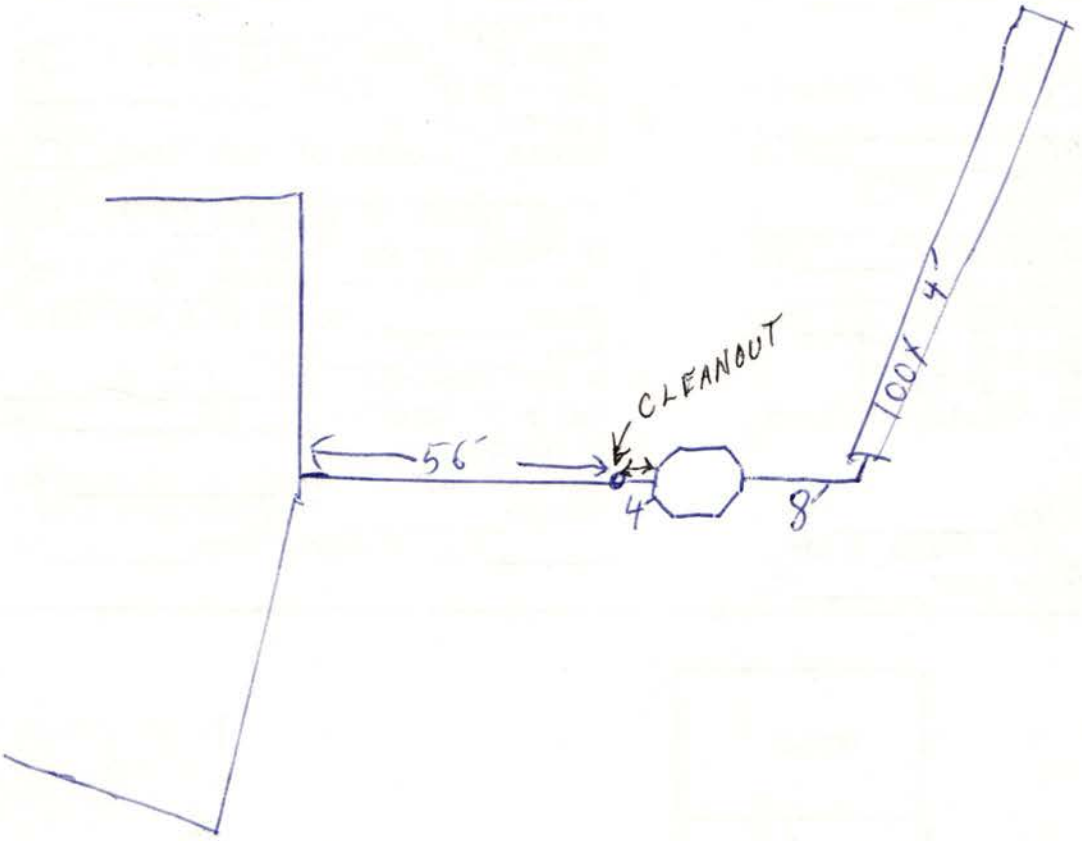

STATE OF NEBRASKA, County of

Filed for record on .... M.

and recorded in the Deed Record ...

..... Register of Deeds ..... of Deeds

LANCASTER COUNTY
REGISTER OF DEEDS
1978 NOV 16 PM 2:59
FILED FOR RECORD

$3.25

INDEXED
MICRO FILED
GENERAL
5½-351
IT

INST. NO. 78-30542

SURVIVORSHIP WARRANTY DEED

John W. Westerhoff, single, herein called the grantor whether one or more,

in consideration of ONE DOLLAR----------($1.00)------

received from grantees, does grant, bargain, sell convey and confirm unto

MELVIN E. LINDNER AND CHERYL M. LINDNER,
Husband and Wife,

as joint tenants with right of survivorship, and not as tenants in common, the following described real property in LANCASTER County, Nebraska:

NEBRASKA DOCUMENTARY STAMP TAX
NOV 16 1978
$ 3.85 BY KT

The North 661.5 feet of the West 395.28 feet of the South Half (S½) of the Northwest Quarter (NW¼) of Section Thirty-three (33), Township Eleven, North, Range Five (5), East of the 6th P.M., Lancaster County, Nebraska,

Rec. 3.85

Grantor states and warrants that Margaret Westerhoff, one of the grantees in the joint tenancy deed in Book 355 page 244 died May 18, 1957.
