LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 1796-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

DECEMBER 18, 1981 — THIS PERMIT EXPIRES

Roger Schmersal — ISSUED TO

Garland NE 68360 — ADDRESS

T11N, R5E, Section 6 — LEGAL DESCRIPTION

NONTRANSFERABLE

REMARKS:

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1796-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 6-17-81

The undersigned hereby applies for a permit to ALTER ☒, EXTEND ☐, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 11 N ; Range 5E ; Section ~~East~~ 6 NW¼;
Block _____; Lot _____; Addition _____
Street Address Rt 2 Garland

2. Property Use: Residential _____ ☒; Commercial _____ ☐
No. Bedrooms 2 Describe _____
Other Use ☐
Describe _____

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: attach septic tank to new house and extend two 100' laterals

5. Work to be done by: Owner ☒ ; or Contractor ☐ , _____
Contractor's Name

6. Estimated cost of project:
Warren Heidtbrink
Malcolm

a. Materials	$	472
b. Labor	$	273
c. Other	$	
TOTAL	$	745

Signature of Applicant (owner or lessee)

Rt. 2 Garland
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd: _____
Filing Fee: $ 30.00


2. Site Visits:
Date: 6/17/81 by: JMN
Date: 6-22-81 by: JMN
Date: 6-23-81 by: JMN

3. Date: Approved ☒; Disapproved ☐
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 6/23/81 by: JMN

N

4' wide
3'10" deep

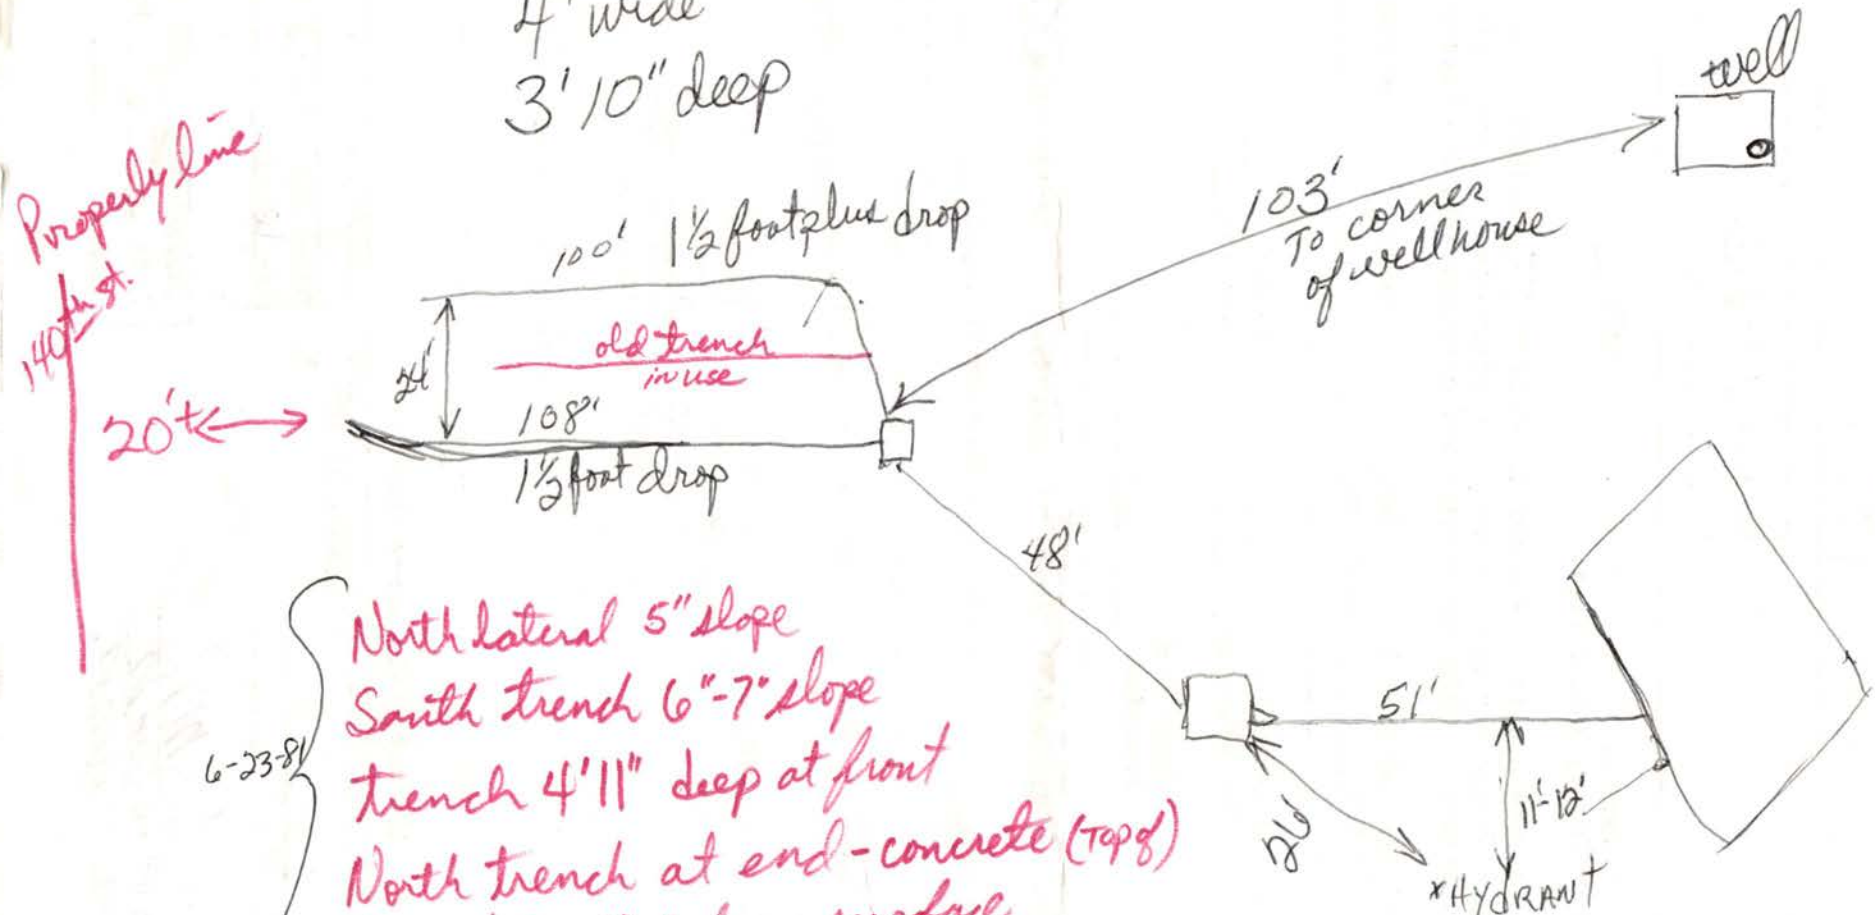

6-23-81

North lateral 5" slope
South trench 6"-7" slope
trench 4'11" deep at front
North trench at end - concrete (top of)
lateral is 4" below surface

redid 1½+ slope to less than 6"/100'
